



HANDLING & INSTALLATION MANUAL

DELTA PANELS™ WALLING SYSTEMS



CONTENTS

1	List of Drawings	3
2	Introduction	4
3	Delta Panel Profiles	5 - 6
4	Delta Facer Profiles	7
5	Safety	8
6	Tools & Equipment	9
7	Delivery Receivals & Storage	10 - 11
8	Handling of the Panels	12 - 14
9	Framing Alignment	14
10	Installation - Panel Preparation	15 - 19
11	Installation - Fasteners, Sealands & Extrusions	20 - 21
12	Installation Panel Cutting	22
13	Cleaning	23
14	Touch-up	23
15	Standard Installation & Connection Details	24 - 45
16	External Cladding - Horizontal Installation & Connection Details ...	46 - 53
17	External Cladding - Vertical Installation & Connection Details	54 - 62
18	Installation of Services & Accessories	63 - 66

1. LIST OF DRAWINGS

No.	Description	Page
10.1	Female Joint Sealant	15
10.2	Window & other Penetrations cut outs	16
10.3	Base Cut Back	17
10.4	45° Wall Mitre	18
10.5	Head Cut	19
15.1	Connection Overview	24
15.2	Wall to Ceiling Joint	25
15.3	Wall to Intermediate Girt Fixing	26
15.4	Wall to Girt , Clamp Plate Fixing	27
15.5	Wall to Insulated Floor	28
15.6	Wall to Floor Detail	29
15.7	Partition to Floor Detail	30
15.8	Alternative Wall to Floor Detail	31
15.9	Alternative Wall to Floor Detail	32
15.10	Alternative Wall to Floor Detail	33
15.11	Alternative Wall to Floor Detail	34
15.12	Alternative Wall to Floor Detail	35
15.13	Alternative Wall to Floor Detail	36
15.14	Typical External Corner	37
15.15	Typical External Corner with 45° Mitre	38
15.16	Wall to Low Ceiling	39
15.17	Wall to Low Ceiling	40
15.18	Typical External Corner, Clean Room	41
15.19	Main Ceiling Suspension	42
15.20	Partition to Ceiling Joint	43
15.21	Partition to Ceiling	44
15.22	Intermediate Ceiling Suspension	45
16.1	Typical Joints Fixing	46
16.2	Joints Base Details	47
16.3	Joints Base Details	48
16.4	Joints Base Details	49
16.5	Joints External Corner	50
16.6	Joints Integrated Window	51
16.7	Joints Recessed Window	52
16.8	Joints Personnel Door Detail	53
17.1	Joints Fixing	54
17.2	Joints Base Detail	55
17.3	Joints Base Detail	56
17.4	Joints Base Detail	57
17.5	Joints External Corner	58
17.6	Joints Internal Corner	59
17.7	Joints Integrated Window	60
17.8	Joints Recessed Window	61
17.9	Penetration Details	62

2 . INTRODUCTION

This manual should be used as a general guide only and is intended to be used in conjunction with the project's installation drawings. The installation drawings should identify the applicable site conditions, specify the components to be used and the required arrangements of the components. Specific building design and construction conditions may require variations from the information in this guide.

Delta Panels does not guarantee and is not liable for the quality of the installation. Delta Panels is not responsible for anything that may be attributable to improper installation, the negligence of other parties or from materials supplied by a third party.

'Owner' as used throughout this manual refers to the projects owner and/or his representatives, such as the project's architect, design engineer and general contractor.




These parties are responsible for determining the following.

- Selection of a competent Installer who is qualified and experienced in the proper installation of insulated building panels and their related flashing requirements.
- That the Installer has reviewed and understands the project's installation drawings and this guide prior to installation.
- The Panels and related components are installed in accordance with the project's installation drawings and the applicable sections of this guide.
- The Panels are suitable for the purposes intended.
- The Project's structural framing is properly designed and in satisfactory condition to accept the installation and design loads imposed by the panels.
- That the Panels and associated components are installed in compliance with the applicable building codes, engineering certifications, service conditions and good engineering and construction practices.


3. DELTA PANELS PROFILES

This Handling & Installation Guide covers the following Delta Panels™ Insulated Panel products.



DeltaCool™

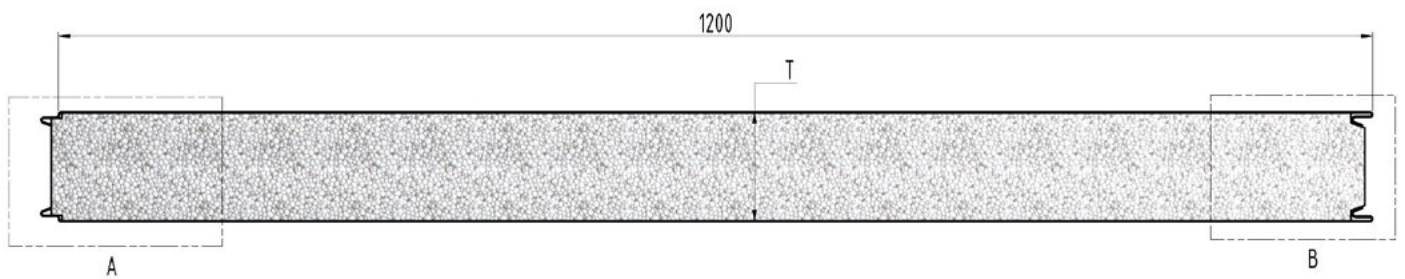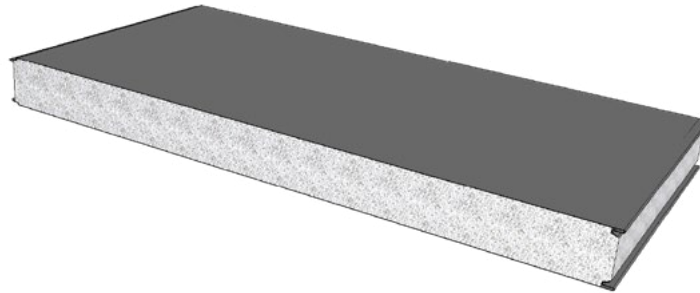

Detail A

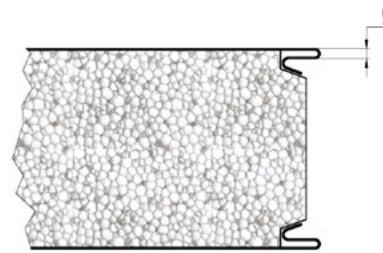







Detail B

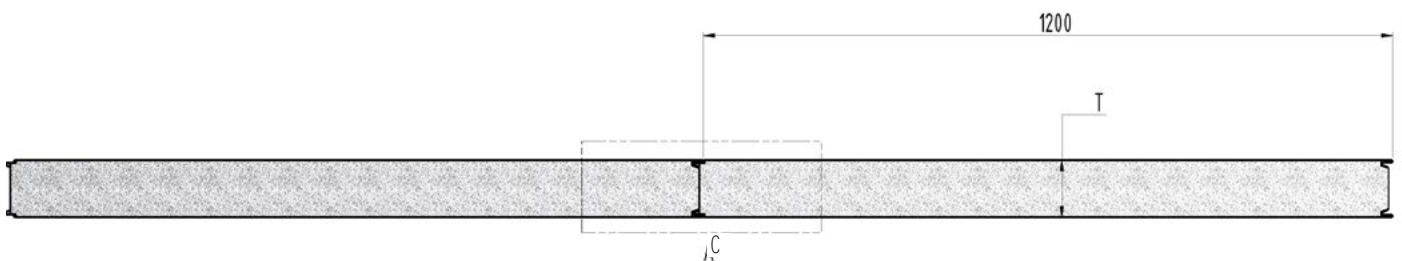

Detail C

3. DELTA PANELS PROFILES


DeltaSecretFix™

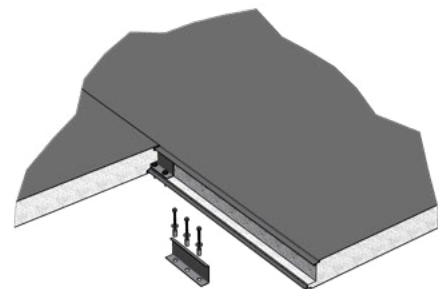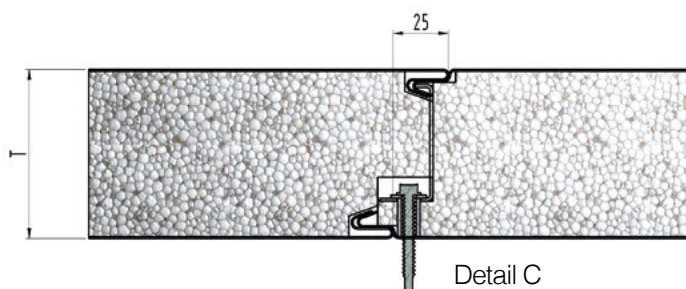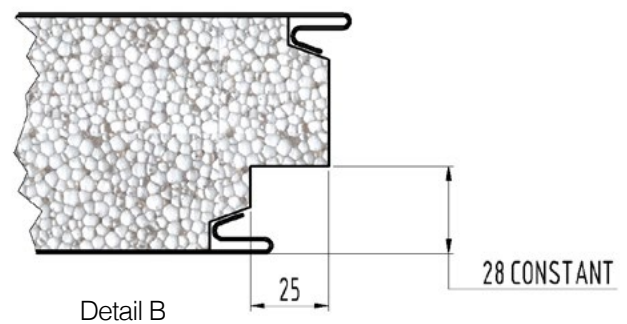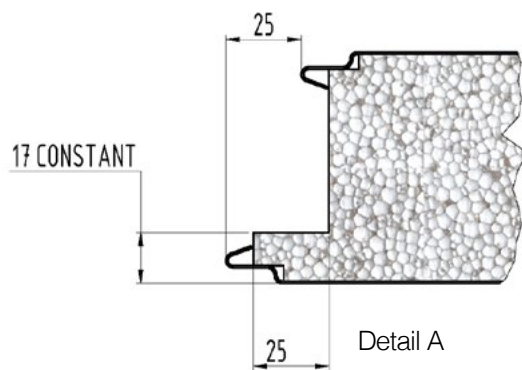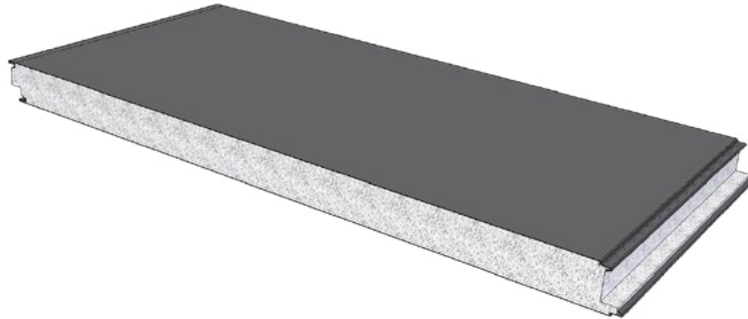


4. DELTA FACER PROFILES

All the Delta Panels™ Wall Panel range are available not only in an extensive range of contemporary colours but also with a variety of facer profiles. These facer profiles allow the panels to be utilised in a wide array of applications.


Smooth - Facer Profile

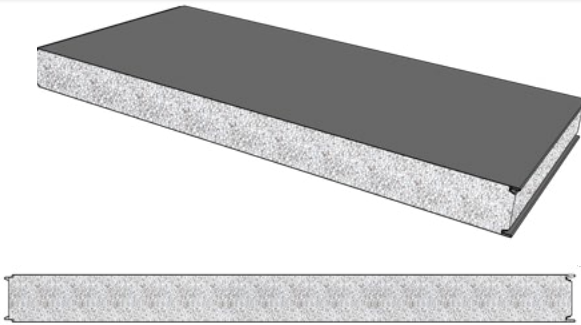


Mesa - Facer Profile

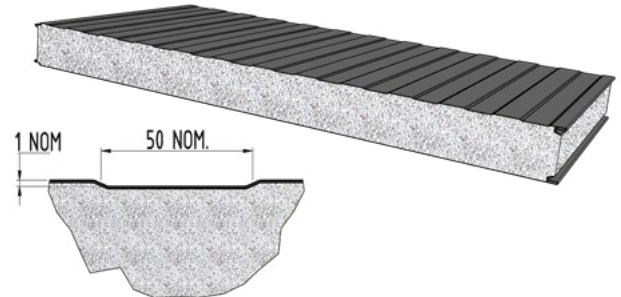


Ribbed - Facer Profile

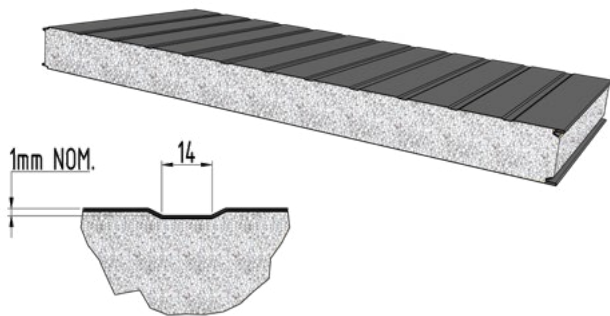


5V - Facer Profile

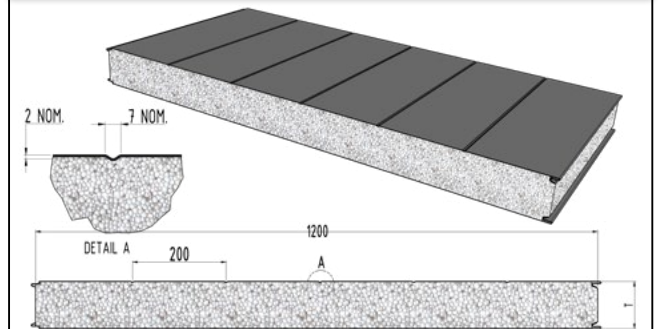


SatinLine - Facer Profile

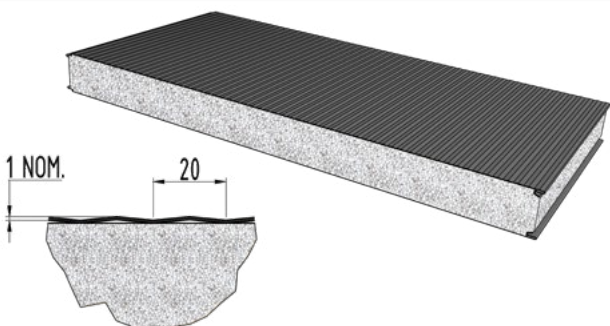


SingleV - Facer Profile

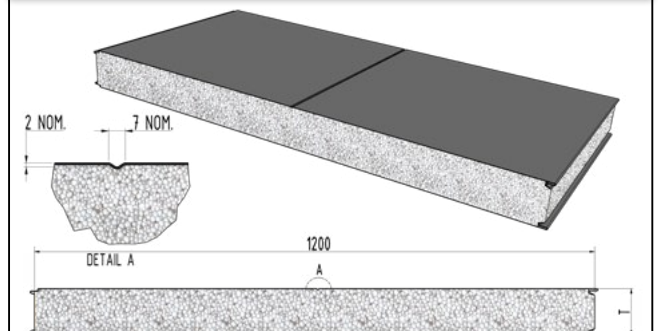

Elegance- Facer Profile

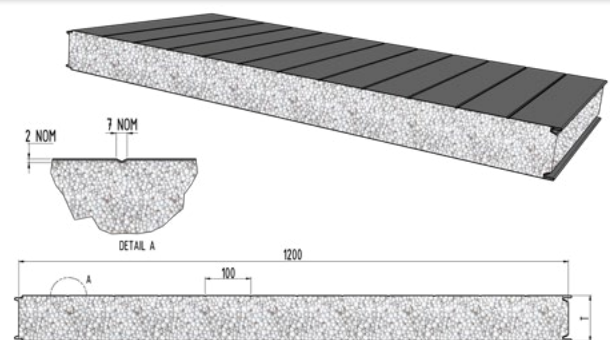

MicroRibbed - Facer Profile

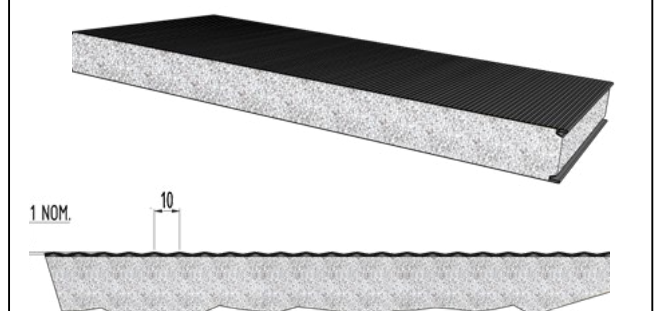

5. SAFETY

Safety

The installation of panels on any building structure requires careful planning to ensure all work can be carried out in a safe manner.

The establishment of a detailed Safe Work Method Statement (SWMS) as well as all onsite safety procedures are the responsibility of the panel installation contractor. The detailed Safe Work Method Statement (SWMS) must include the roles and responsibilities of all persons involved in the project. It must clearly outline what safety equipment is required, how it is to be utilized for each stage of the project and must comply with all aspects of the current Workplace Health and Safety Act. If the installer determines that they cannot install the panels in accordance with the installation drawings contained in this guide in conjunction with the Safe Work Method Statement (SWMS) requirements, it is their responsibility to determine appropriate alternative procedures.

Safety Data Sheets (MSDS)

Prior to the commencement of any installation, the panel installation contractor must read and familiarize themselves with the Safety Data Sheets (MSDS) applicable to the panel type being used. Current versions of Delta Panels' Data Safety Sheet EPS-FR Panels, Data Safety Sheet PIR Panels, Data Safety Sheet TPC Panels & Data Safety Sheet MW Panels are available upon request or online at www.deltapanel.com

General Safety Reminder.

- Hooks, wire cables and hardware used as tie-offs should be covered so that they do not scratch panel and trim surfaces.
- Use an approved and safe walking platform in high traffic areas to prevent damage to panels.
- Do not use panels as working platforms. Unsecured panels can slide or collapse under the weight of workers and equipment.
- Do not stand on the end of unsupported cantilevered panels, as this may result in panel collapse.
- Avoid point loads (concentrated loads in small areas). Heavy equipment, ladders, platform feet etc. may cause panel damage that could result in collapse.
- Do not install panels in high winds or other unsafe working conditions.
- Secure all loose panels with banding or tie-downs.
- Use clamps as necessary to hold panels in place until fastening is complete.
- Avoid panel and lifting equipment contact with electrical power lines, equipment and services.
- Verify that the building structure is complete and properly aligned, with all connections and bracing in place and secured.

6. TOOLS & EQUIPMENT

List of Equipment which may be required

- All suitable Personal Protective Equipment (PPE) , including suitable Protective Gloves, Footwear, Headwear and Eye Protection
- Installation of temporary Safety Mesh (if deemed necessary under the SWM)
- Fall Restraints as defined by AS/NZS 1891.4:3.1.4 (if deemed necessary under the SWM)
- Sufficient Sun Protection (Hat, Sunscreen)*
- Electric Leads with Earth Leakage Device.
- Turn-Up / Turn-Down Tool or Wide Mouth Vice-grip Pliers
- Drill or Screw Gun, Drill Bits, Hex Head Driver Bits
- Electric Saw with appropriate Cold Cutting Metal Blade or Nibblers
- Tin Snips
- Pop Rivet Tool
- Tape Measure
- Sharp Thin-bladed Knife or Box Cutter
- Adjustable Carpenter's Square
- String / Chalk Line
- Marking Pen
- Spirit Level
- Old Blankets or Equivalent
- Stable, fit-for-purpose Working Platform
- Plastic Paint Scraper
- Safety Harness
- Hard Hats
- Appropriate Footwear
- Scissor Lifts, Scaffold and/or Ladders

** sunscreen can cause paint deterioration if it comes into contact with the surface of the panel*

7. DELIVERY RECEIVALS & STORAGE

Receiving Panel Packs

- The panels are carefully packed to protect them during transport.
- They are a ready-to-install, finished product and special care should be taken when unloading and handling them to avoid permanent damage to the panels. Particularly the underside ceiling.
- Ensure that adequate lifting equipment (ie crane or forklift) is available prior to the delivery truck arriving
- Ensure that a suitable level location is available to store the off-loaded panels in.
- When unloading the truck, the packs of panels will have attached stickers indicating the correct lifting points.



- For packs of panels under 8 meters a forklift may be used.
- For longer packs a forklift with spreader lifting lugs is recommended.



7. DELIVERY RECEIVALS & STORAGE



- For longer packs the panel packs will need to be craned off the delivery vehicle
- If the panels exceed 8 meters a spreader bar is required to ensure that the slings do not cause any damage to the packs.
- The packs of panels should be stored correctly on the site in an area that will eliminate any chance of damage occurring to the packs
- The Delivery Docket will clearly state the quantity, description and type of panels delivered along with any associated components. It is the owners responsibility to cross check the delivery docket with the actual goods received at the time the goods are received.

Onsite Storage

- The panels should not be unpacked until it is time to install them, in the meantime they should be stored in an area away from traffic to eliminate the possibility of damage.
- Panels exposed to direct sunlight can result in Thermal Bowing which can prevent proper engagement during installation. Store the panels in a shaded area or leave the panels fully packaged until required for installation.
- All protective packaging when removed should be disposed of correctly
- Be aware that there is protective film on the steel surfaces of the panels if this film is left exposed to sunlight for a period of time it may become difficult to remove. It is advised to keep the original packaging shroud over the top of the panel packs to eliminate sun exposure
- Keep panels a safe distance from other on site trades that are welding, cutting or painting.


8. HANDLING OF THE PANELS

Insulated panels are used in a wide variety of different construction applications, varying from household patios enclosures, small & large industrial cold-rooms through to major industrial cladding projects. Depending upon the actual application and the working condition of the construction site, panels can be moved into their installation position by various means.

For larger commercial and industrial projects panel installation time is typically reduced when using lifting equipment. However the equipment must be designed to cater for the panel lengths, weights and profiles to be lifted. It is therefore important to verify the requirements of your specific project with the company supplying the lifting equipment.

Manual Lifting

- The use of safety gloves along with wrist protection is advisable when handling metal panels
- When lifting the panels off the pack always lift the panels vertically.
- Do not slide them across each other or twist sideways.
- Always lift from the underside, never lift using the top sheet.




- Care must be taken to avoid damage to the corners and overlaps.
- When relocating long panels always carry them on their edge, with one worker at either end, plus an additional worker at 3.5 metre intervals.
- When placing panels down, always place them down vertically & onto a non-abrasive, flat & stable support.
- **Never** drag panels, always lift and carry them to protect the panel surfaces from scratching.




8. HANDLING OF THE PANELS

Crane and Sling


- A crane can be used to lift panels into their final fixing position
- Care must be taken to correctly align the sling to the marked lifting points (as per attached tables)
- Set the packs onto the site in the proper orientation for the erection sequence
- A spreader bar must be used to ensure that the load is evenly disturbed
- Protective blocks are to be used under the slings to ensure that the steel skins are not deformed or crushed during the lifting process.



Packs over 1800 kgs and less than 10 meters may be lifted as shown in figure

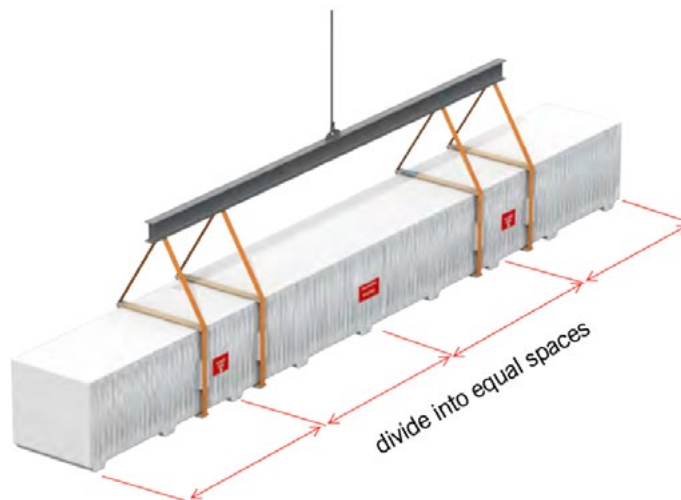

Packs over 1800 kgs and/or over 10 metres may be lifted as shown in figure

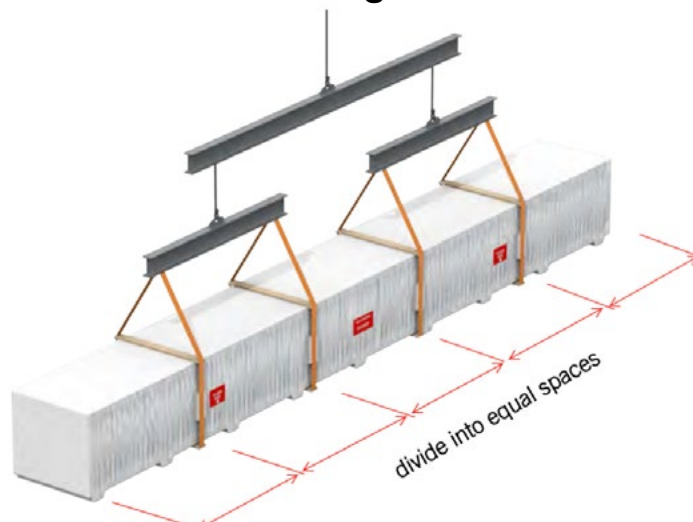

8. HANDLING OF THE PANELS

Vacuum Lifting

Individual panels can be lifted using a vacuum lifter (clad-boy) with outriggers. An alternative method is the use of slings.

The vacuum lifting equipment must be designed to cater for the panels lengths, weights and the profile of the top sheet.




9. FRAMING ALIGNMENT

It is important that any dimensional differences between the actual building framework and the drawings is resolved prior to the installation of the panels. Improper framing alignment can cause difficulty with panel engagement resulting in rippling or buckling of the panel faces.

- Framing alignment should be checked before panels are installed.
- Compare structural and panel installation drawings to ensure roof supports are in correct location.
- Carry out an on-site measurement of the support spacing and overall building dimensions.
- All supports not in alignment must be corrected by the responsible party before panel installation begins.

10. INSTALLATION - PANEL PREPARATION

10.1 FEMALE JOINT SEALANT

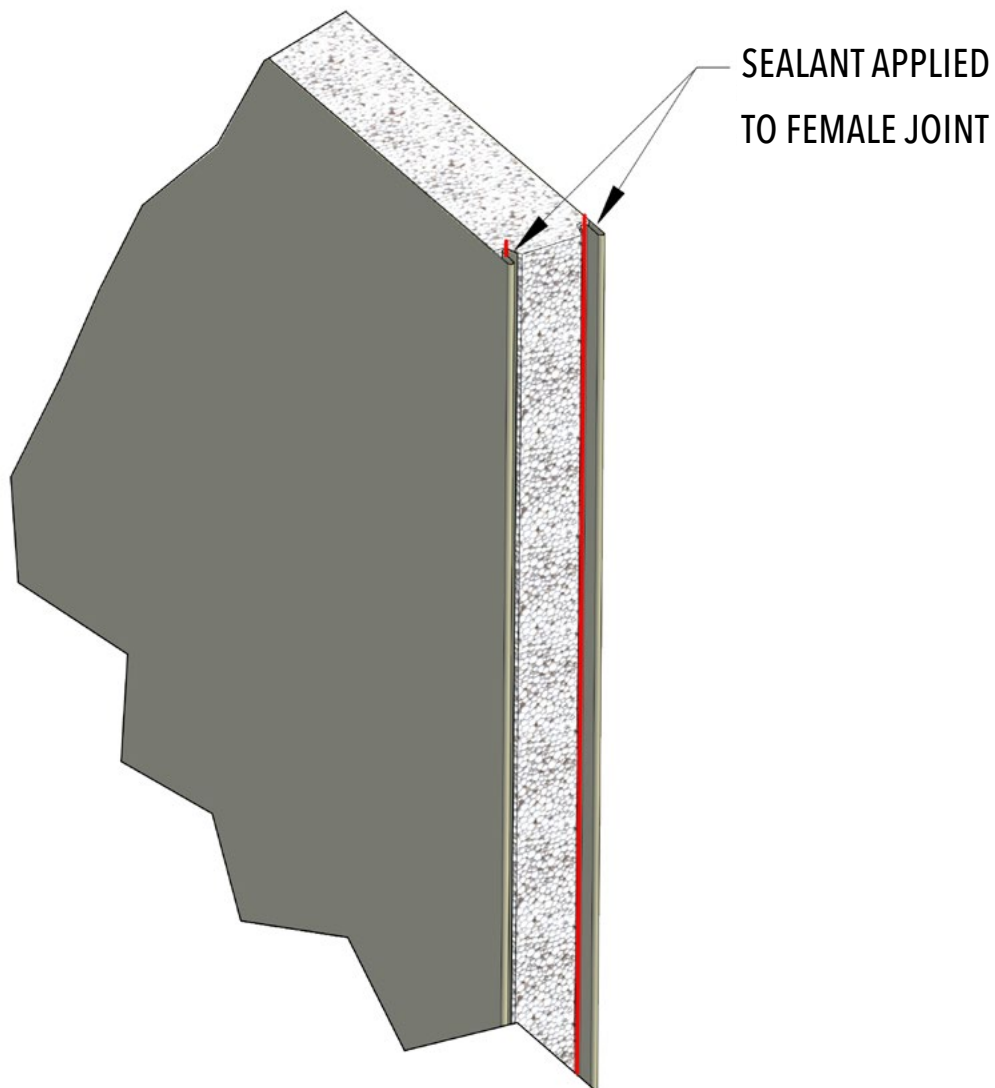

Description

FEMALE JOINT SEALANT

Filename & Path
Z:\Vau\1\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
17/12/2020


Designed by
DP

Drawing No.
DELTA PANEL CUT TYPES

Rev: A Sheet
1/5

10. INSTALLATION - PANEL PREPARATION

10.2 WINDOW & OTHER PENETRATIONS CUT OUTS

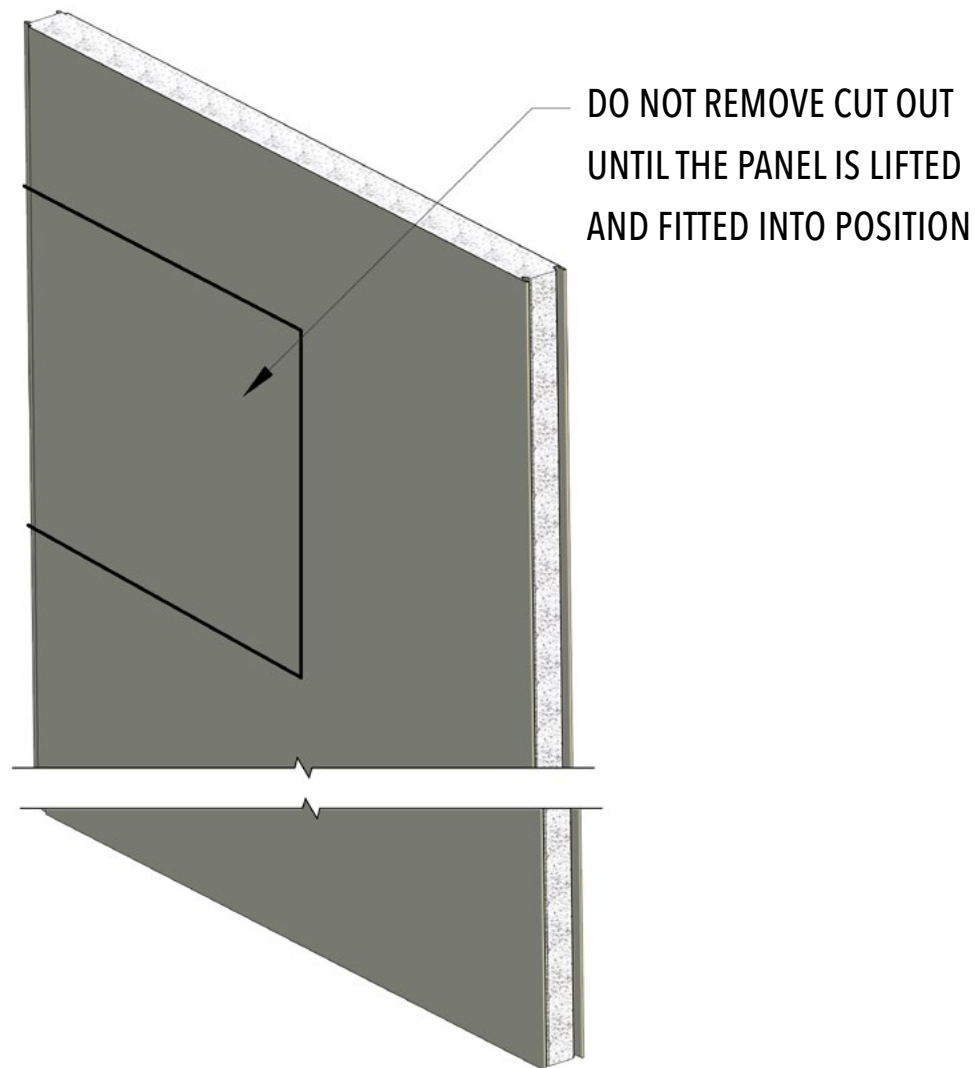

Description

WINDOW & OTHER PENETRATIONS CUT OUTS

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
17/12/2020


Designed by
DP

Drawing No.
DELTA PANEL CUT TYPES

Rev: A Sheet
2/5

10. INSTALLATION - PANEL PREPARATION

10.3 BASE CUT BACK

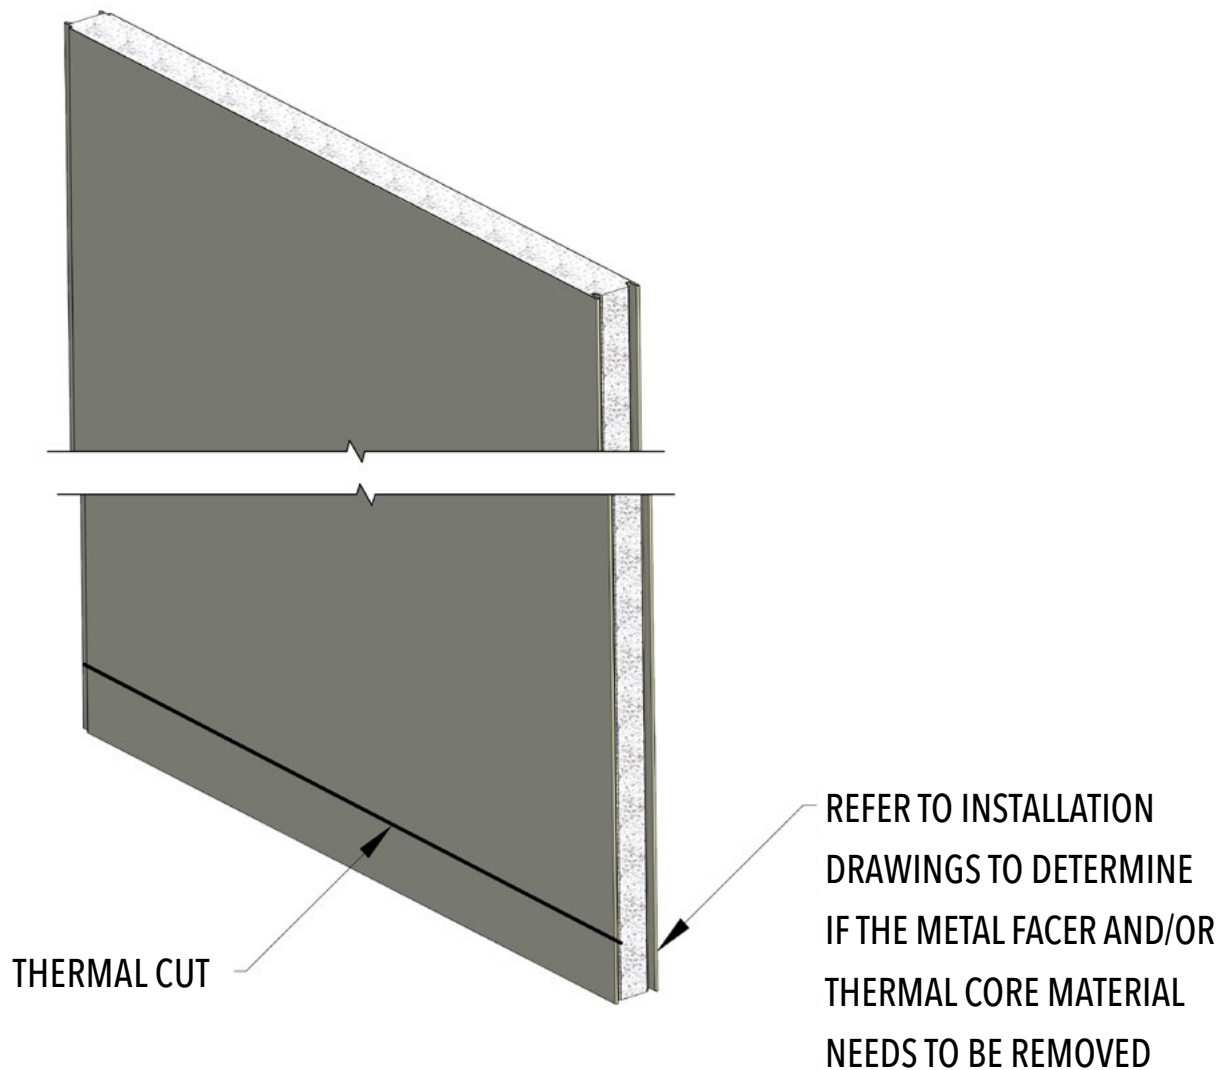

Description

BASE CUT BACK

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
17/12/2020


Designed by
DP

Drawing No.
DELTA PANEL CUT TYPES

Rev: A Sheet 3/5

10. INSTALLATION - PANEL PREPARATION

10.4 45° WALL MITRE

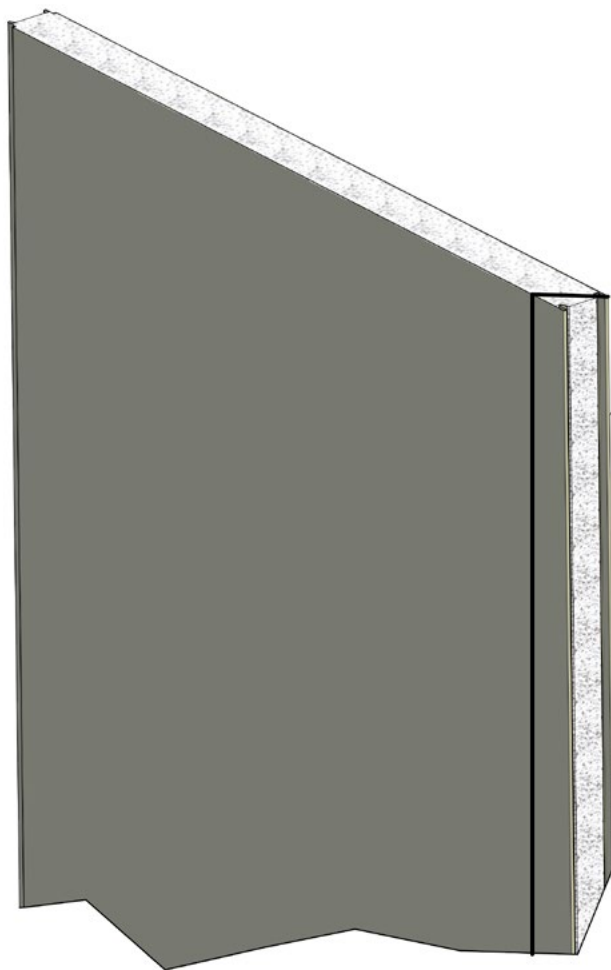

A 45° CUT OUT NEEDS TO BE REMOVED TO ENSURE THAT THERE IS NO THERMAL BRIDGING AT THE STRUCTURE'S CORNER JOINTS



Description

45° WALL MITRE

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
17/12/2020


Designed by
DP

Drawing No.
DELTA PANEL CUT TYPES

Rev: A Sheet 4/5

10. INSTALLATION - PANEL PREPARATION

10.5 HEAD CUT

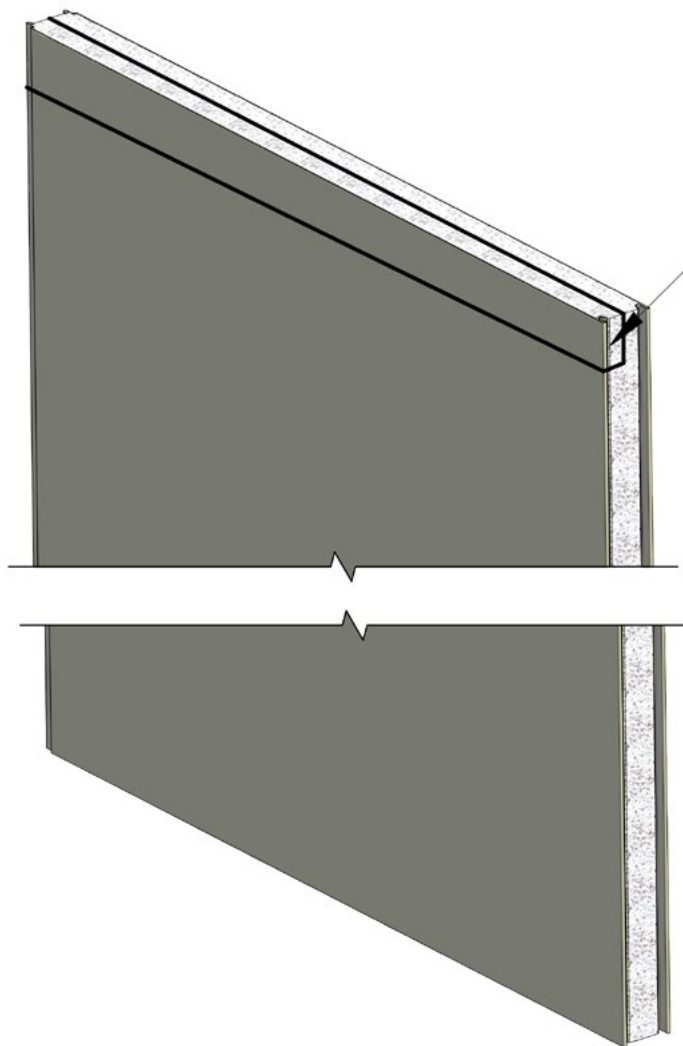

THE METAL FACER AND/OR SOME OF THE THERMAL CORE MATERIAL SHOULD BE REMOVED TO FORM A FULLY PREPARED ROOF-TO-WALL ASSEMBLY



Description

HEAD CUT

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
17/12/2020

Designed by
DP

Drawing No.
DELTA PANEL CUT TYPES

Rev: A Sheet 5/5

11. INSTALLATION - FASTENERS, SEALANTS & EXTRUSIONS

Fasteners

Rivets - 4mm Aluminum Rivets



Hammer Drive Anchor

- 0.6mm x 30mm



Screws

- Steel Screws

Metal Self Drilling Screw (SDS) - Fittings - Fixing
Fixing into Steel Beams up to 12.5mm




- Wood Screws

T17 - Fixing | Fixing into Timber Beams



NOTE: Not to be used in overhead installations

Mushroom Head Bolt

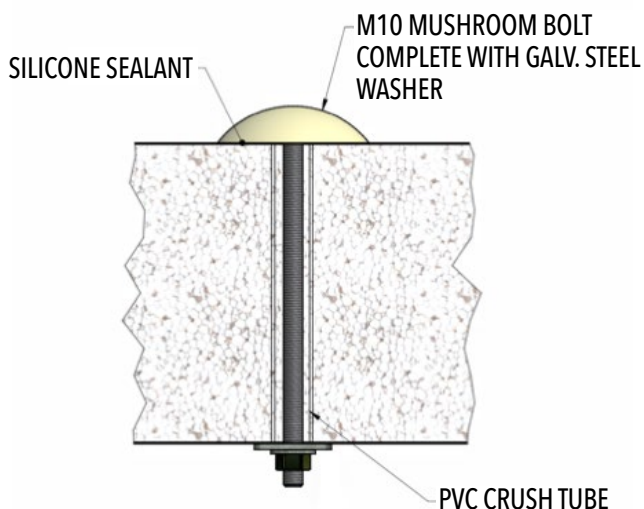

Sealants

Sealant should be of neutral cure and meet recommendations as outlined in BlueScope TB-9 Sealants for Exterior Finishes.

- Silicone Sealant

- Mastic Sealant

- Fire-Resistant Sealant



Extrusions

Aluminium or Pre-Painted Steel Angles

- 40/40 mm & 70/40mm



Aluminium or Pre-Painted Steel Channels

- 50mm -250mm



Coving

- Round coving



Coving

- Arrowhead coving



11. INSTALLATION - AS ISO 9705 - GROUP 1 INSTALLATION REQUIREMENTS

Fasteners

Rivets

- 4.8 x 12mm 304 grade stainless steel rivets



Steel Angles/Channels

1.2mm Pre-Painted Steel Angles

- 40/40 mm & 70/40mm



1.2mm Pre-Painted Steel Channels

- 50mm -250mm



To Comply with the AS ISO 9705 Group 1 Accreditation the following parameters must be followed

DeltaCool-EPS-FR™ Construction/Installation Parameters

- Insulating sandwich panel, nominal thickness 250mm or less
- Panel core of Class SL (to AS 1366.3) expanded EPS
- Clad both sides with "Colorbond" steel, thickness 0.4mm or greater
- Panel to panel junctions require steel angles fixed to the steel skins at not more than 300mm centre, with steel rivets. Ceiling panel to panels joins require steel (stitch) rivet connecting the metal skins at not more than 1200mm centres.

DeltaCool-TPC™ Construction/Installation Parameters

- The interlocking joints to be filled with a fire-resistant sealant secured with 4.8 x 12mm 304 grade stainless steel rivets at 1200mm centres.
- The internal mitred corners in the walls and the stepped wall to ceiling junctions to be filled with a fire-resistant sealant and covered with 40 x 40 x 1.2mm pre-painted steel angle secured with 4.8 x 12mm 304 grade stainless steel rivets at 200mm centres.
- Panel comprising 0.6mm steel skins with a 100mm thick Phenolic composite (TPC) core.

12. INSTALLATION - PANEL CUTTING

Equipment Recommendations

- Personnel cutting panels should always wear safety glasses, gloves and long sleeve shirts.
- Panel cutting should take place prior to installation when possible.
- Use care when using saws to avoid panel delamination; make sure the blade is sharp and let the saw cut at its own pace - **do not force**.
- Use the following cutting tools to avoid panel damage:
 - o Circular Saw with metal cutting blade or panel thumper blade
 - o Nibblers
 - o Panel saw



- The use of abrasive saws/grinder blades will damage the paint finish and metal facings
- For small penetrations, cut each panel face with a portable router, then cut the foam with a serrated knife. Metal flashings may be cut with power snips, nibblers or hand snips.



Cutting Recommendations

- Place the panel on padded sawhorses.
- Clean any surface grime and debris off panel face to be cut with clean rag.
- Mark cut line with chalk or washable felt tip marker.
- Masking tape may be applied on both sides of cut line to minimise panel scratching.
- Recheck measurements and cut with appropriate tool.
- Remove burrs at cut edges with deburring tool.



13. INSTALLATION - CLEANING

- Metal shavings from cutting and drilling should be removed as panels are erected using a soft bristle brush or clean cotton rag.
- For general cleaning, use a low pressure power wash with plain water. If necessary, use carwash soap or a 5% solution of mild laundry detergent. Use a clean cotton rag, sponge or soft bristle brush as required. Rinse thoroughly.
- Sealants, grease, tar and wax can be removed from panels and trim by using WD-40. Apply to a clean cotton rag, and avoid smearing over a large area. Then follow up with general cleaning instructions as above.
- For rust stains, remove the source (typically metal filings), then clean the affected area using one of the following methods: soap and water, or citrus oil based cleaning fluids.
- Concrete/mortar splatter must be washed off immediately with a high pressure wash and mild detergent.
- Do not use solvents, wire brushes, steel wool, or any other abrasive method to clean the painted surface of panels.

14. TOUCH UP


- Touch-up paint is for minor scratches only.
- Colour coded touch-up pens can also be used for small scratches.



- Test all touch up colours on an offcut piece of panel to ensure that the paint colour is a correct match prior to applying to the finished roof section
- Clean affected area with a clean cloth, and apply touch-up in the scratch using a fine artist brush.
- Allow 30-45 minutes for tack free and 24 hours for complete drying.

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.1 CONNECTION OVERVIEW

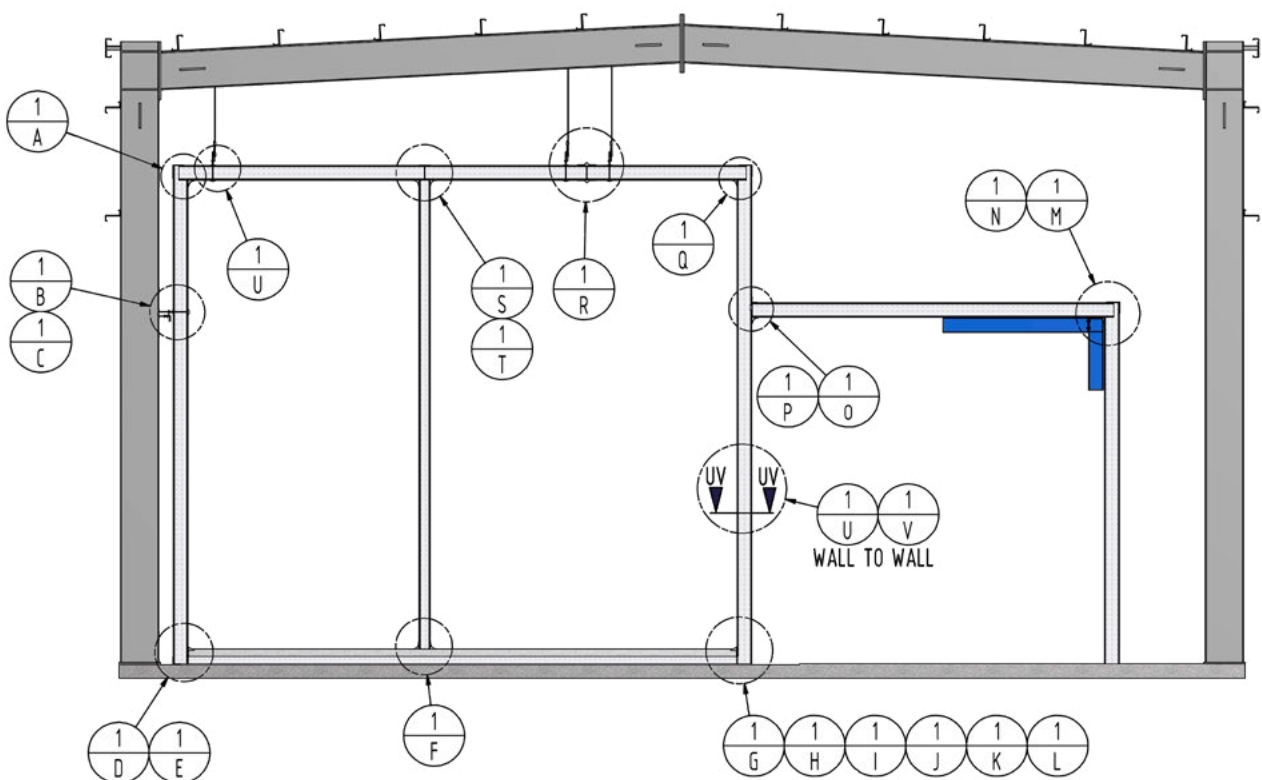

Description

CONNECTION OVERVIEW

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020

Designed by
MDI


Drawing No.
COLD STORE OVERVIEW

Rev:
A

Sheet
1/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.2 WALL TO CEILING JOINT

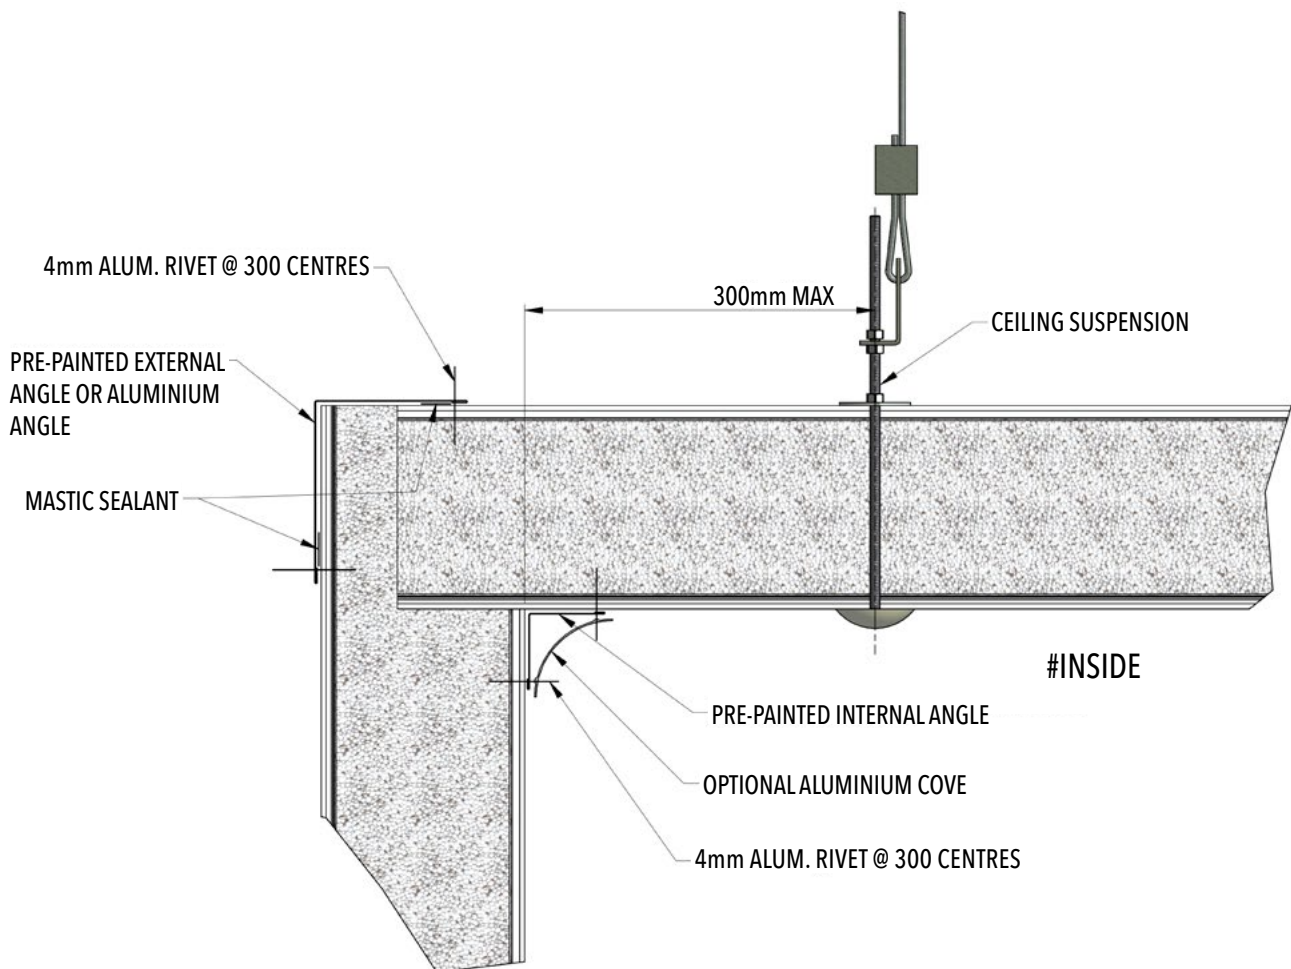

Description

WALL TO CEILING JOINT

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1A

Rev: A Sheet 2/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.3 WALL TO INTERMEDIATE GIRT FIXING

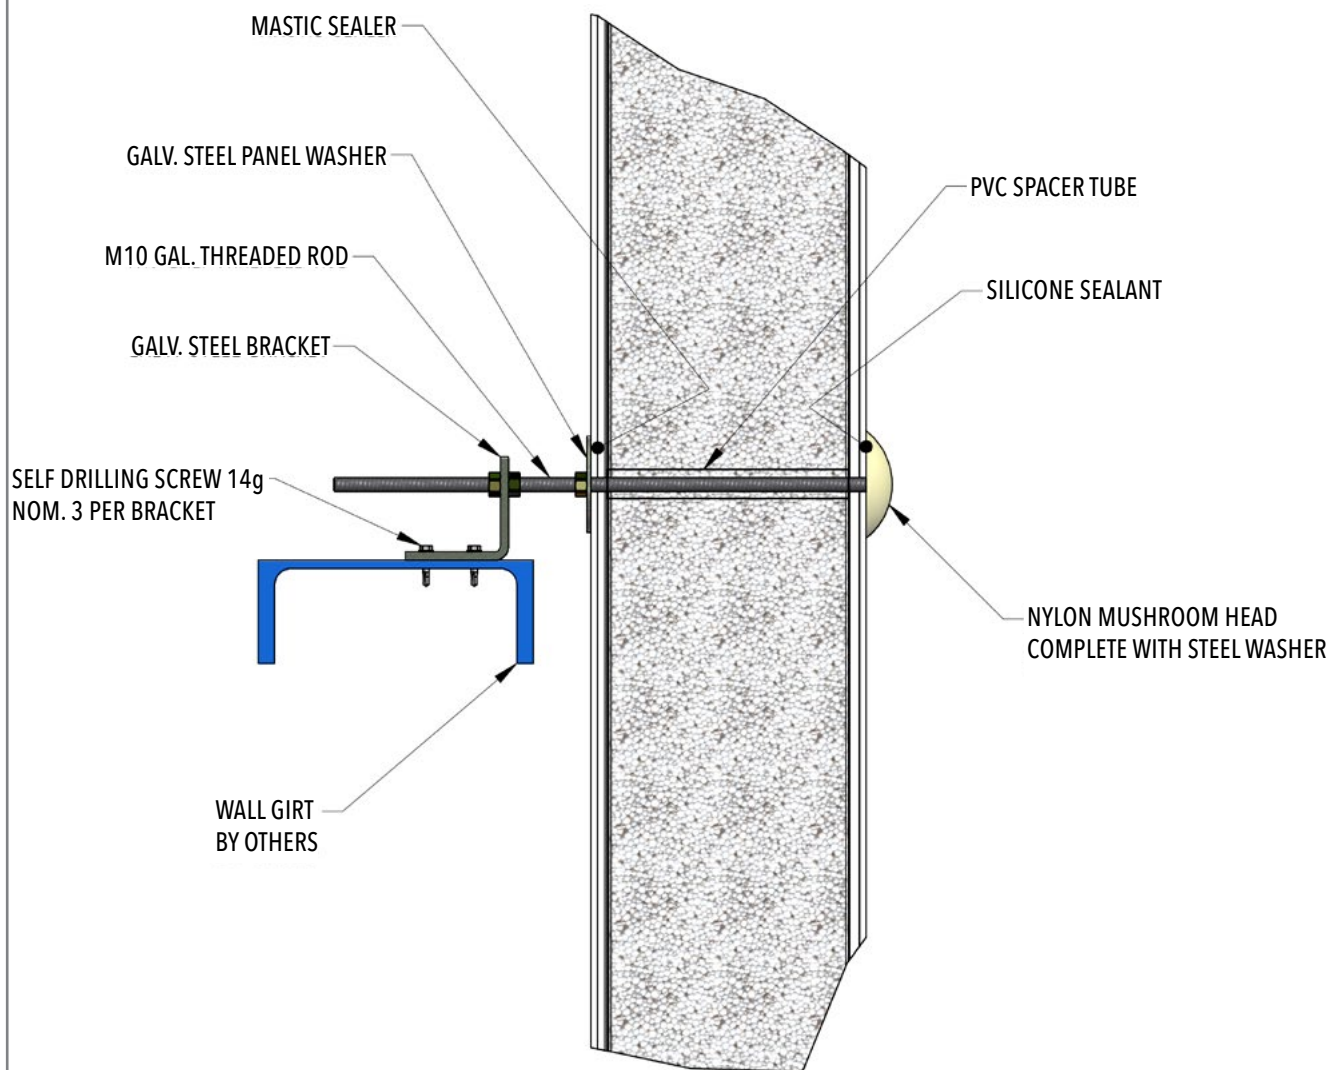

Description

WALL TO INTERMEDIATE GIRT FIXING

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1B

Rev: A Sheet
3/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.4 WALL TO GIRT, CLAMP PLATE FIXING

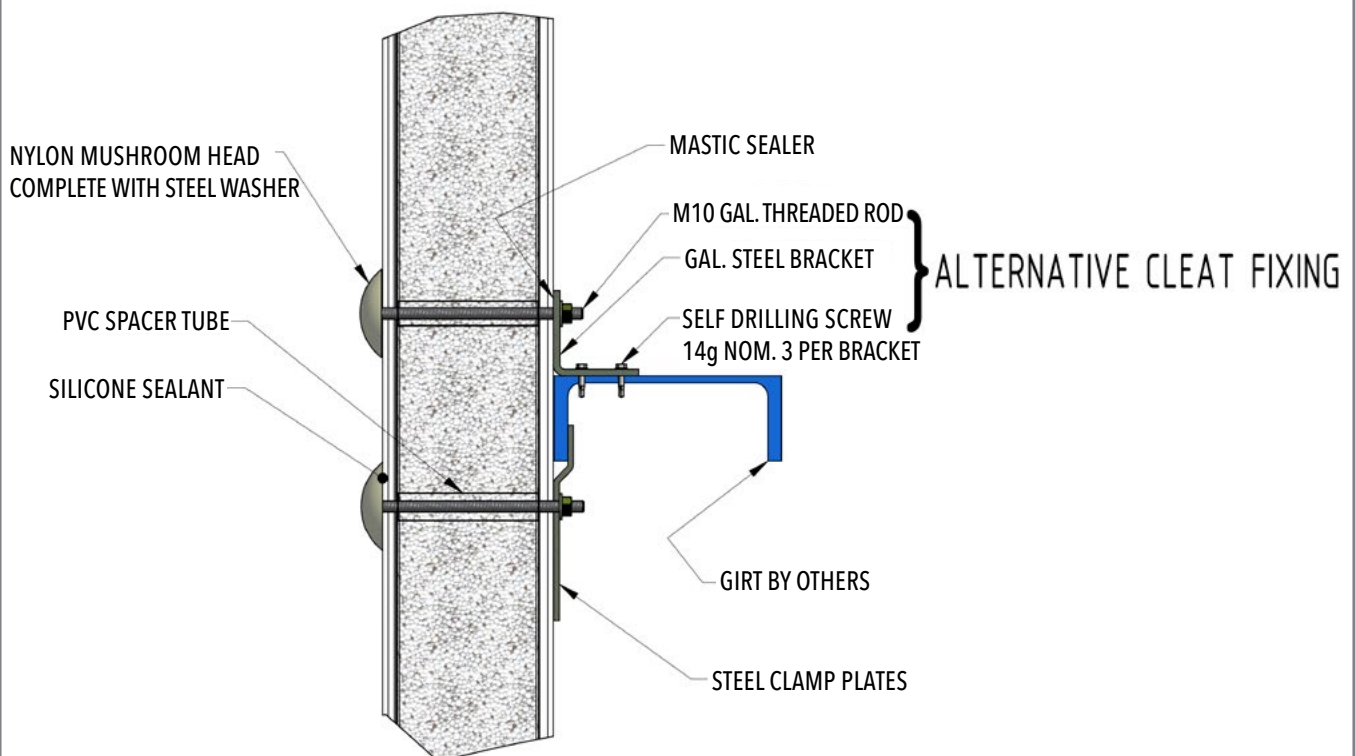

Description

WALL TO GIRT, CLAMP PLATE FIXING

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1C

Rev: A Sheet
4/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.5 WALL TO INSULATED FLOOR

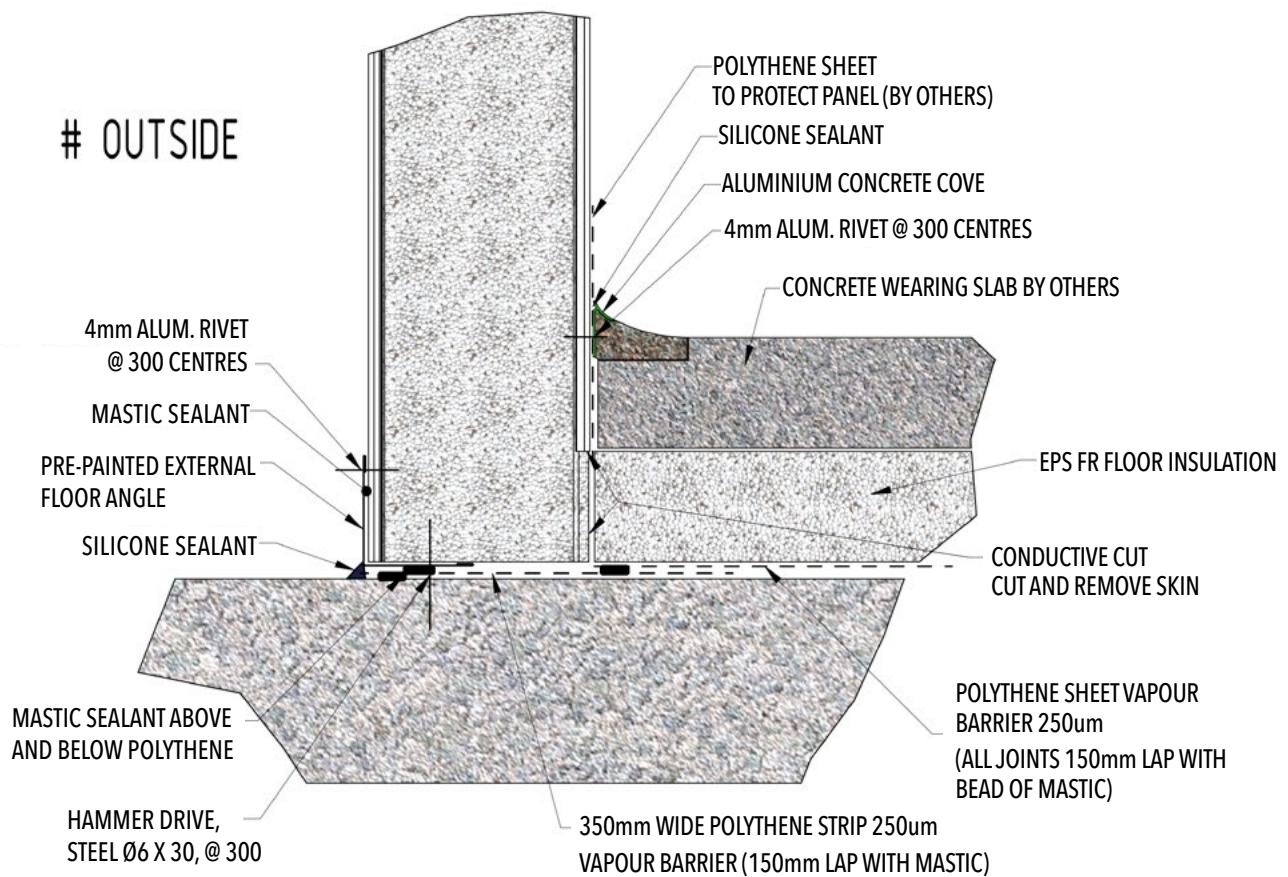

Description

WALL TO INSULATED FLOOR

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1D

Rev: A Sheet 5/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.6 WALL TO FLOOR DETAIL

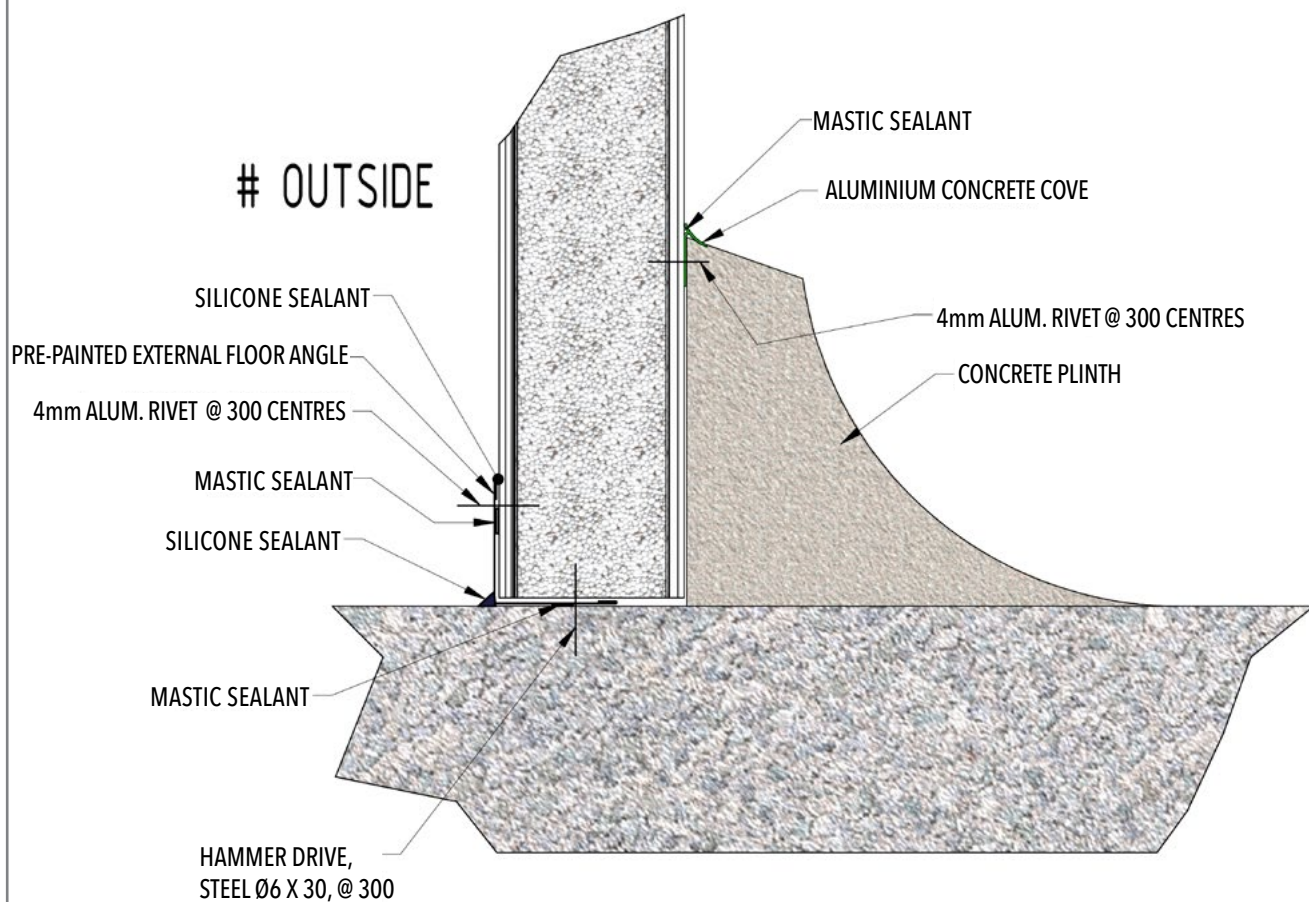

Description

WALL TO FLOOR DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1E

Rev: A Sheet 6/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.7 PARTITION TO FLOOR DETAIL

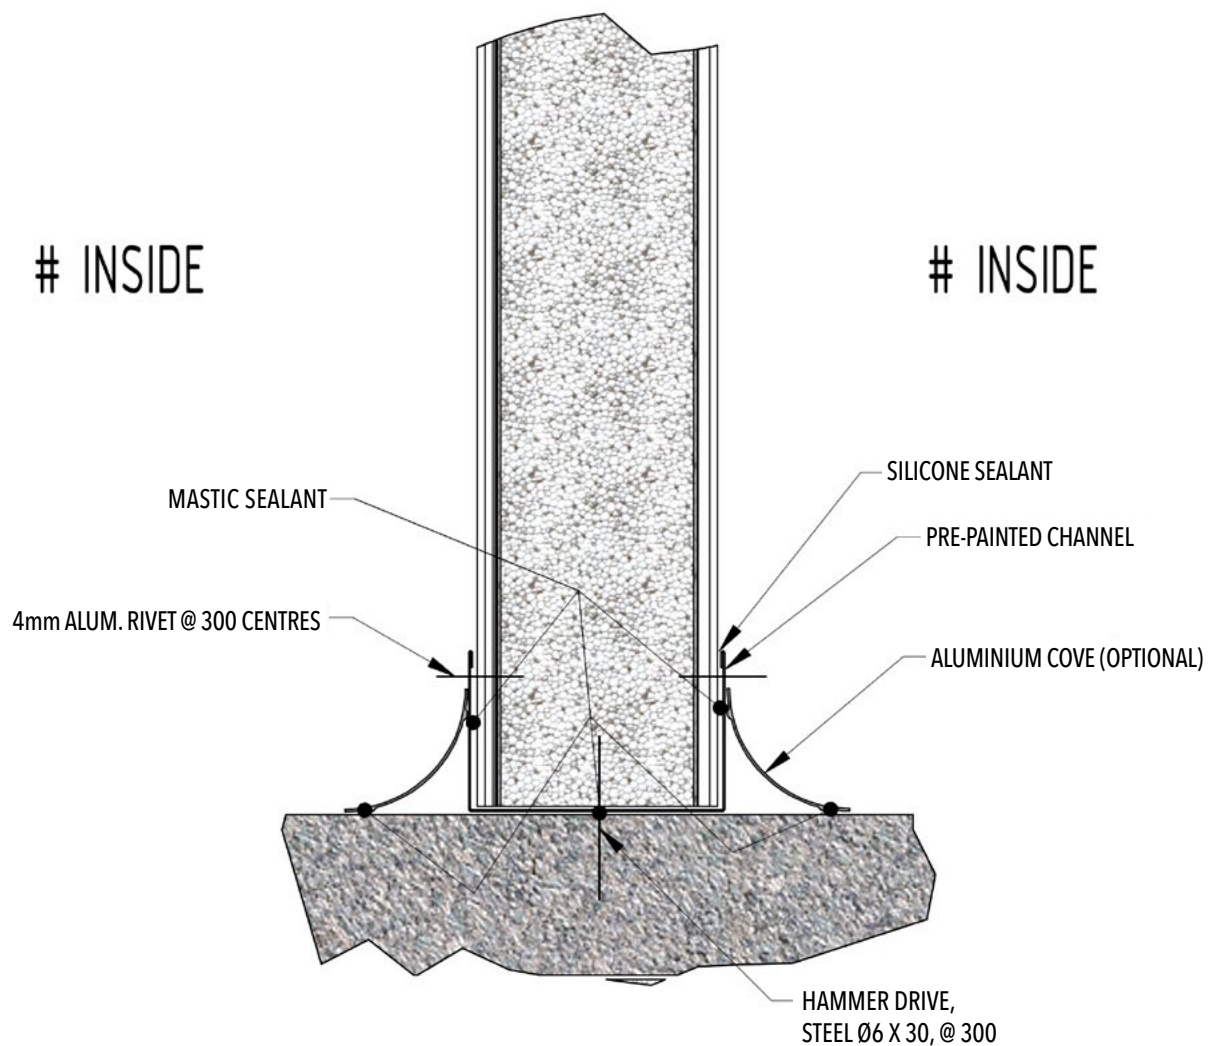

Description

PARTITION TO FLOOR DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1F

Rev: A Sheet 7/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.8 ALTERNATE WALL TO FLOOR DETAIL

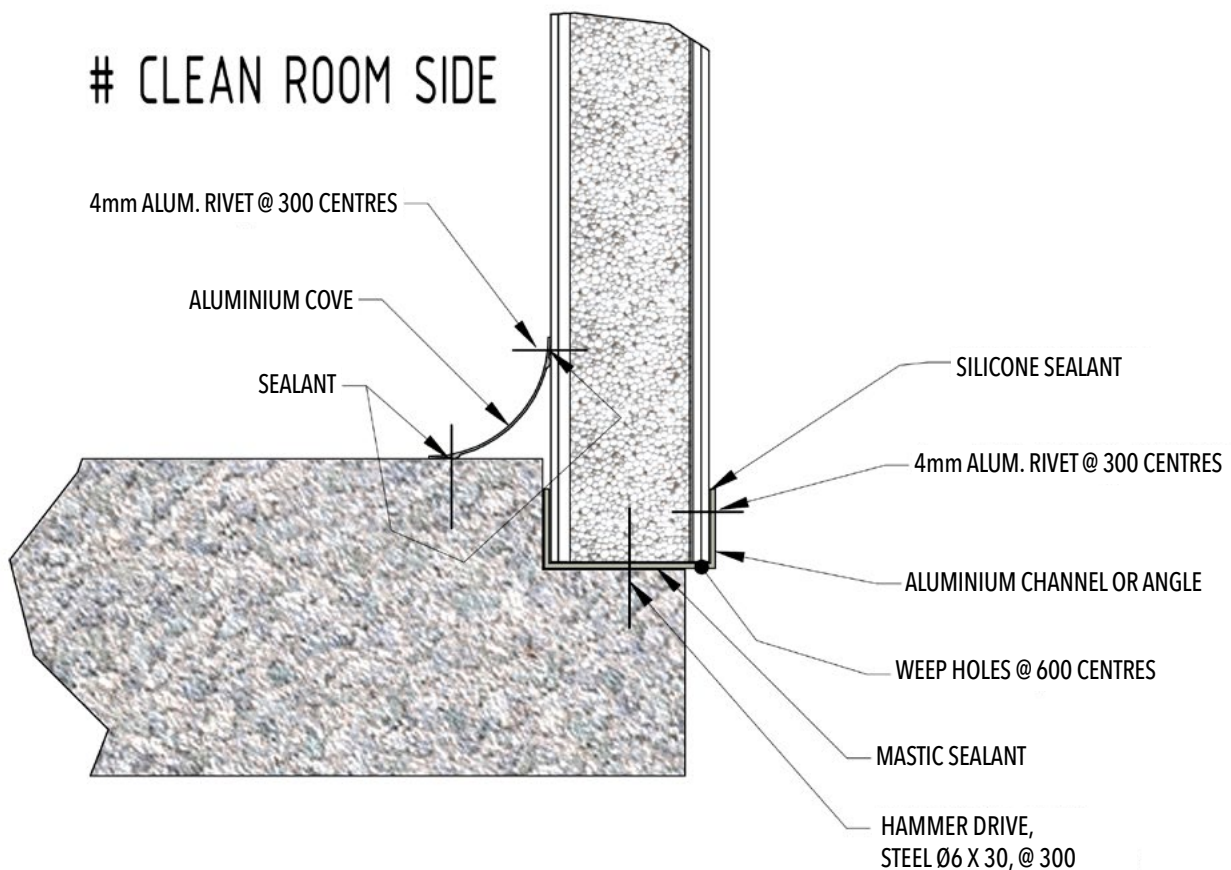

Description

ALTERNATE WALL TO FLOOR DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020

Designed by
MDI


Drawing No.
COLD STORE 1G

Rev: A Sheet
8/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.9 ALTERNATE WALL TO FLOOR DETAIL

CLEAN ROOM SIDE

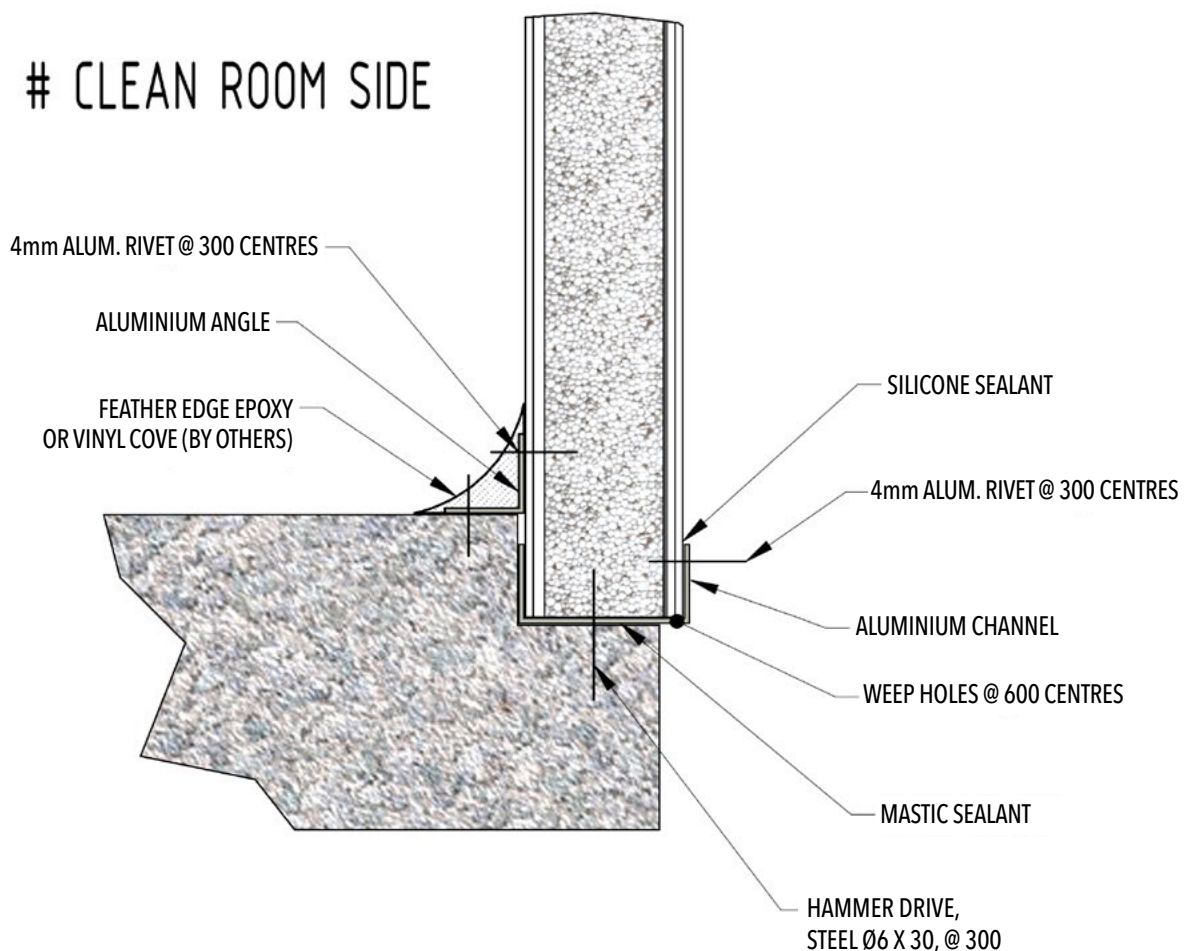

Description

ALTERNATE WALL TO FLOOR DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1H

Rev: A Sheet 9/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.10 ALTERNATE WALL TO FLOOR DETAIL

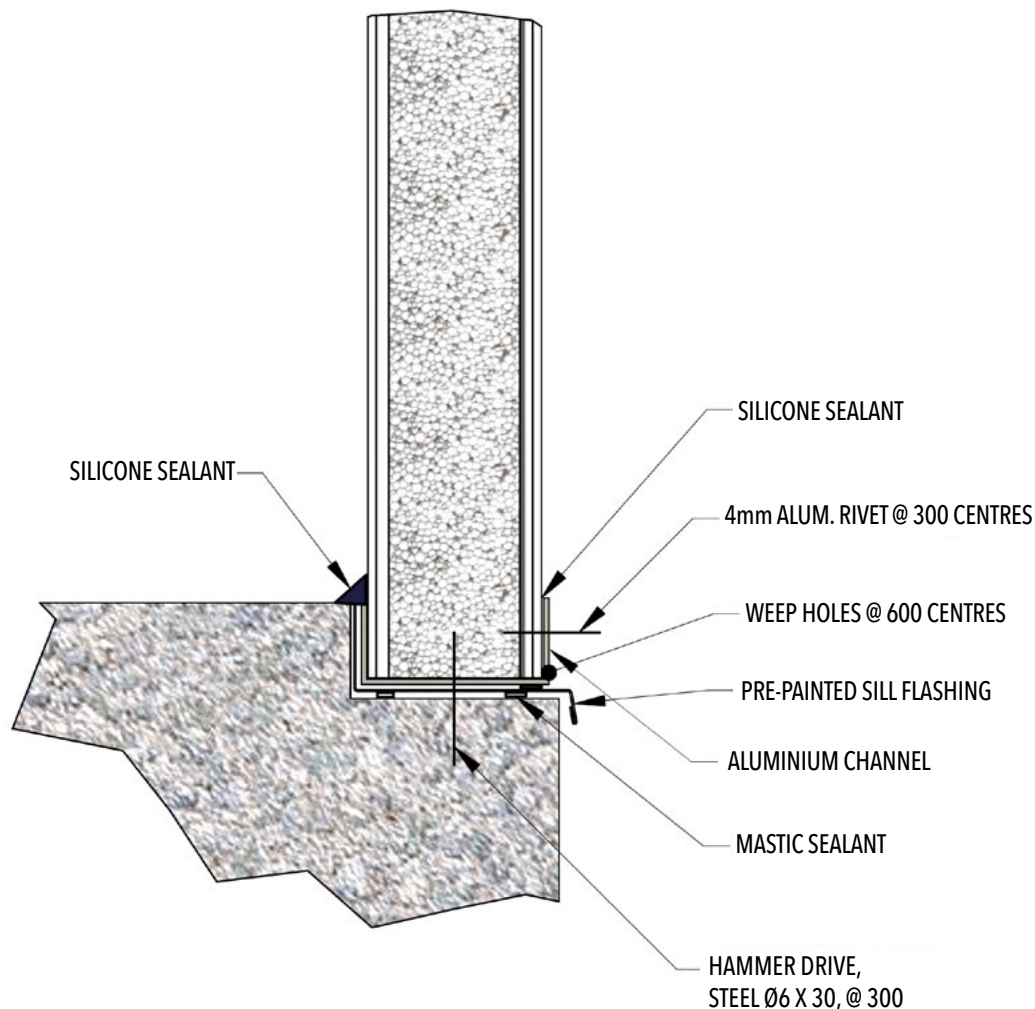

Description

ALTERNATE WALL TO FLOOR DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 11

Rev: A Sheet
10/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.11 ALTERNATE WALL TO FLOOR DETAIL

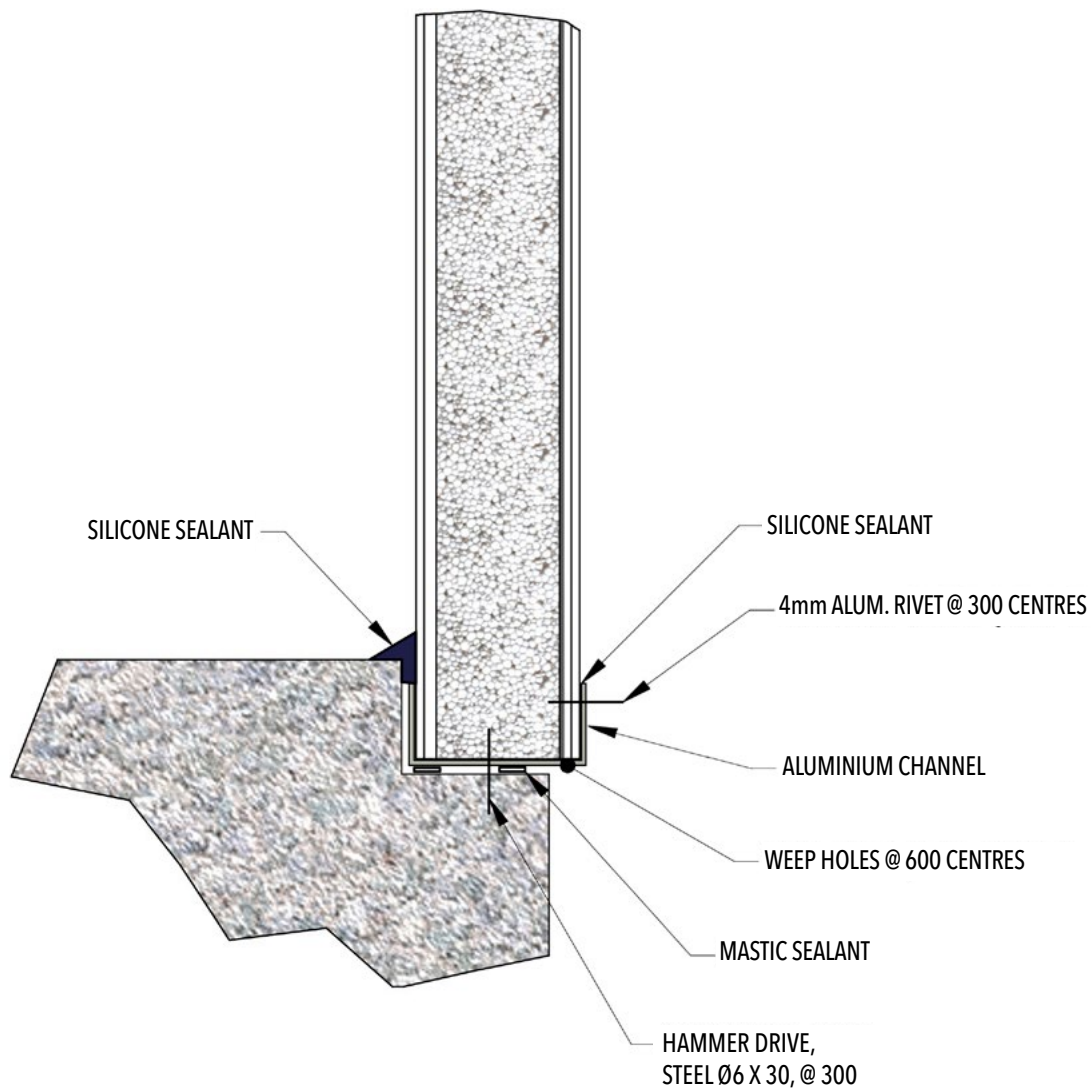

Description

ALTERNATE WALL TO FLOOR DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1J

Rev: A Sheet
11/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.12 ALTERNATE WALL TO FLOOR DETAIL

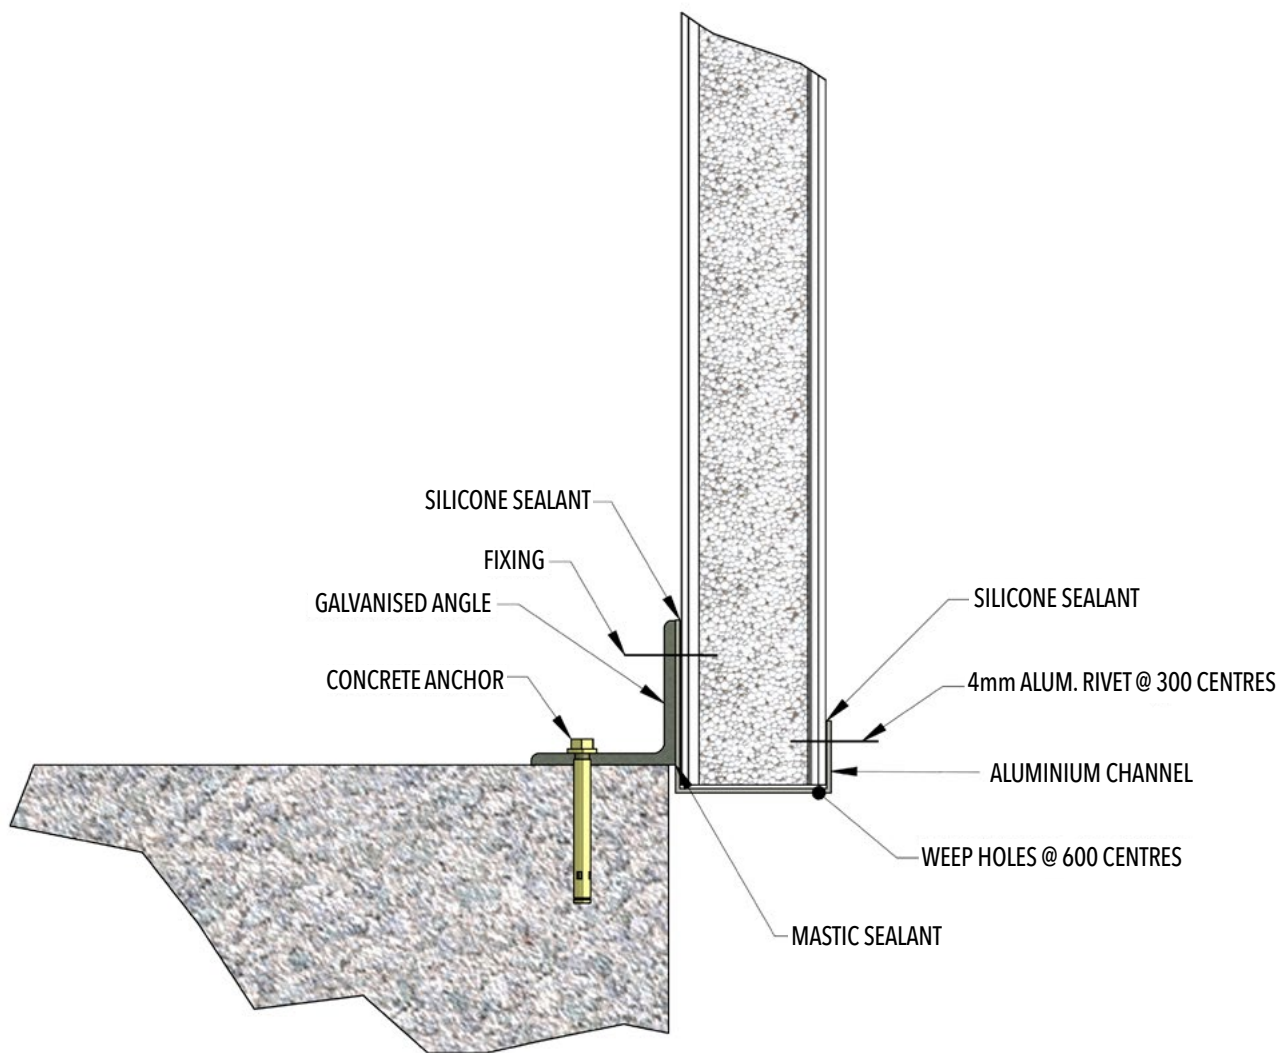

Description

ALTERNATE WALL TO FLOOR DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1K

Rev: A Sheet
12/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.13 ALTERNATE WALL TO FLOOR DETAIL

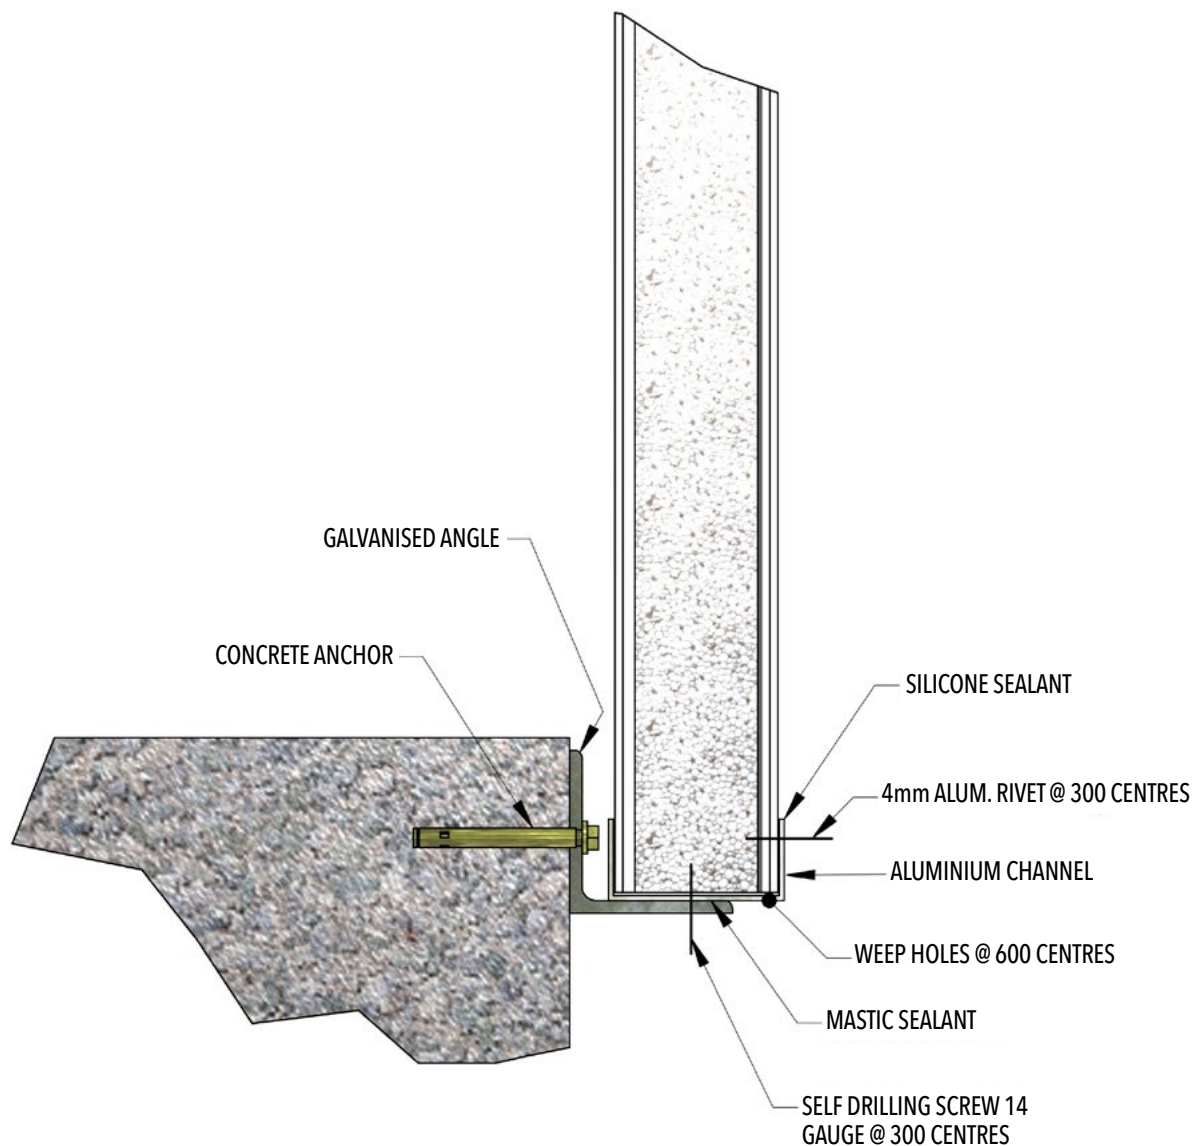

Description

ALTERNATE WALL TO FLOOR DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1L

Rev: A Sheet 13/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.14 TYPICAL EXTERNAL CORNER

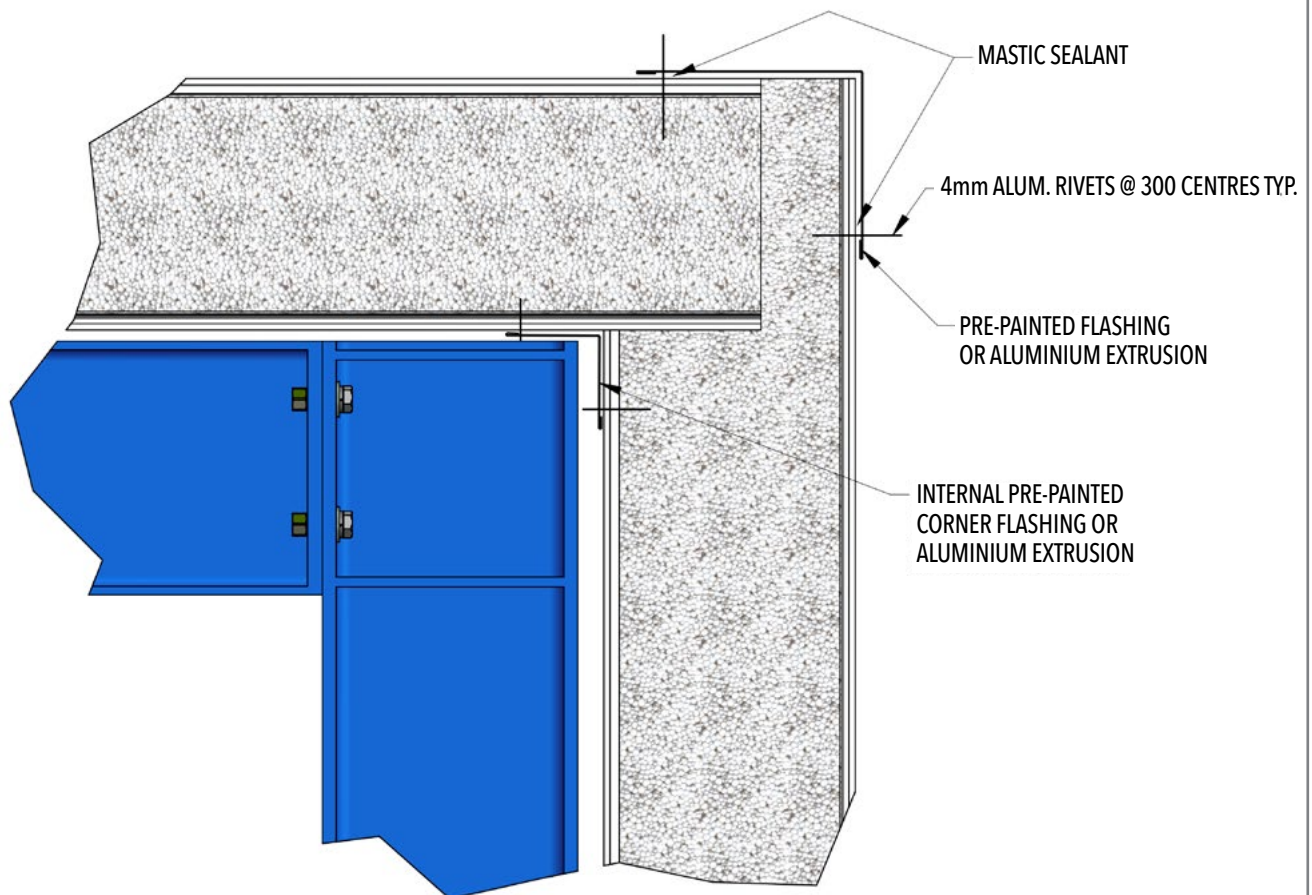

Description

TYPICAL EXTERNAL CORNER

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1M

Rev: A Sheet
14/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.15 TYPICAL EXTERNAL CORNER WITH 45 DEG. MITRE

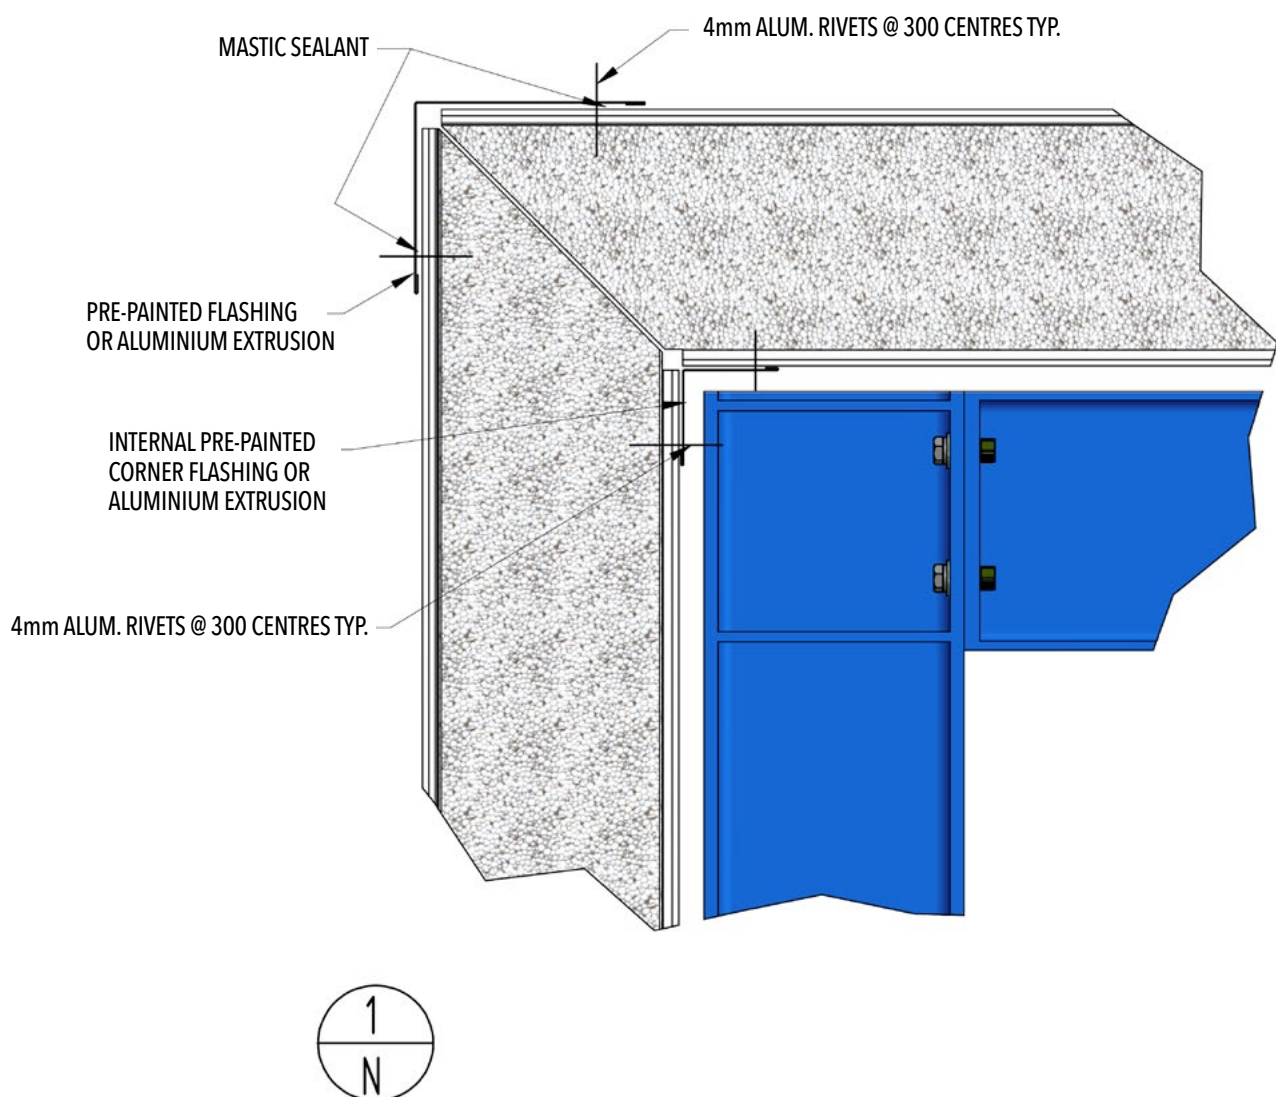

© COPYRIGHT RESERVED
Email: info@deltapanel.com

Description

TYPICAL EXTERNAL CORNER WITH 45 DEG. MITRE

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1N

Rev: A Sheet
15/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.16 WALL TO LOW CEILING

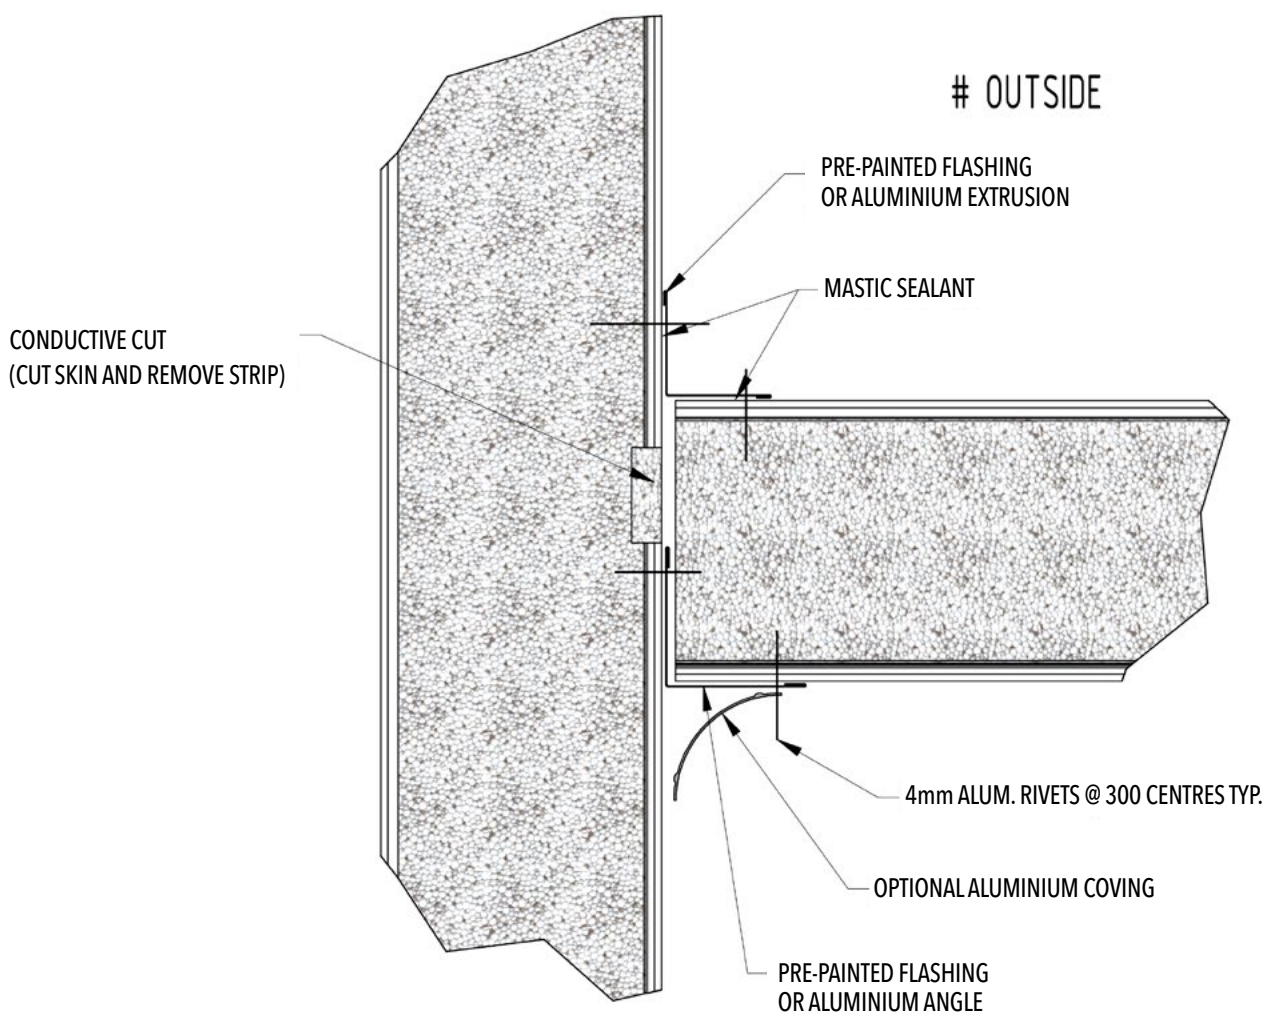

Description

WALL TO LOW CEILING

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 10

Rev: A Sheet
16/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.17 WALL TO LOW CEILING

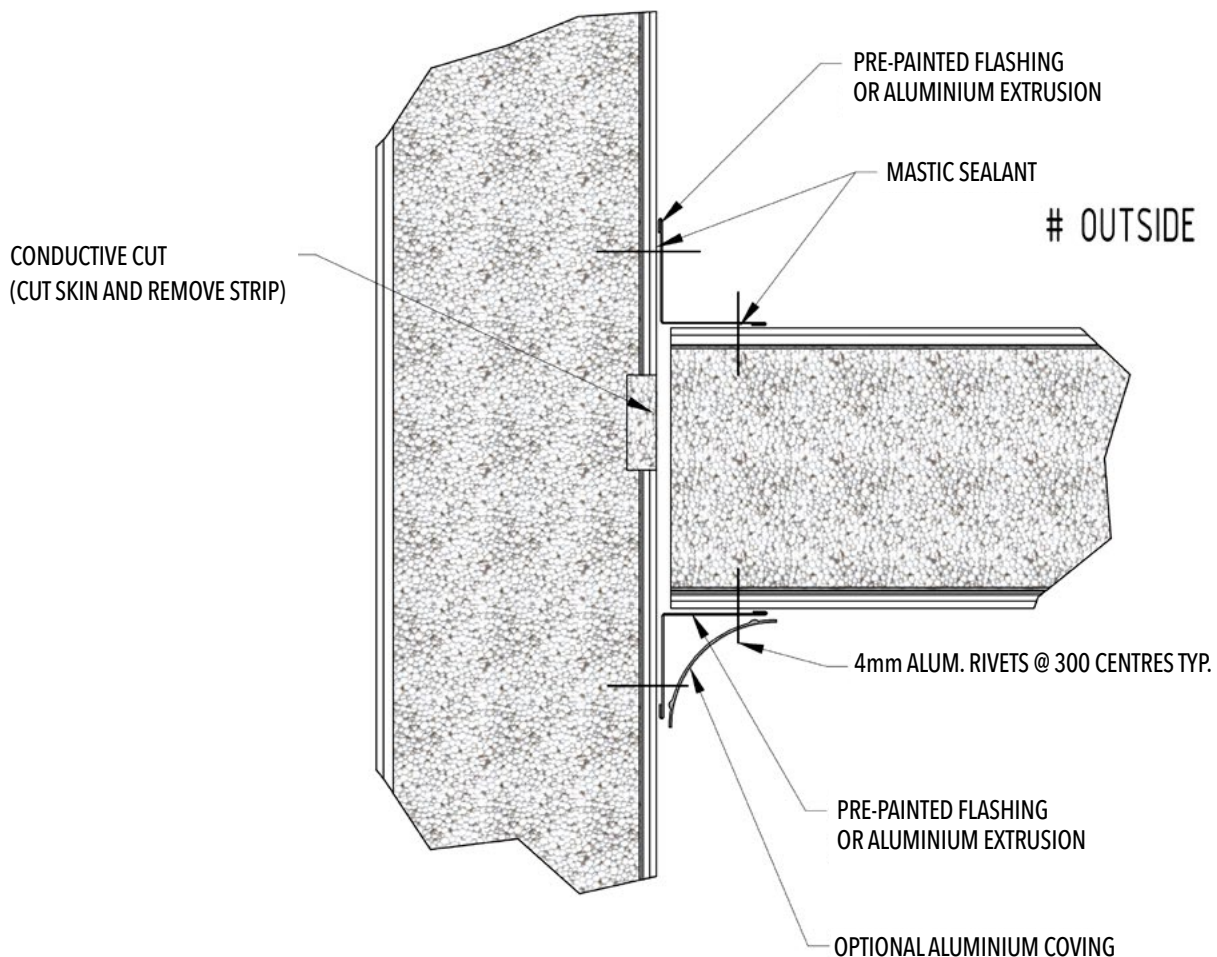

Description

WALL TO LOW CEILING

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1P

Rev: A Sheet
17/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.18 TYPICAL EXTERNAL CORNER, CLEAN ROOM

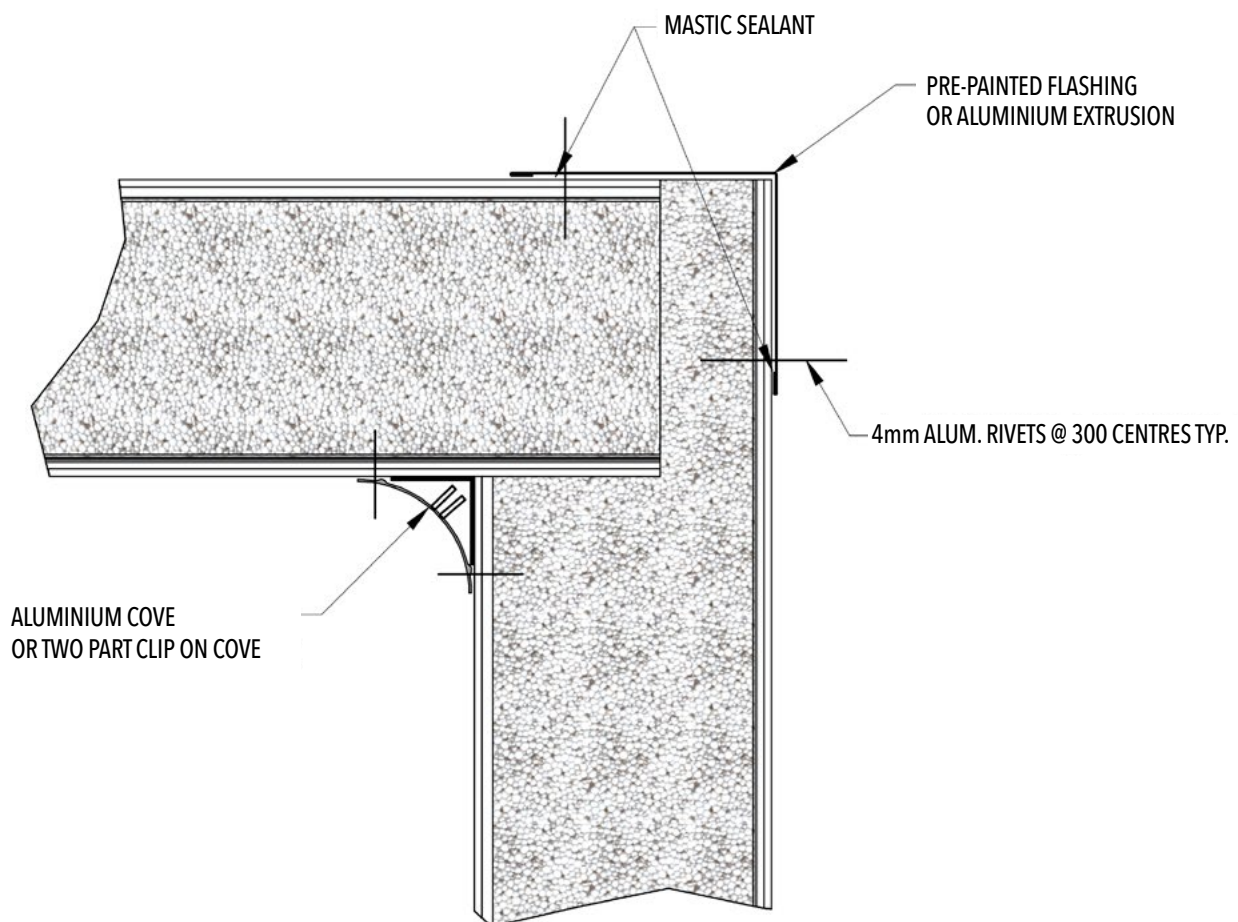

Description

TYPICAL EXTERNAL CORNER, CLEAN ROOM

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1Q

Rev: A Sheet
18/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.19 MAIN CEILING SUSPENSION

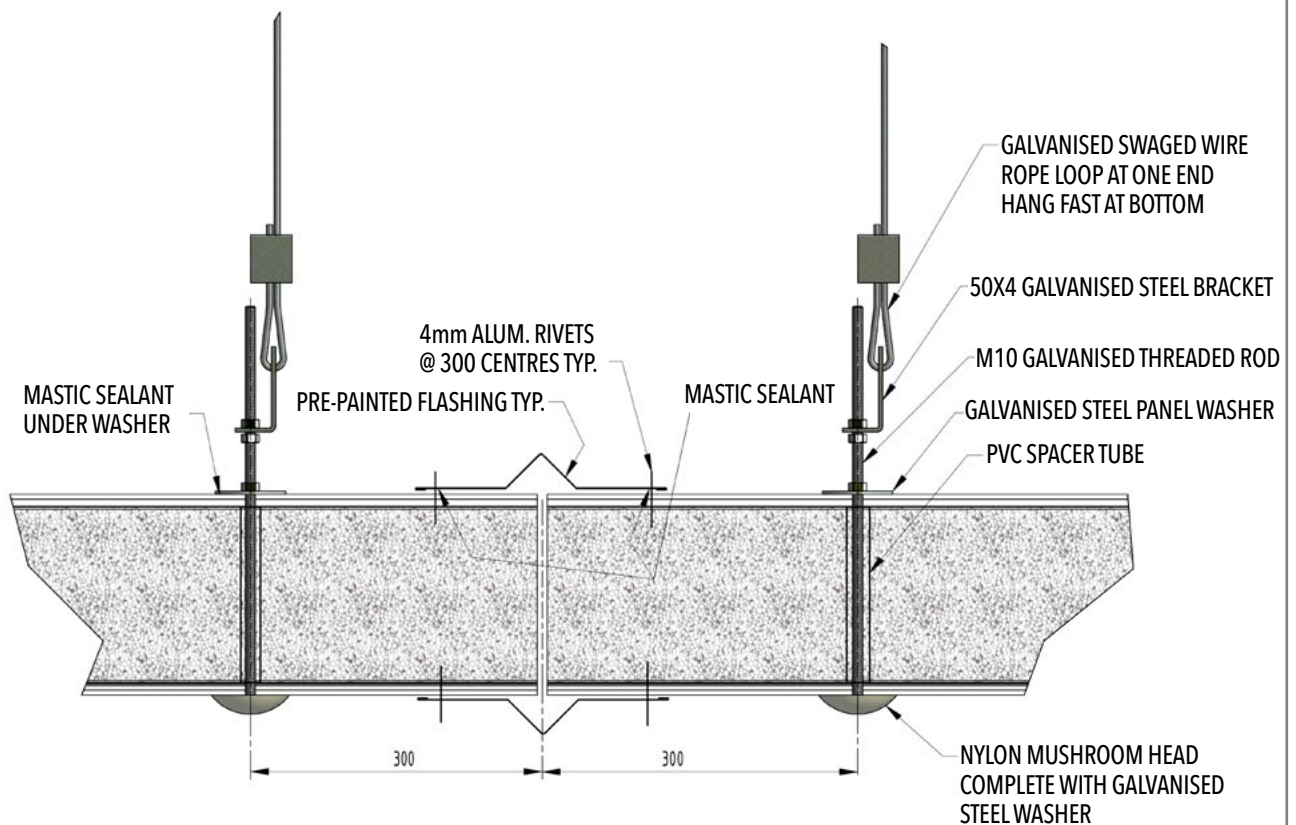

Description

MAIN CEILING SUSPENSION

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1R

Rev: A Sheet
19/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.20 PARTITION TO CEILING JOINT

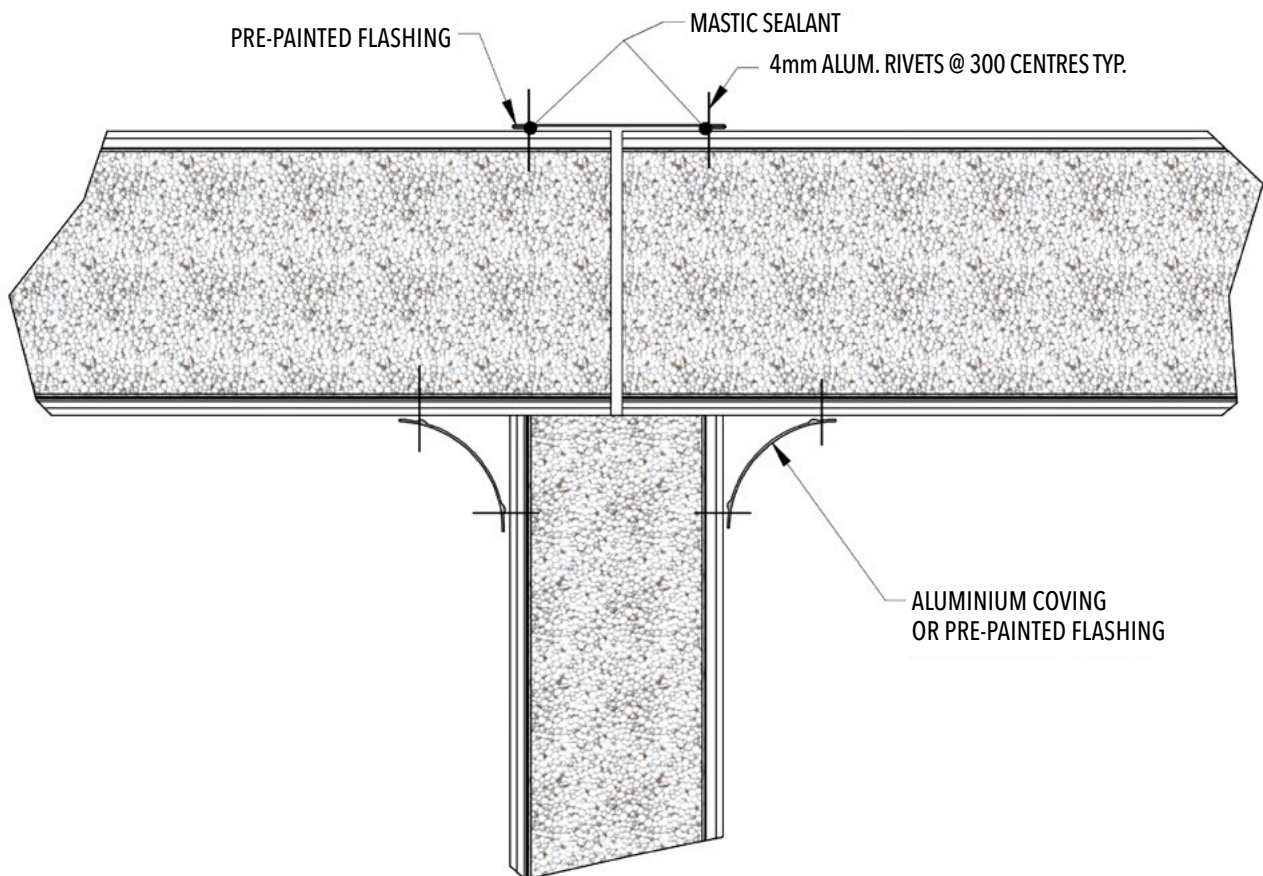

Description

PARTITION TO CEILING JOINT

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1S

Rev: A Sheet
20/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.21 PARTITION TO CEILING

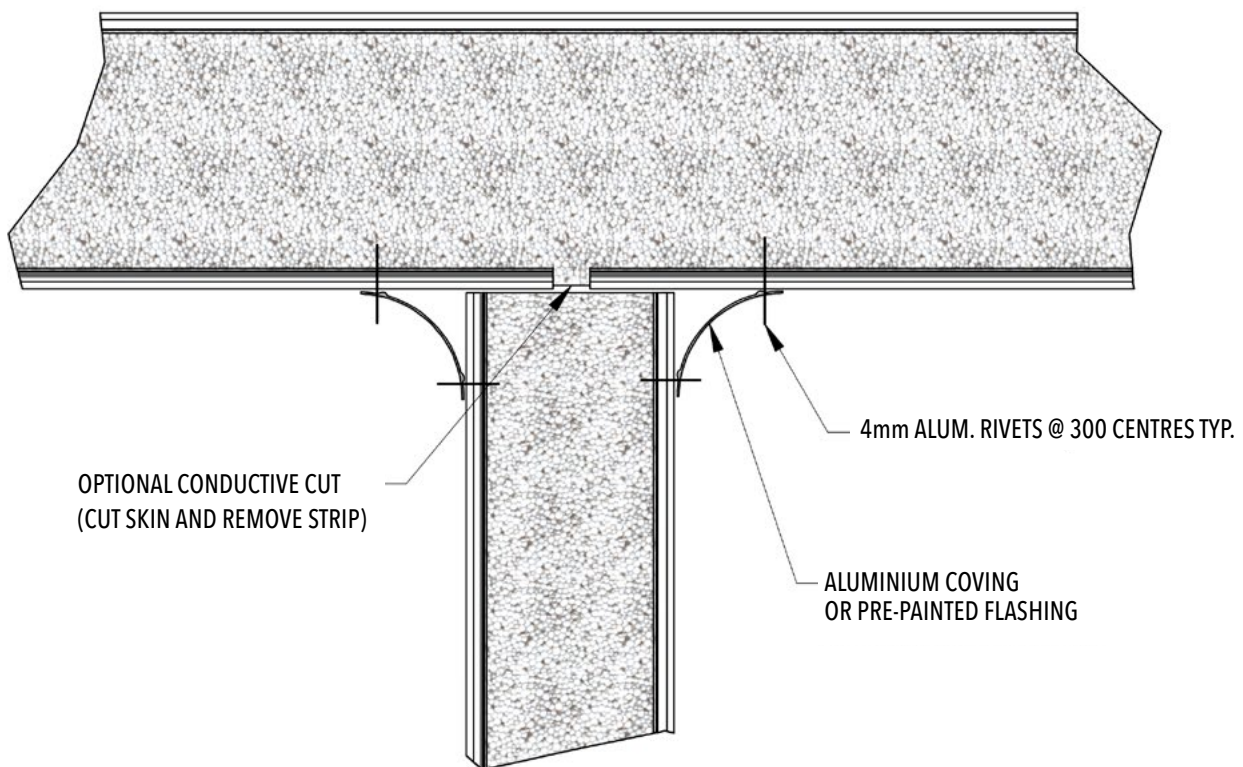

Description

PARTITION TO CEILING

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020


Designed by
MDI

Drawing No.
COLD STORE 1T

Rev: A Sheet
21/22

15. STANDARD INSTALLATION & CONNECTION DETAILS

15.22 INTERMEDIATE CEILING SUSPENSION

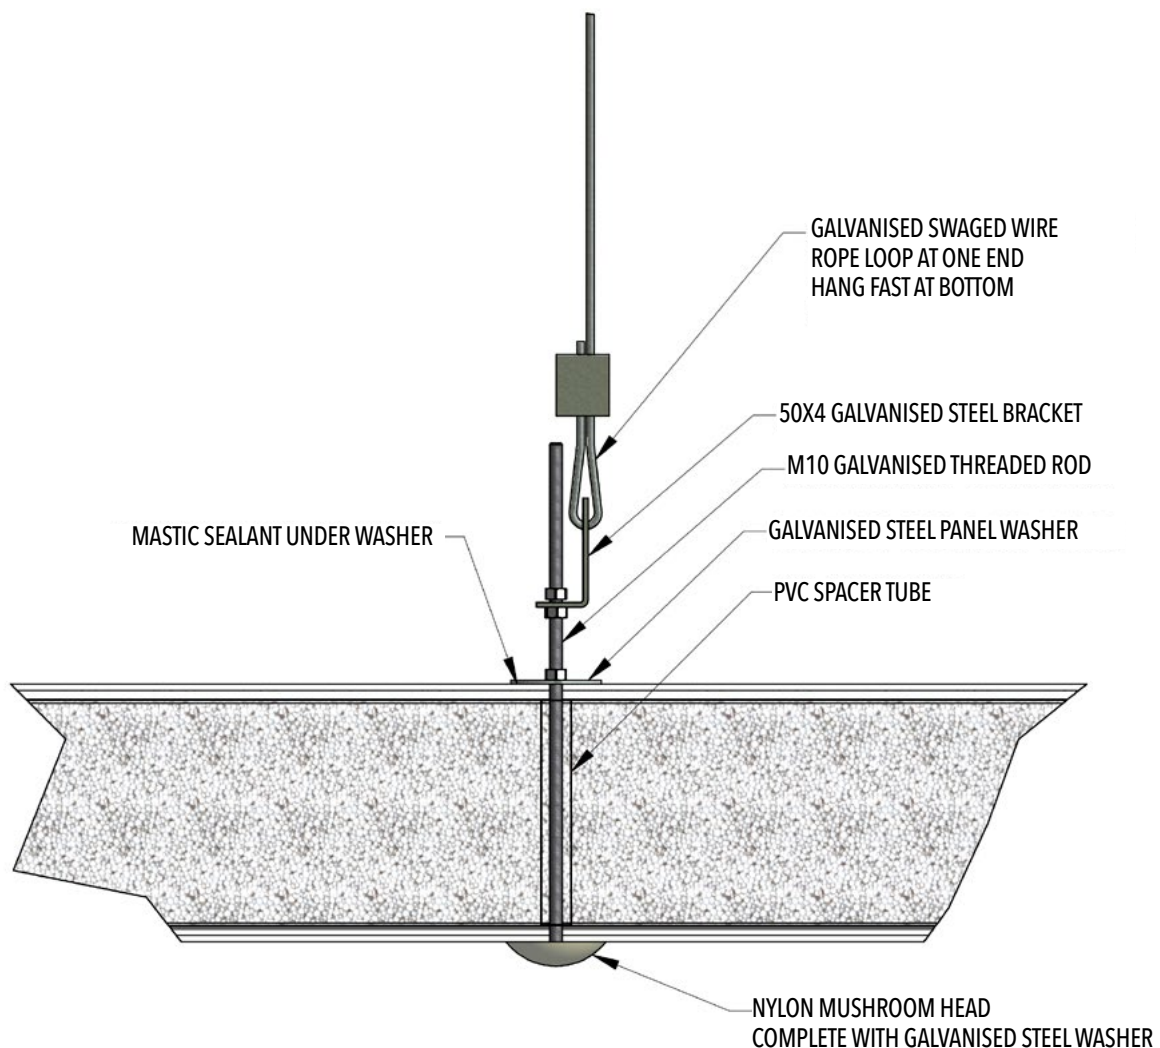

Description

INTERMEDIATE CEILING SUSPENSION

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\DELTA COLDROOM\COLD STORE.iam

Date:
20/10/2020

Designed by
MDI


Drawing No.
COLD STORE 1U

Rev: A Sheet
22/22

16. EXTERNAL CLADDING -

HORIZONTAL INSTALLATION & CONNECTION DETAILS

16.1 TYPICAL JOINTS FIXING

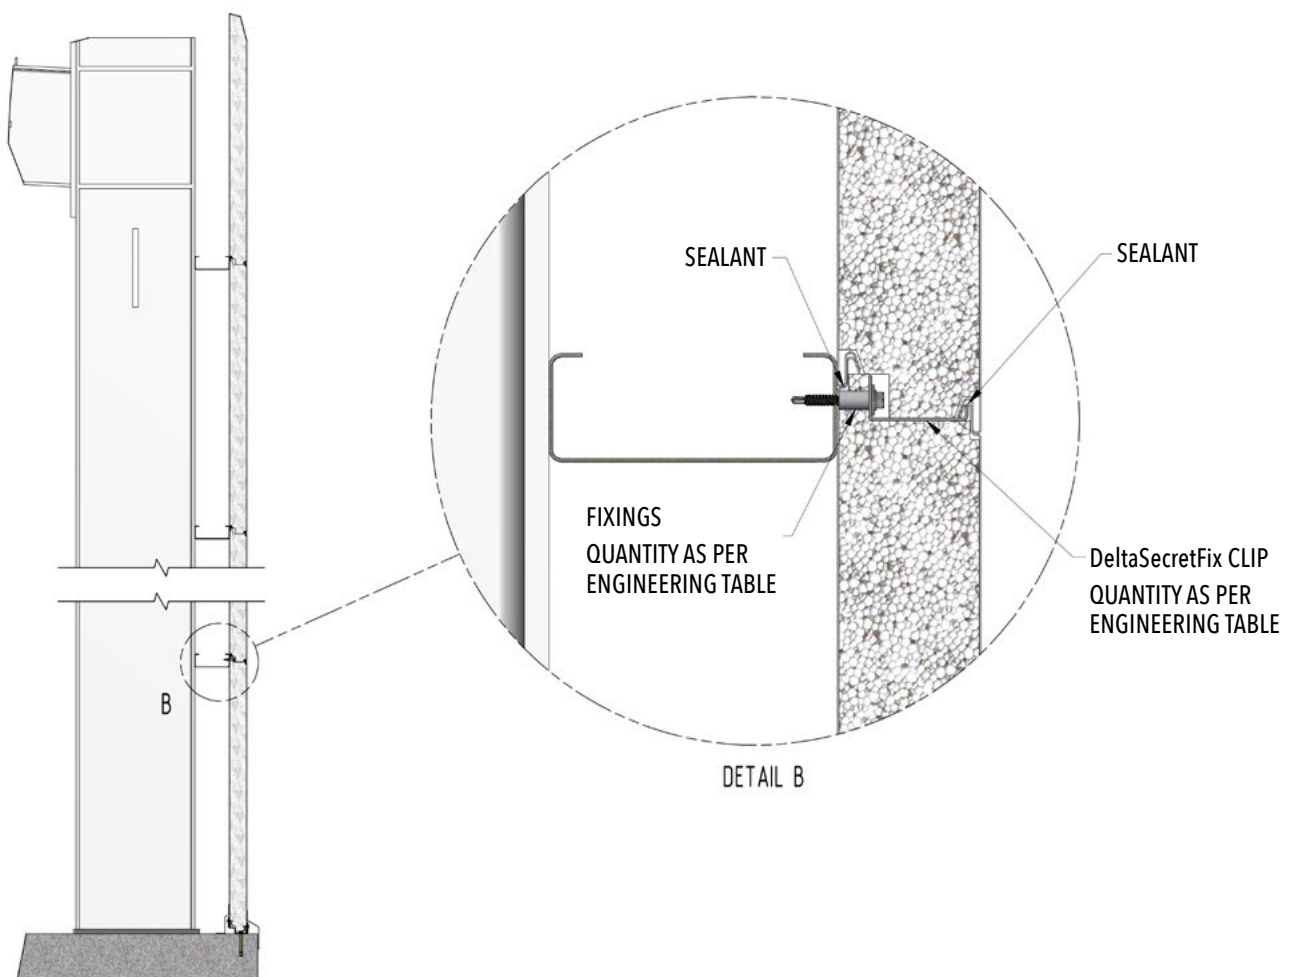

Description

SECRET FIX HORIZONTAL JOINTS TYP. JOINTS FIXING

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
7/12/2020

Designed by
DP


Drawing No.
WC1006-1

Rev: A Sheet
1/8

16. EXTERNAL CLADDING -

HORIZONTAL INSTALLATION & CONNECTION DETAILS

16.2 JOINTS BASE DETAIL

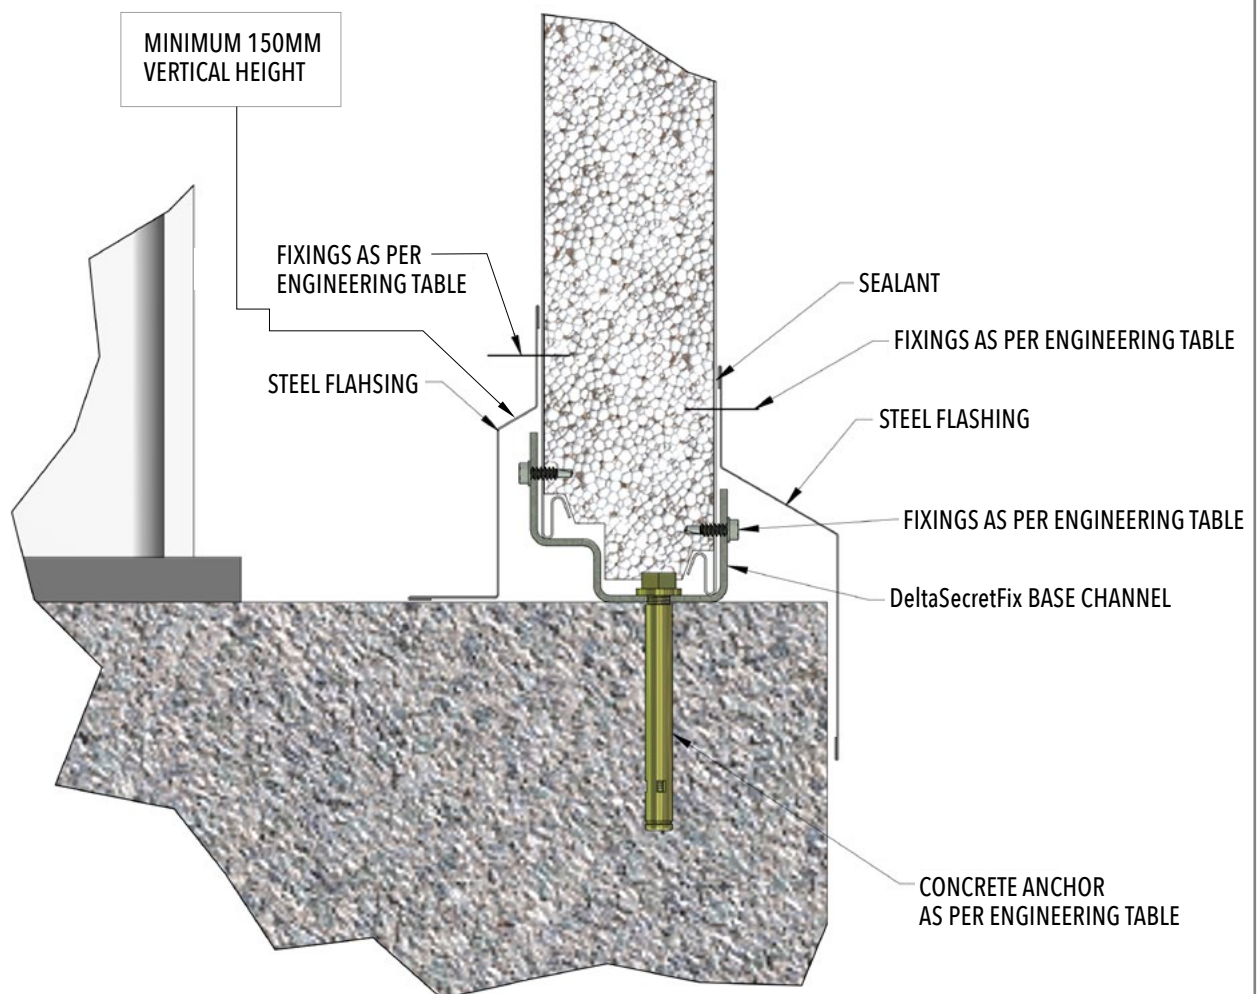

Description

SECRET FIX HORIZONTAL JOINTS BASE DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
7/12/2020

Designed by
DP


Drawing No.
WC1006-2

Rev: A
Sheet 2/8

16. EXTERNAL CLADDING -

HORIZONTAL INSTALLATION & CONNECTION DETAILS

16.3 JOINTS BASE DETAIL

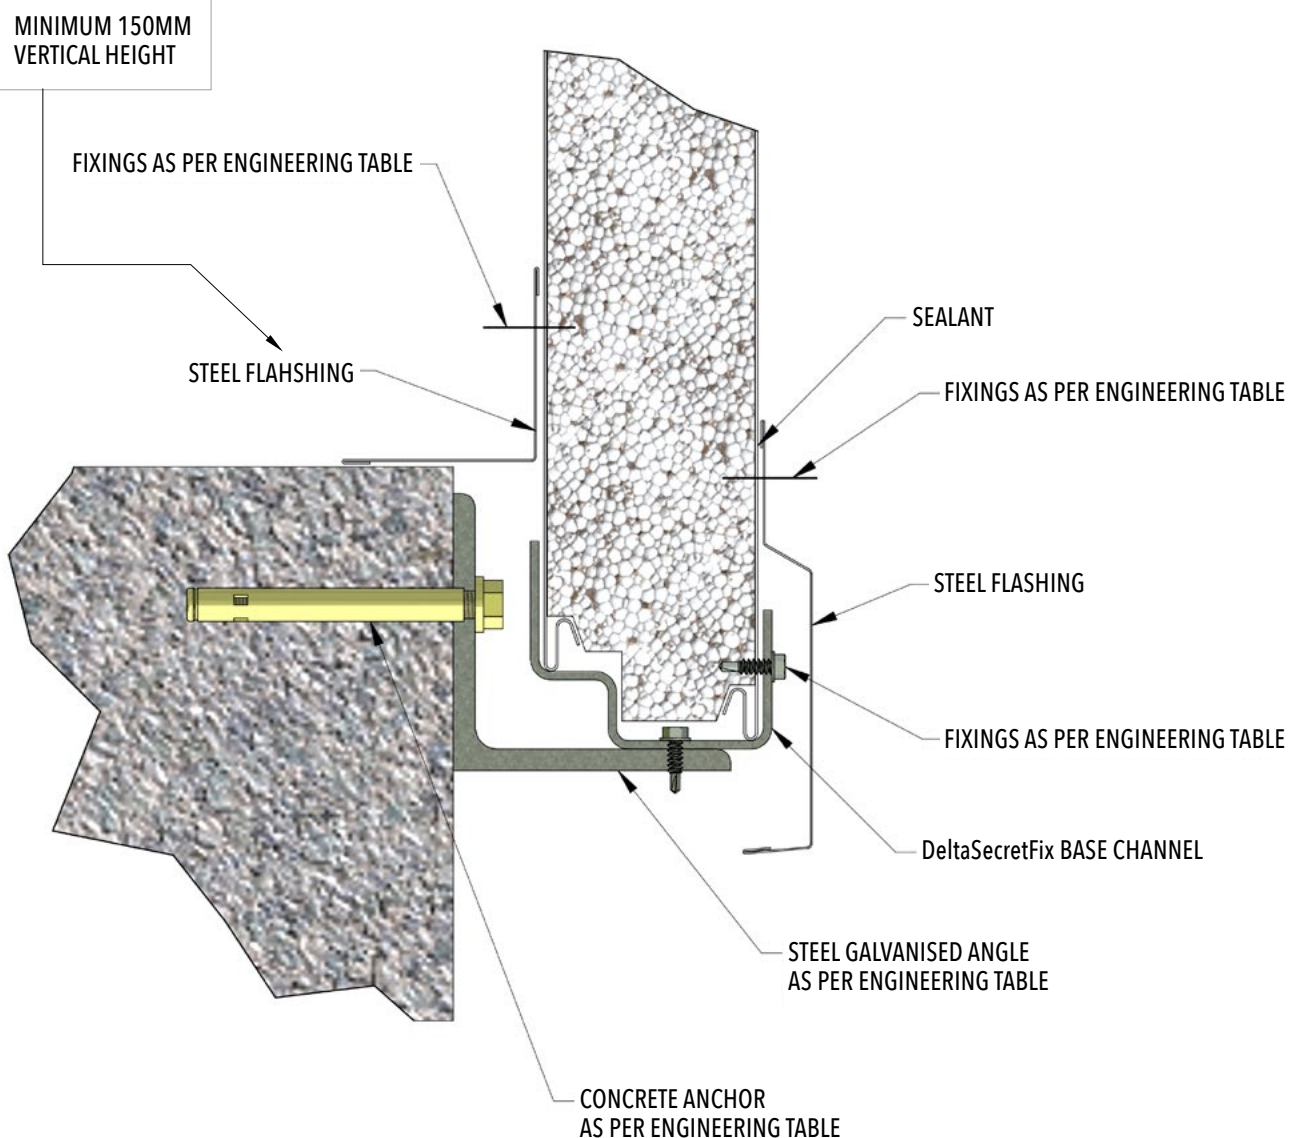

Description

SECRET FIX HORIZONTAL JOINTS BASE DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
7/12/2020

Designed by
DP

Drawing No.
WC1006-3


Rev: A Sheet 3/8

16. EXTERNAL CLADDING -

HORIZONTAL INSTALLATION & CONNECTION DETAILS

16.4 JOINTS BASE DETAIL

MINIMUM 150MM
VERTICAL HEIGHT

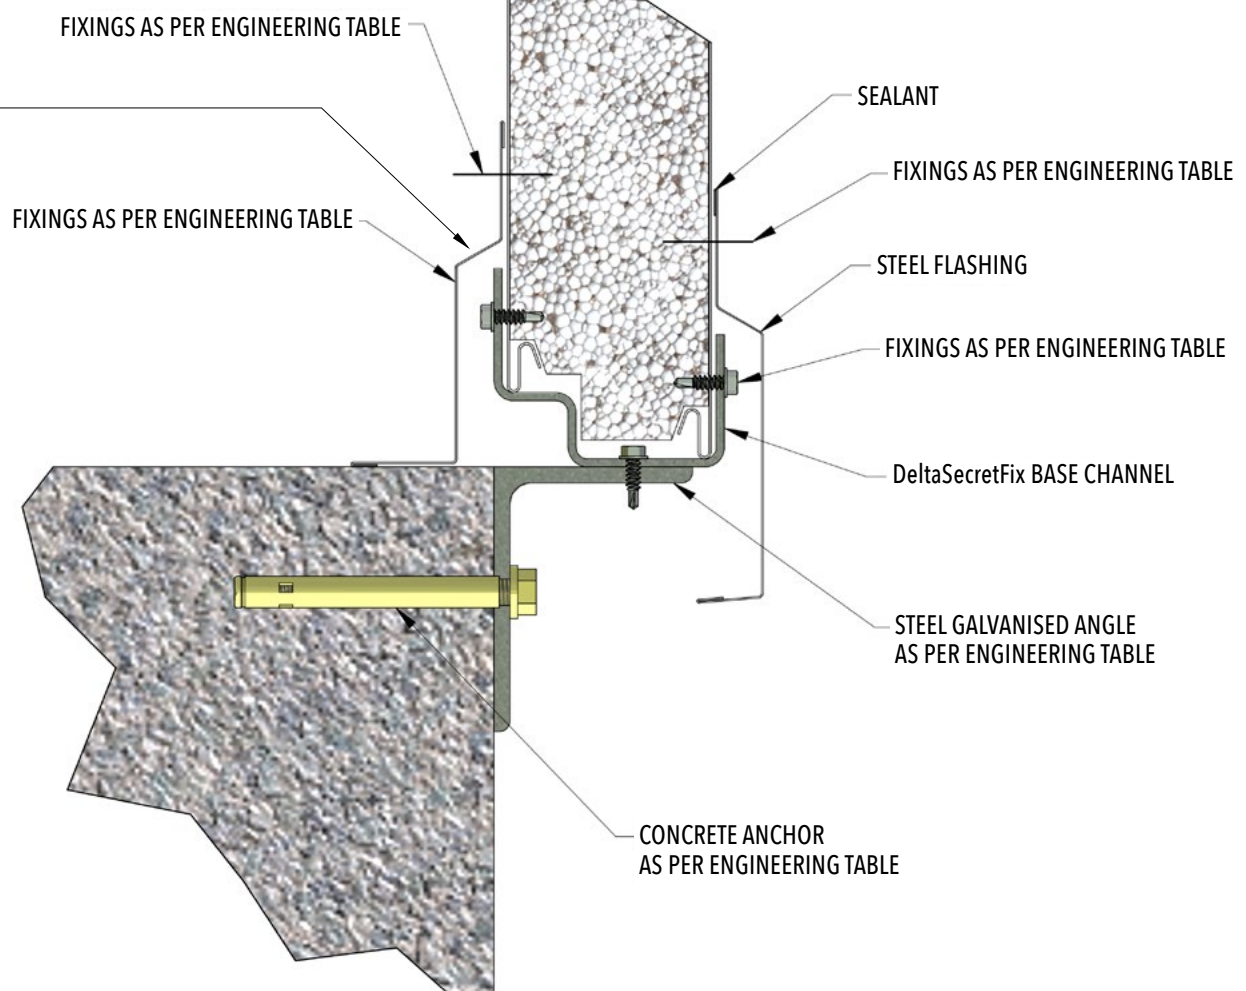

Description

SECRET FIX HORIZONTAL JOINTS BASE DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
7/12/2020

Designed by
DP


Drawing No.
WC1006-4

Rev: A Sheet
4/8

16. EXTERNAL CLADDING -

HORIZONTAL INSTALLATION & CONNECTION DETAILS

16.5 JOINTS EXTERNAL CORNER

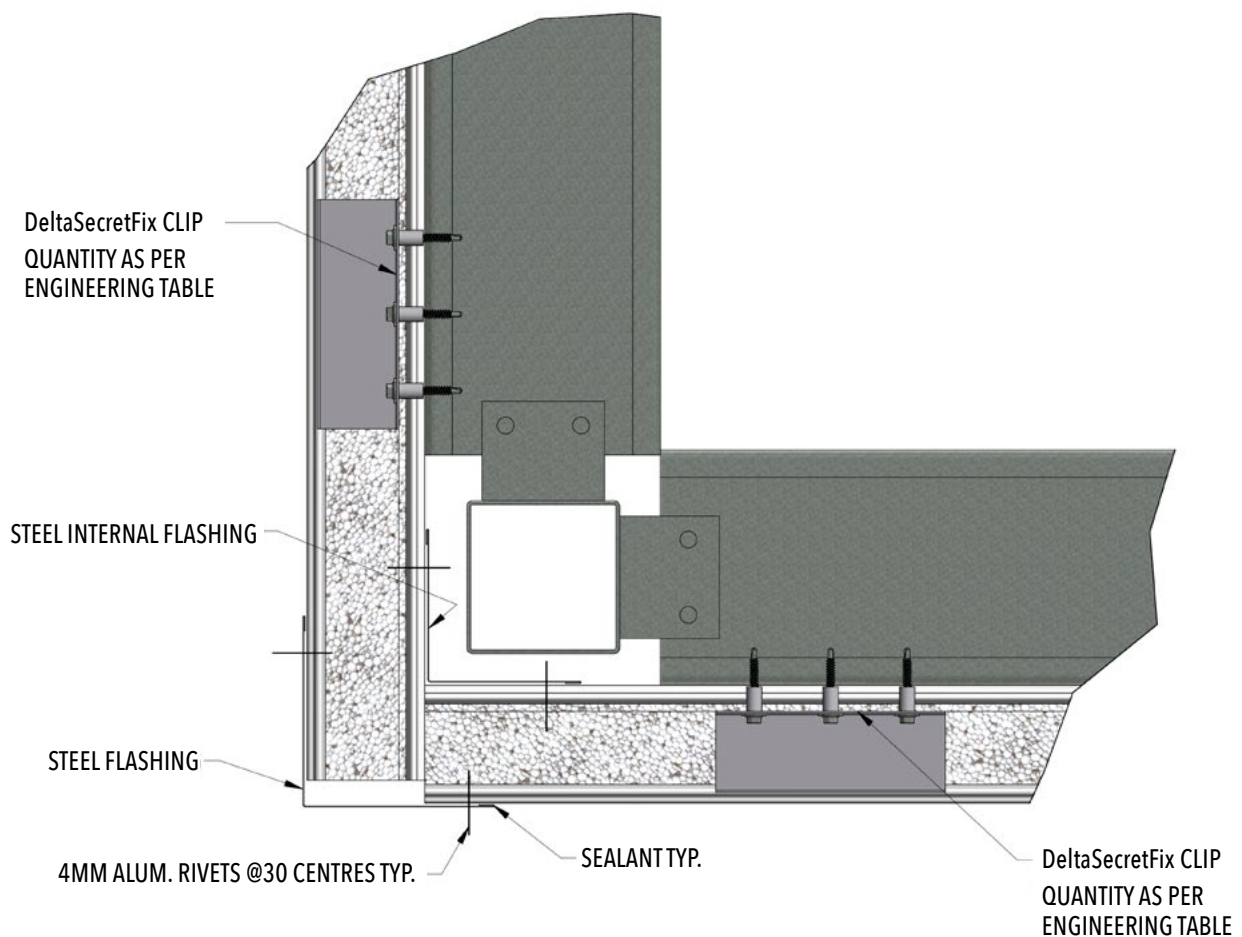

Description

SECRET FIX HORIZONTAL JOINTS EXTERNAL CORNER

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
7/12/2020


Designed by
DP

Drawing No.
WC1006-5

Rev: A Sheet
5/8

16. EXTERNAL CLADDING - HORIZONTAL INSTALLATION & CONNECTION DETAILS

16.6 JOINTS INTEGRATED WINDOW

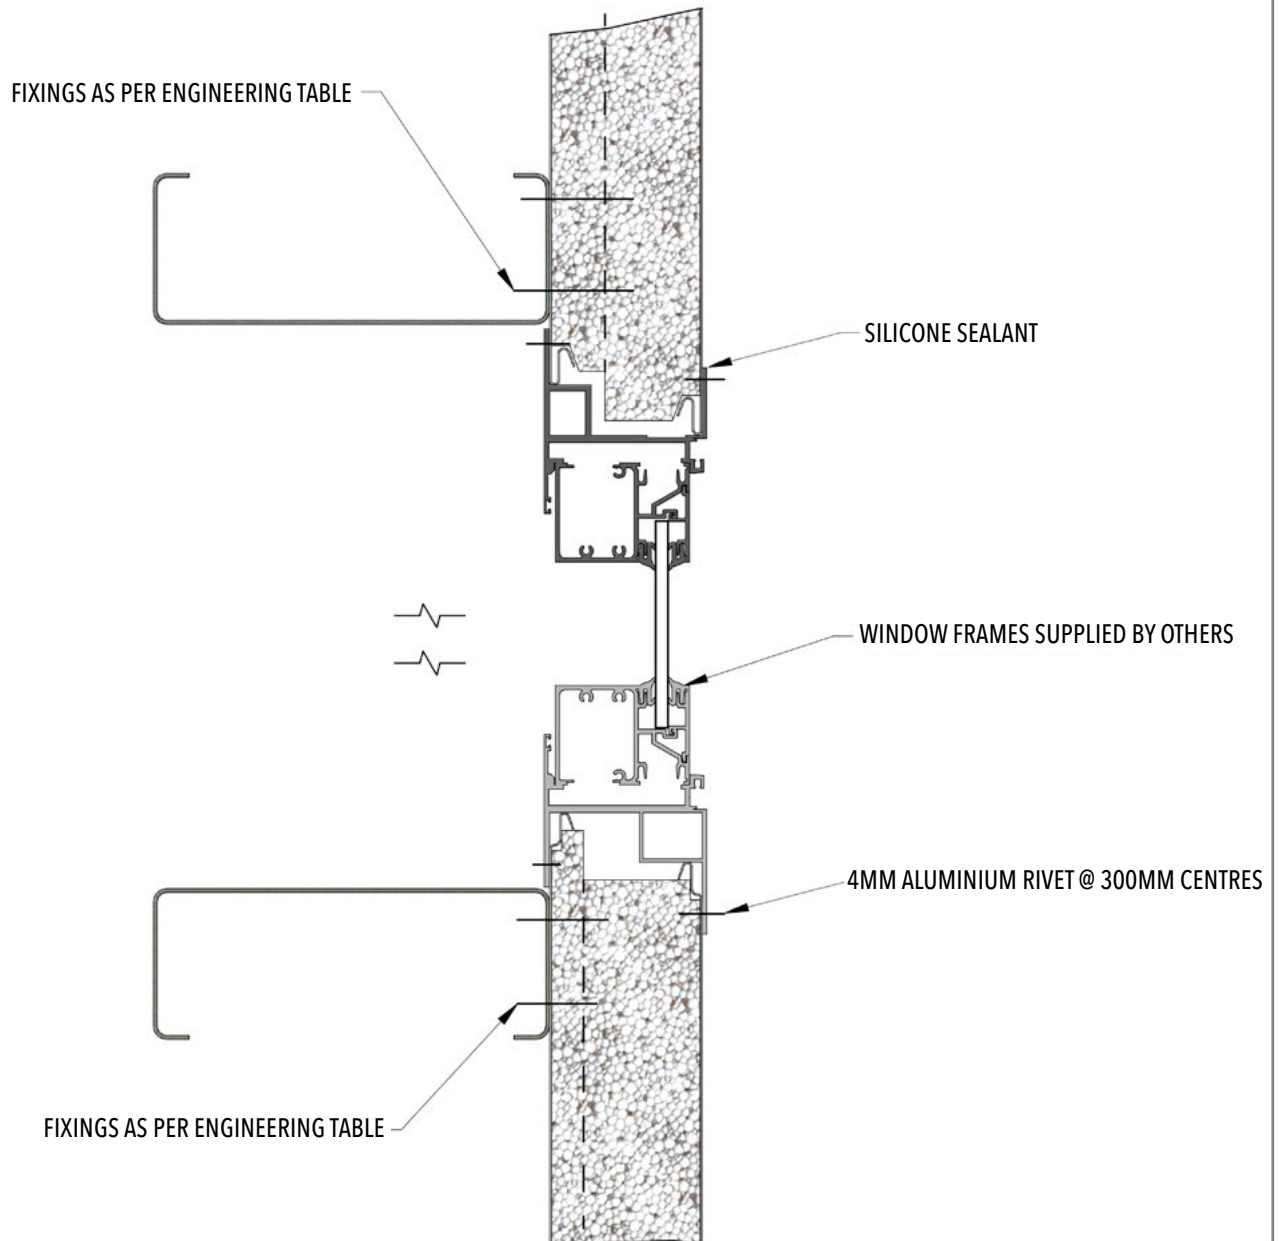

Description

SECRET FIX HORIZONTAL JOINTS INTEGRATED WINDOW

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iaw

Date:
7/12/2020

Designed by
DP


Drawing No.
WC1006-6

Rev: A Sheet
6/8

16. EXTERNAL CLADDING -

HORIZONTAL INSTALLATION & CONNECTION DETAILS

16.7 JOINTS RECESSED WINDOW

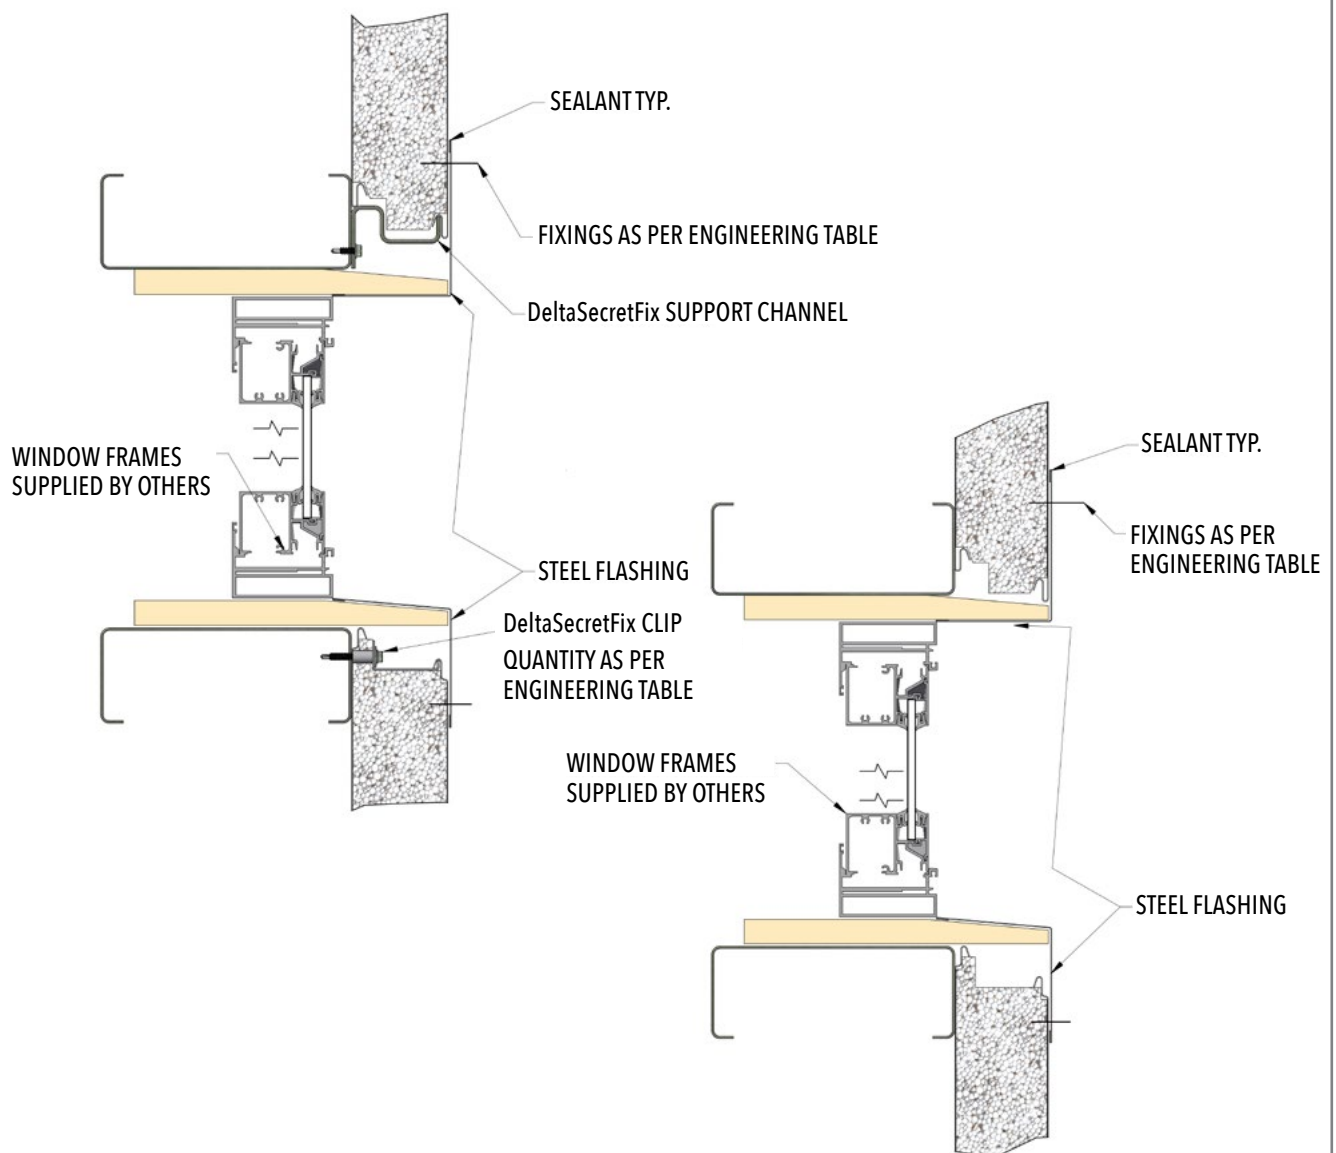

Description

SECRET FIX HORIZONTAL JOINTS RECESSED WINDOW

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
7/12/2020

Designed by
DP


Drawing No.
WC1006-7

Rev: A Sheet
7/8

16. EXTERNAL CLADDING -

HORIZONTAL INSTALLATION & CONNECTION DETAILS

16.8 JOINTS PERSONNEL DOOR DETAIL

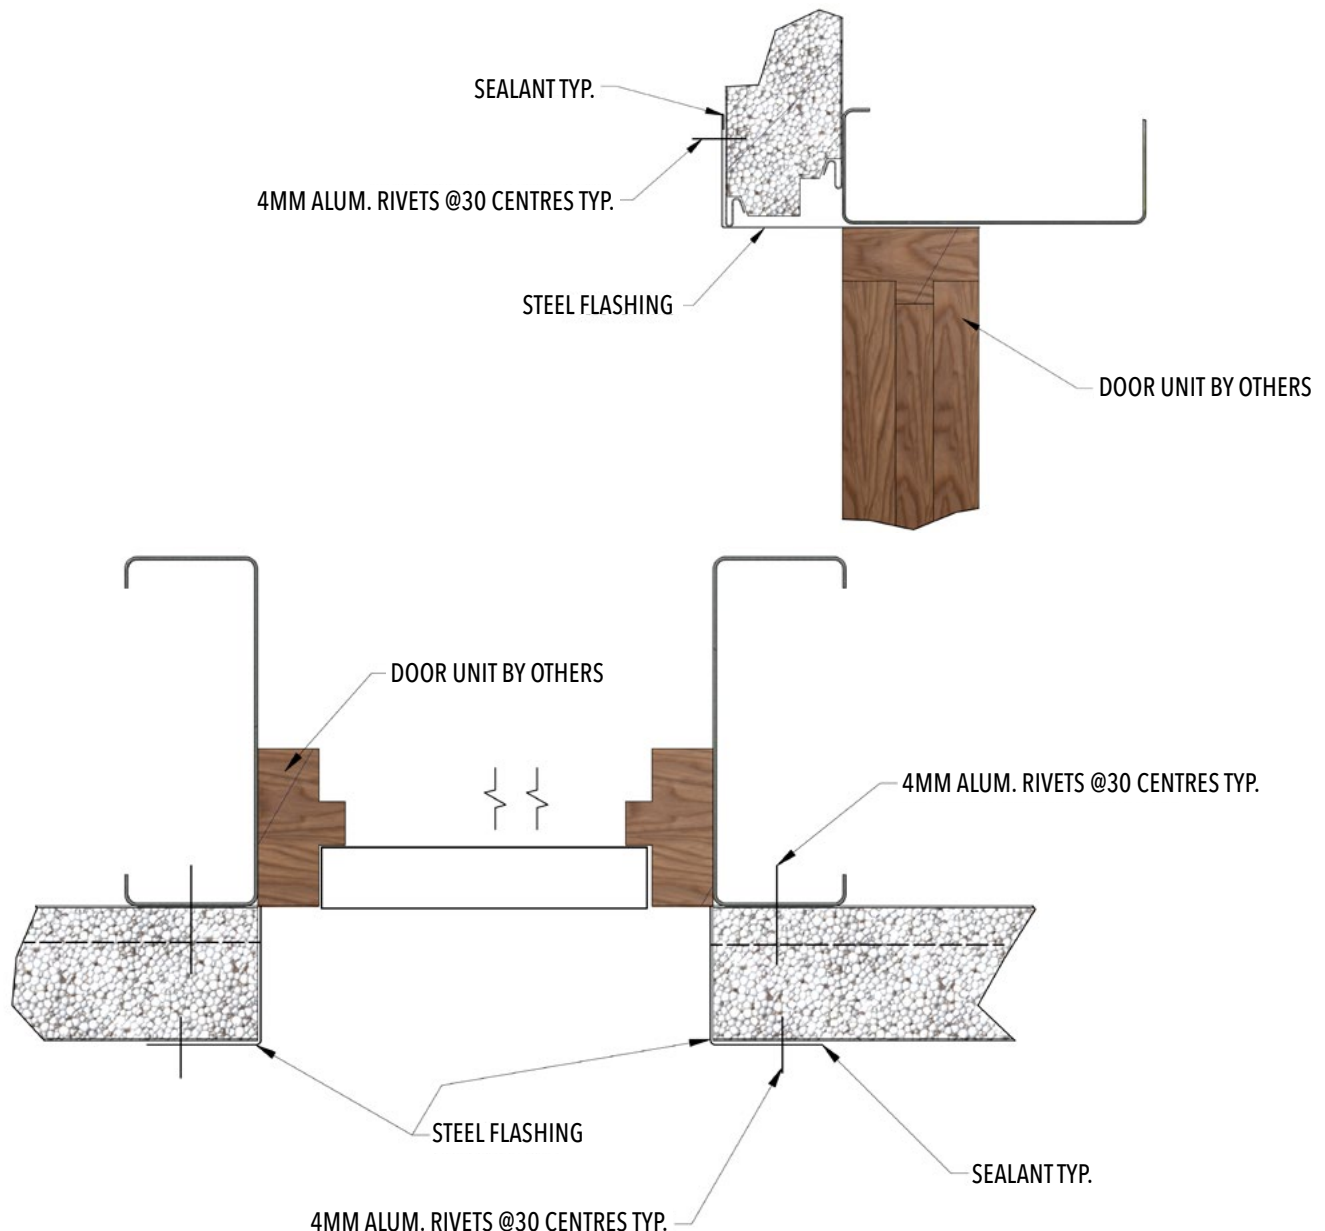

Description

SECRET FIX HORIZONTAL JOINTS PERSONNEL DOOR DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
7/12/2020


Designed by
DP

Drawing No.
WC1006-8

Rev: A Sheet
8/8

17. EXTERNAL CLADDING - VERTICAL INSTALLATION & CONNECTION DETAILS

17.1 JOINTS FIXING

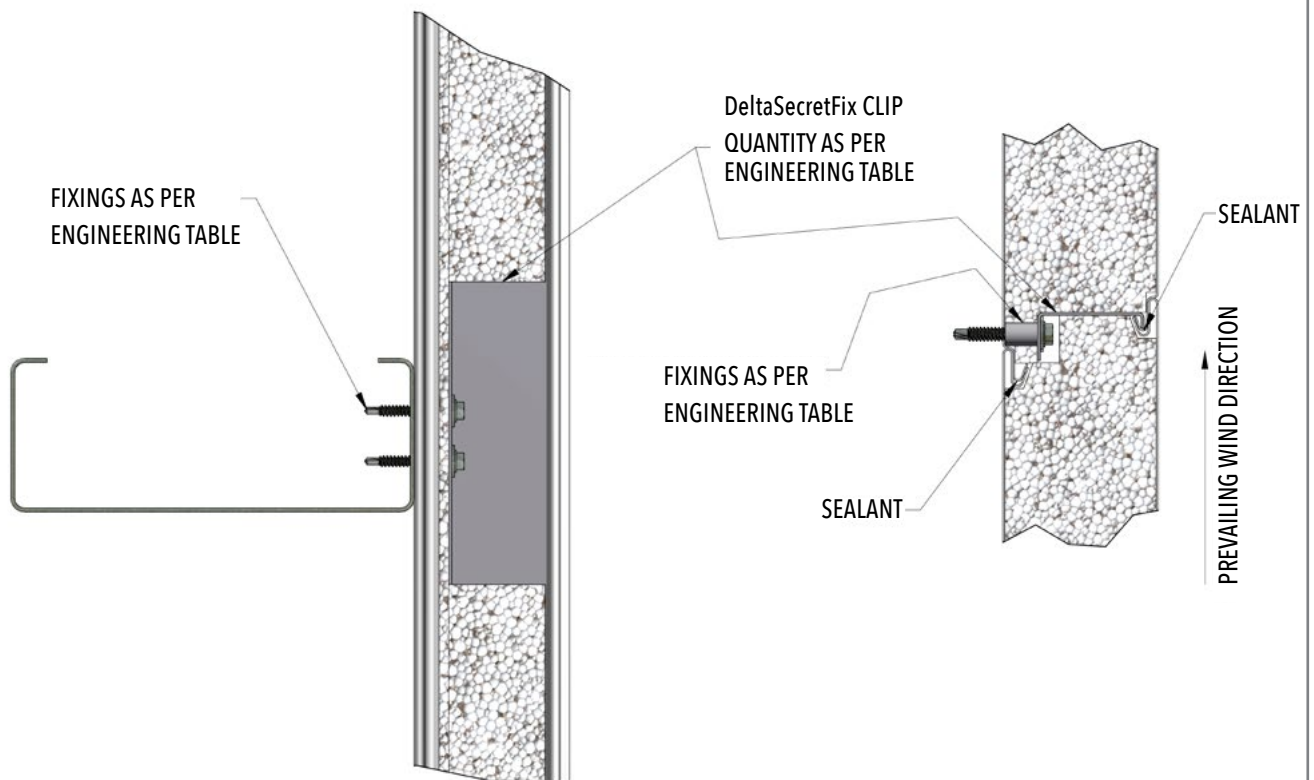

Description

SECRET FIX VERTICAL JOINTS FIXING

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
7/12/2020


Designed by
DP

Drawing No.
WC1005-1

Rev: A
Sheet 1/9

17. EXTERNAL CLADDING - VERTICAL INSTALLATION & CONNECTION DETAILS

17.2 JOINTS BASE DETAIL

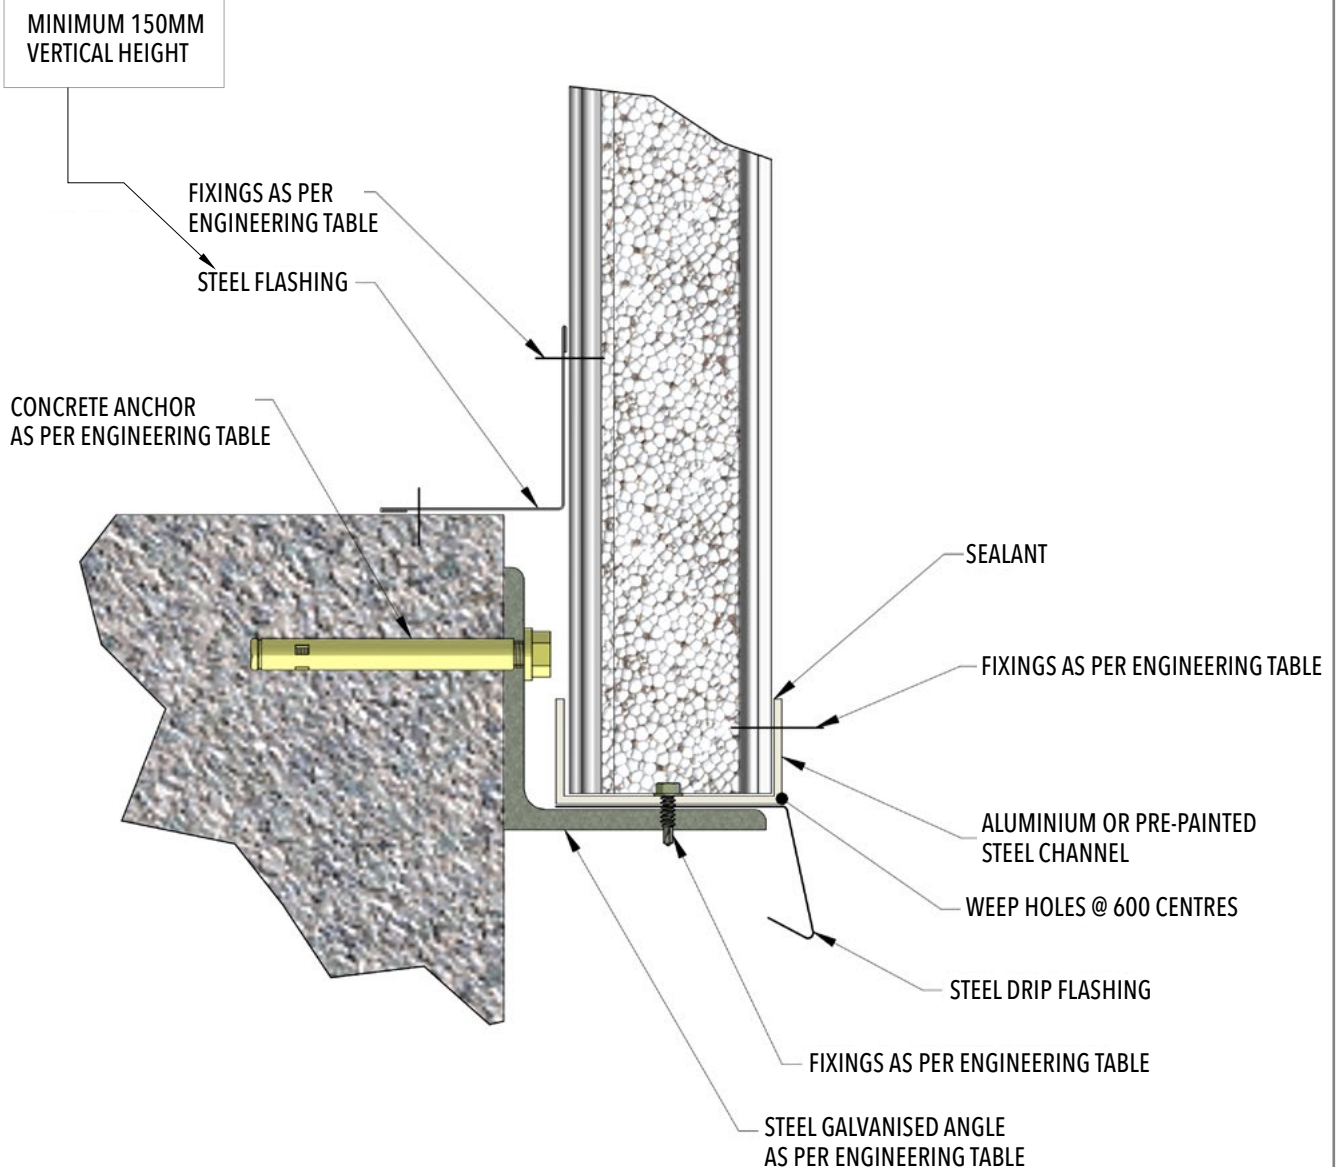

Description

SECRET FIX VERTICAL JOINTS BASE DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
7/12/2020


Designed by
DP

Drawing No.
WC1005-2

Rev: A Sheet
2/9

17. EXTERNAL CLADDING - VERTICAL INSTALLATION & CONNECTION DETAILS

17.3 JOINTS BASE DETAIL

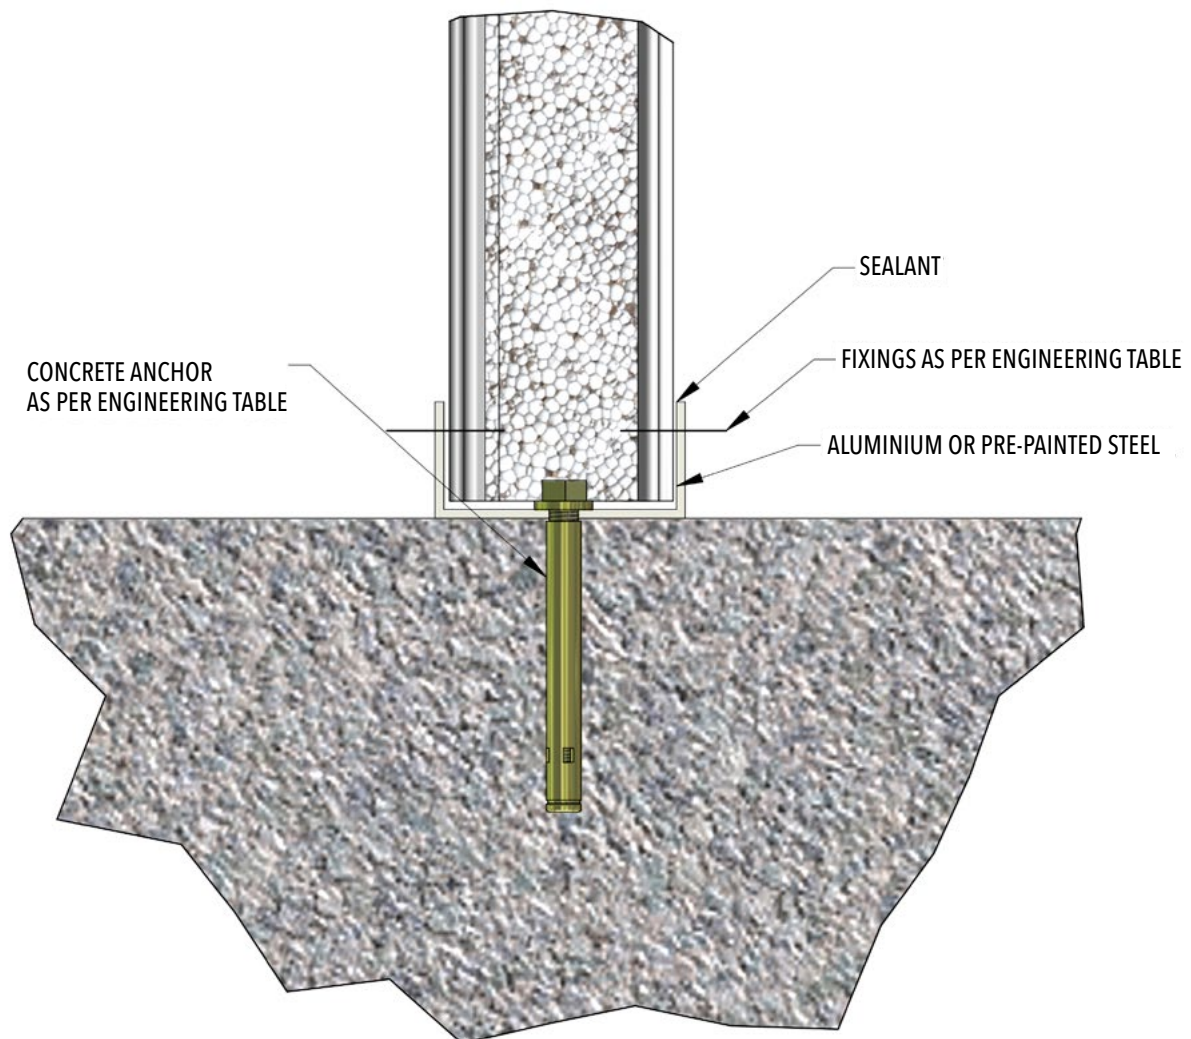

Description

SECRET FIX VERTICAL JOINTS BASE DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
7/12/2020


Designed by
DP

Drawing No.
WC1005-3

Rev: A Sheet
3/9

17. EXTERNAL CLADDING - VERTICAL INSTALLATION & CONNECTION DETAILS

17.4 JOINTS BASE DETAIL

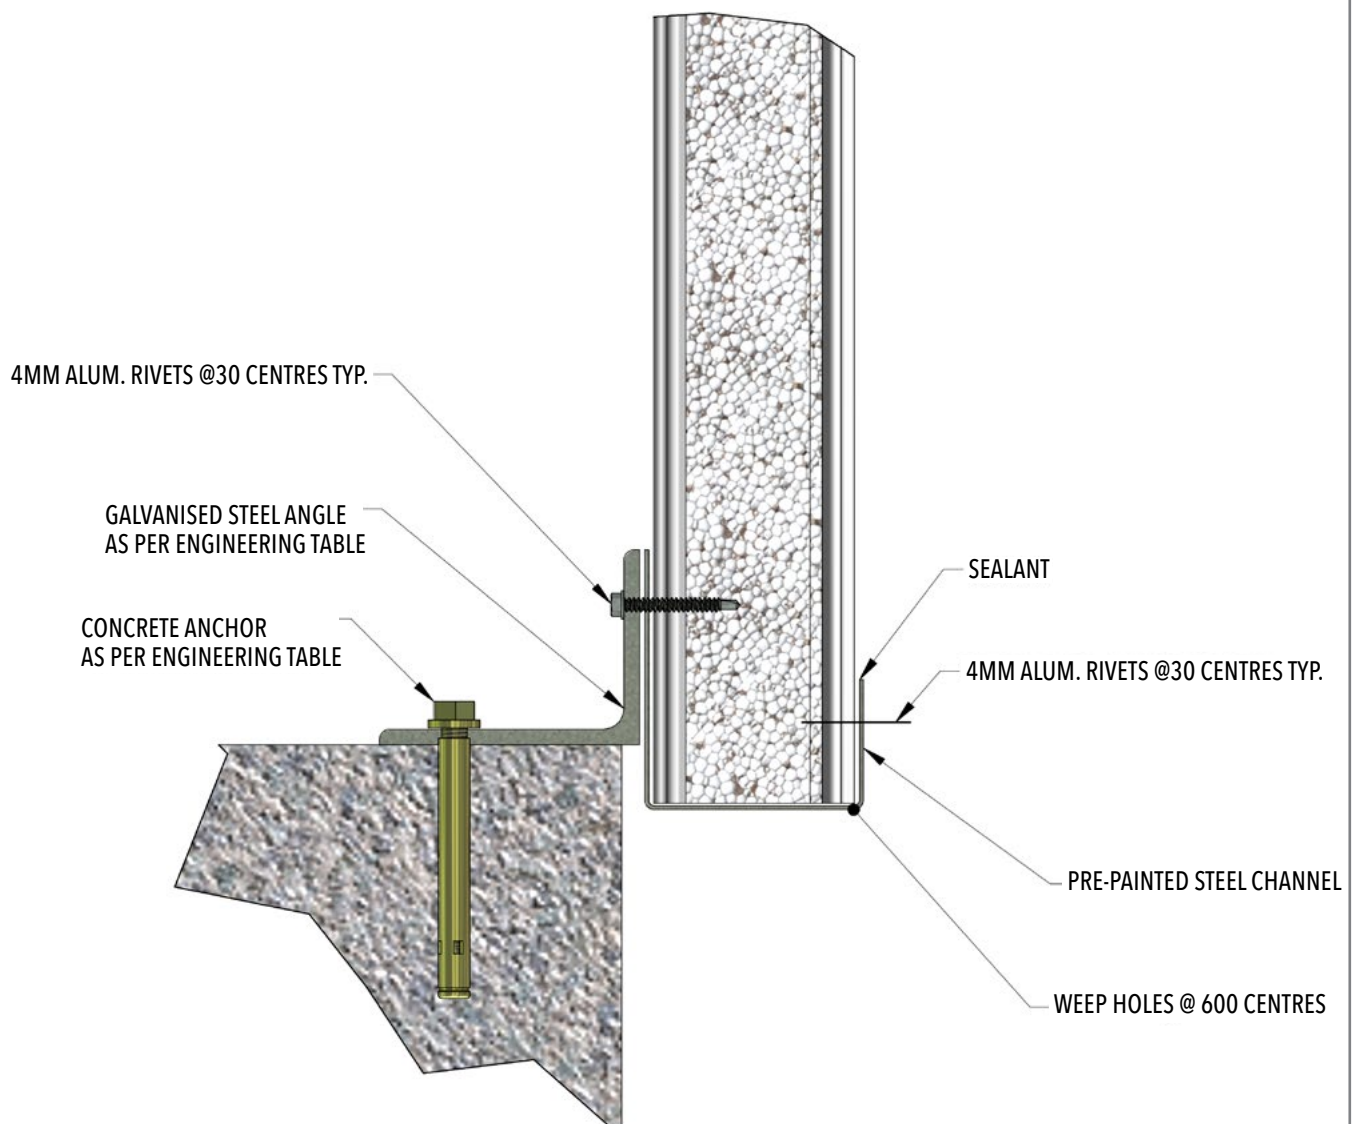

Description

SECRET FIX VERTICAL JOINTS BASE DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
7/12/2020

Designed by
DP


Drawing No.
WC1005-4

Rev: A Sheet
4/9

17. EXTERNAL CLADDING -

VERTICAL INSTALLATION & CONNECTION DETAILS

17.5 JOINTS EXTERNAL CORNER

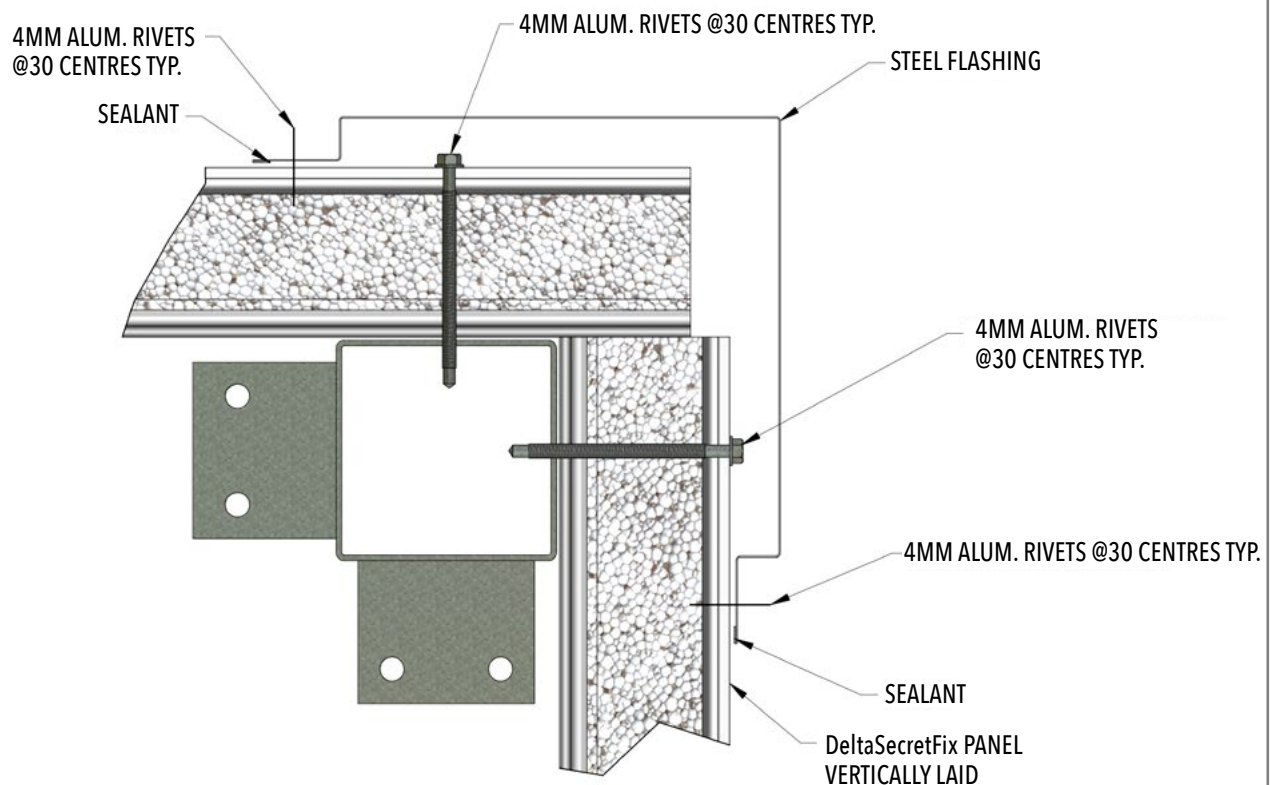

Description

SECRET FIX VERTICAL JOINTS EXTERNAL CORNER

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
7/12/2020


Designed by
DP

Drawing No.
WC1005-5

Rev: A Sheet
5/9

17. EXTERNAL CLADDING - VERTICAL INSTALLATION & CONNECTION DETAILS

17.6 JOINTS INTERNAL CORNER

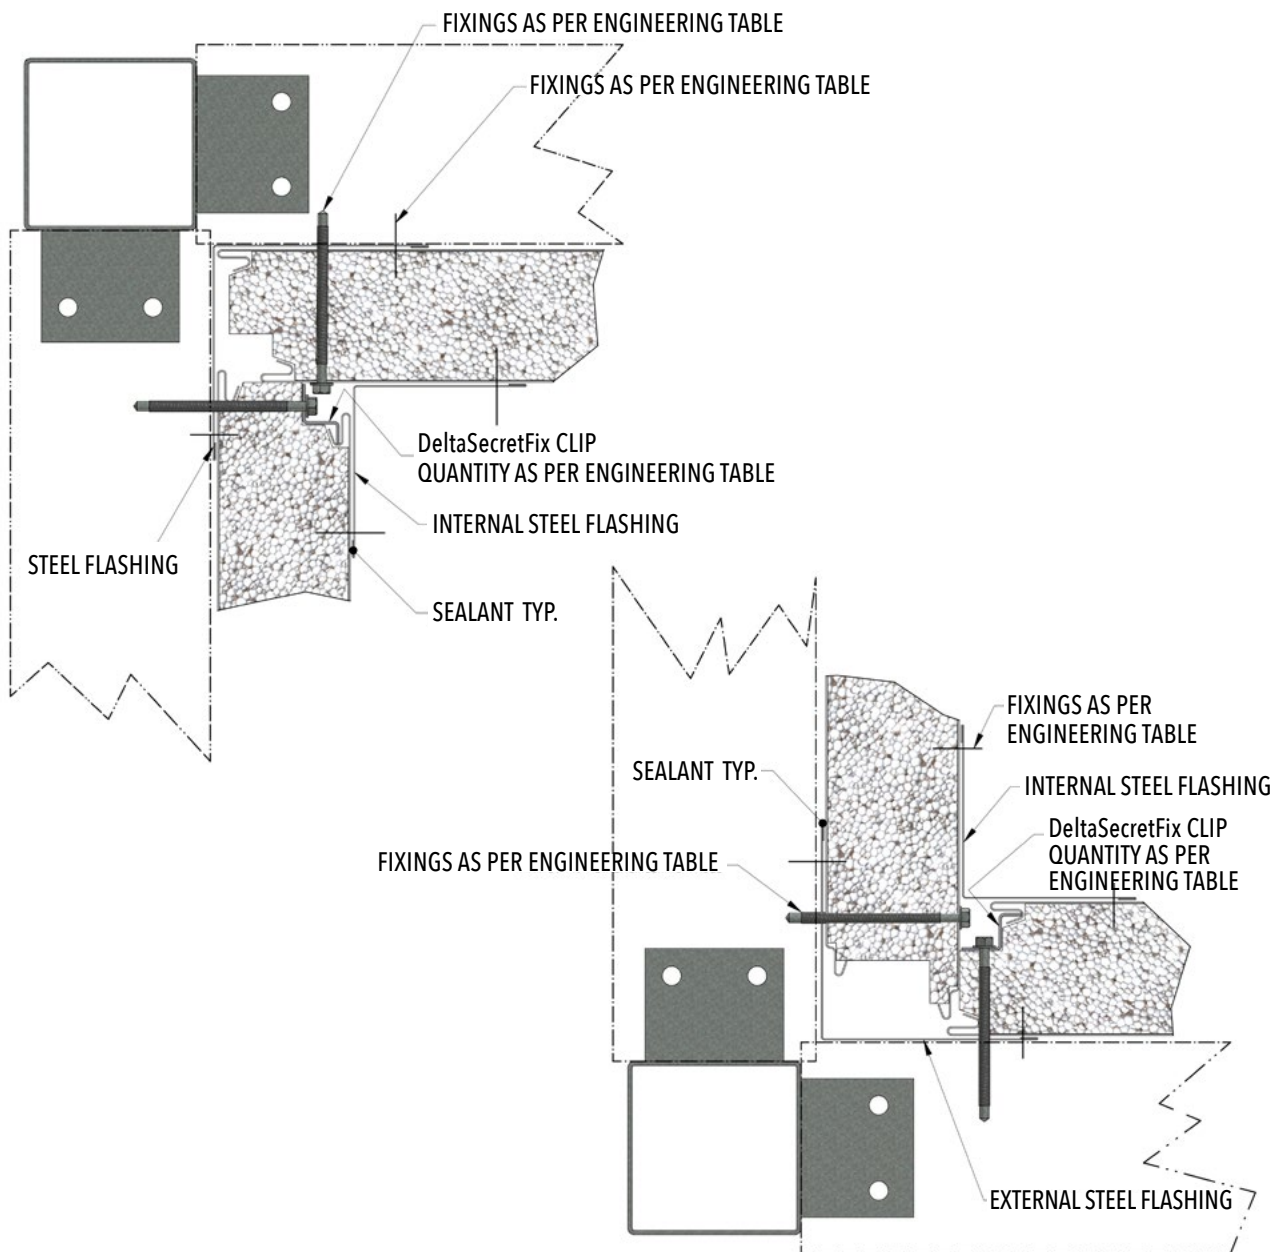

Description

SECRET FIX VERTICAL JOINTS INTERNAL CORNER

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Drawing No.
WC1005-6


Date:
7/12/2020

Designed by
DP

Rev: A Sheet
6/9

17. EXTERNAL CLADDING - VERTICAL INSTALLATION & CONNECTION DETAILS

17.7 JOINTS INTEGRATED WINDOW

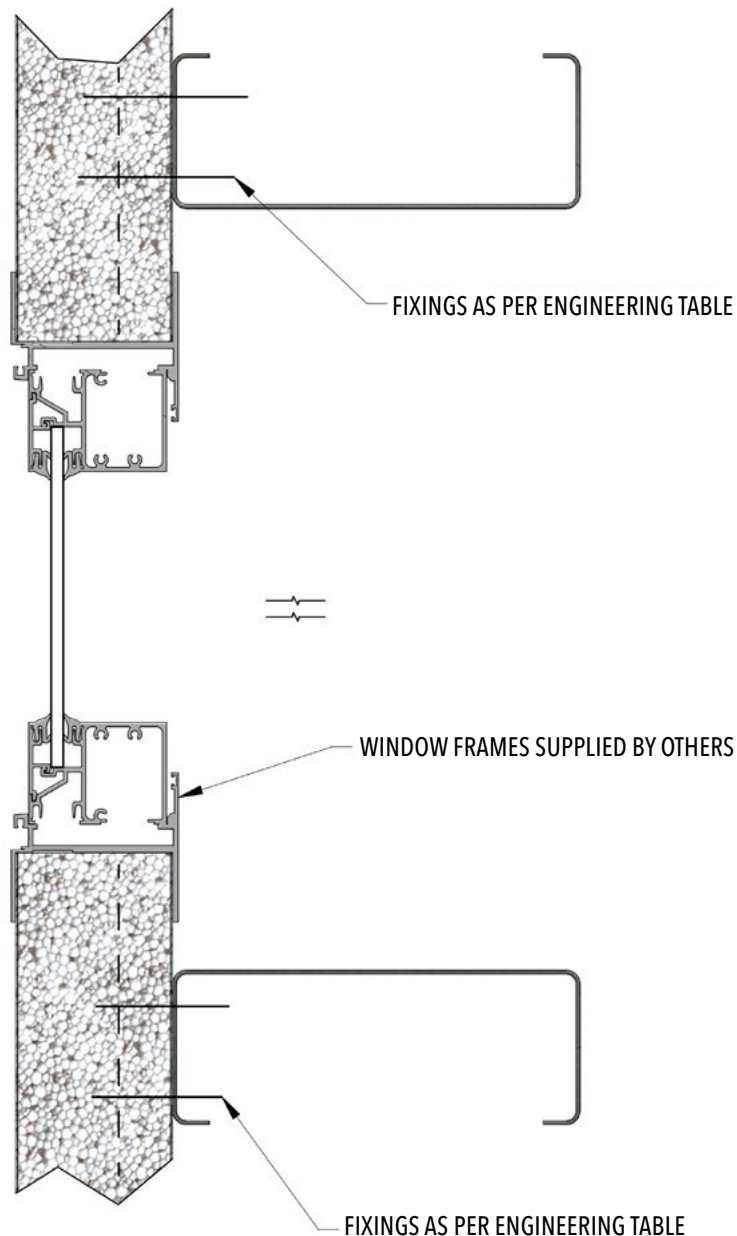

Description

SECRET FIX VERTICAL JOINTS INTEGRATED WINDOW

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
7/12/2020


Designed by
DP

Drawing No.
WC1005-7

Rev: A Sheet
7/9

17. EXTERNAL CLADDING - VERTICAL INSTALLATION & CONNECTION DETAILS

17.8 JOINTS RECESSED WINDOW

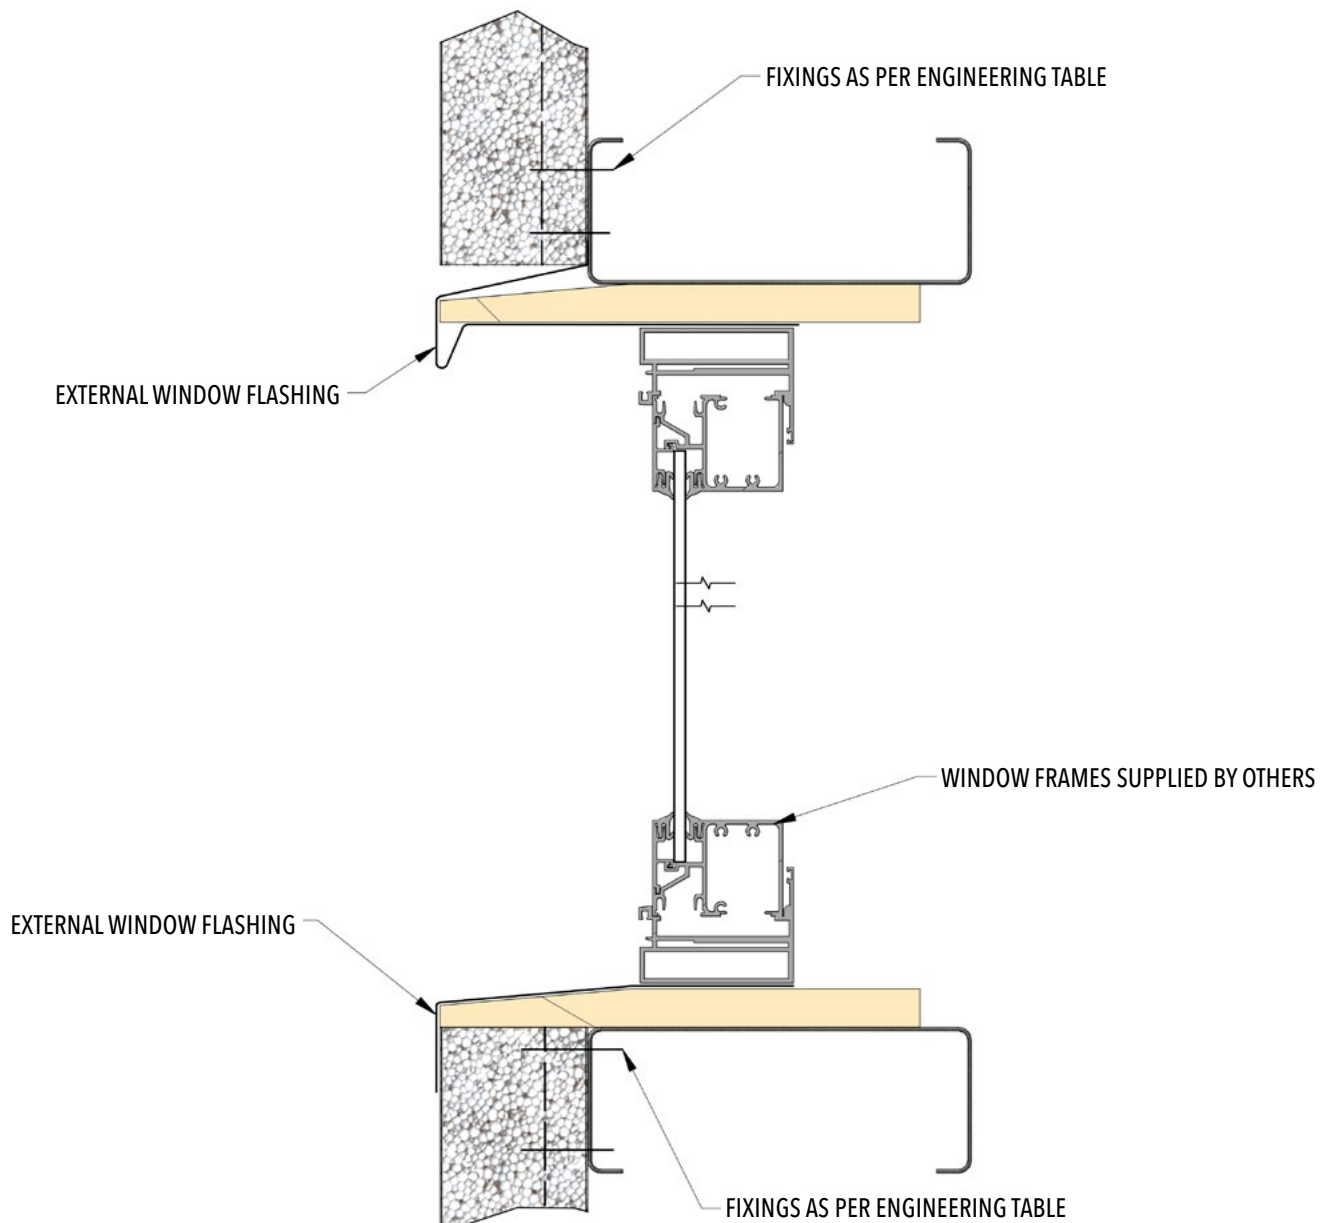

Description

SECRET FIX VERTICAL JOINTS RECESSED WINDOW

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iaw

Date:
7/12/2020


Designed by
DP

Drawing No.
WC1005-8

Rev: A Sheet
8/9

17. EXTERNAL CLADDING - VERTICAL INSTALLATION & CONNECTION DETAILS

17.9 PENETRATION DETAIL

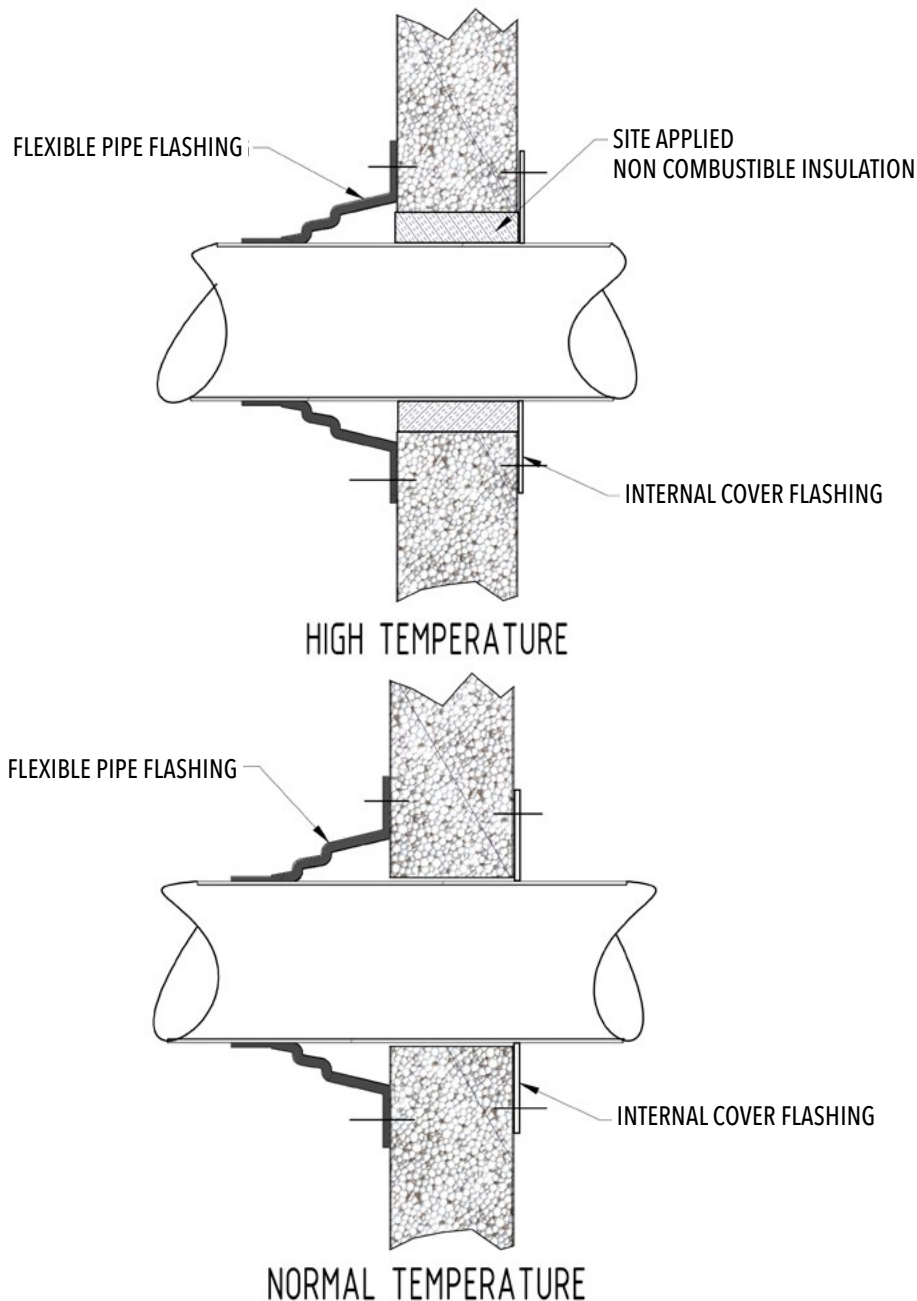

Description

SECRET FIX PENETRATION DETAIL

Filename & Path
Z:\Vault\DELTA PANELS & PATIOS\WALL CLADDING
INSTRUCTIONS\WC1005.iam

Date:
7/12/2020

Designed by
DP

Drawing No.
WC1005-9


Rev: A Sheet
9/9

18. INSTALLATION OF SERVICES & ACCESSORIES

Recessed Lighting

Delta Panels™ have a range of low voltage LED recess lighting, DeltaLowProfile™ Light, specifically designed to be installed into insulated panels.

Recess cut-outs are required to be made into the underneath of the panel

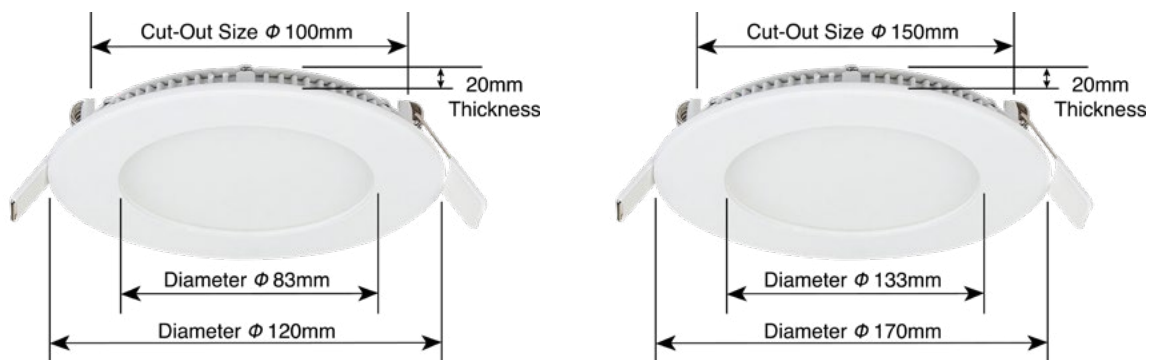

All electrical cabling is double insulated but the use of electrical conduit is still recommended

For ease of future access it is recommended to house the driver either behind the light fitting or in the eave of ridge capping.

A qualified electrician is required to install the GPO outlets for the low voltage lights.

Detailed procedures are outlined in the DeltaLowProfile™ Safety & Installation Manual, which is supplied with the lights and is also available online at www.deltapanel.com

Panel Lighting

Delta Panels™ have a range of low voltage LED panel lighting, DeltaPanelLight™, specifically designed to be installed into the underneath skin of insulated panels.

There is no requirement for cut-outs into the underneath of the panel, as frame is directly attached onto the underneath surface of the panel.



All electrical cabling is double insulated but the use of electrical conduit is still recommended

For ease of future access it is recommended to house the driver behind the light panel within the support frame.

A qualified electrician is required to install the GPO outlets for the low voltage LED panel lights.

Detailed procedures are outlined in the DeltaPanelLight™ Safety & Installation Manual, which is supplied with the lights and is also available online at www.deltapanel.com


18. INSTALLATION OF SERVICES & ACCESSORIES

Ceiling Fans

To mount ceiling fans to insulated panels it is necessary to ensure that the weight of the fan is spread over the whole of the top skin of the ceiling panel.

All electrical work must be carried out by a Licensed Electrician.

BRACKET INSTALLATION DETAILS

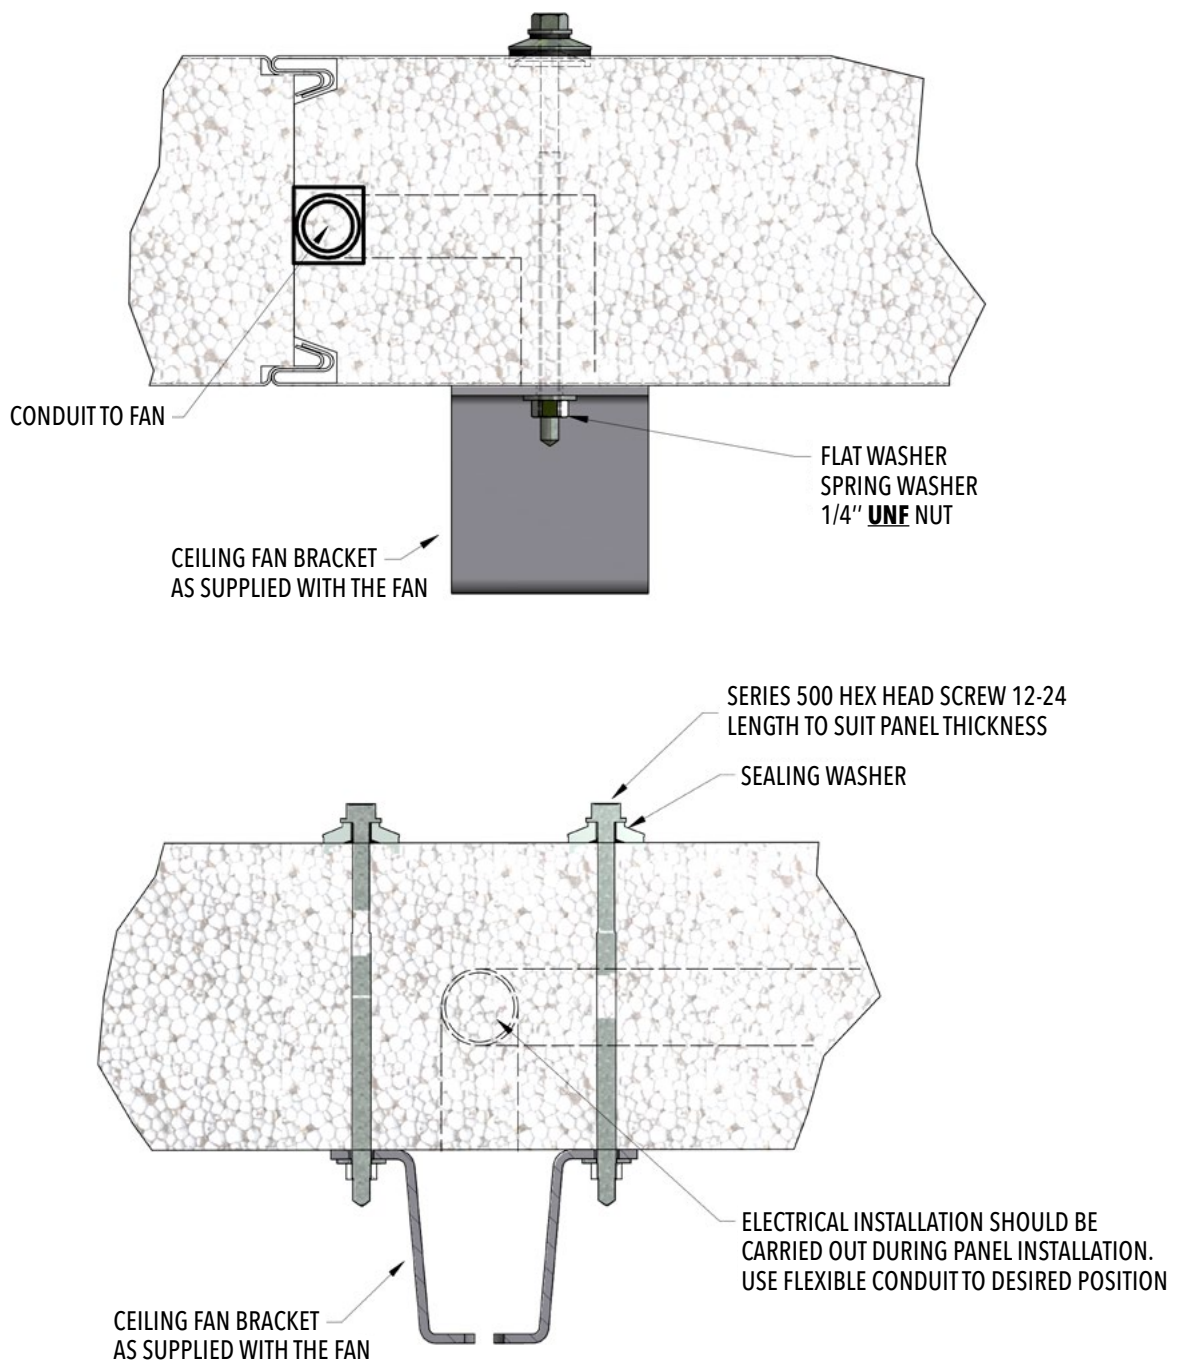


18. INSTALLATION OF SERVICES & ACCESSORIES

All Purpose Service Support Bracket

To fix an all purpose support bracket to insulated panels it is necessary to ensure that the weight is spread over the whole of the top skin of the panel. Therefore a through-fastening arrangement is required.

Ridge fixing as close as possible to the panel join is highly recommended

ALL PURPOSE SERVICE SUPPORT BRACKET

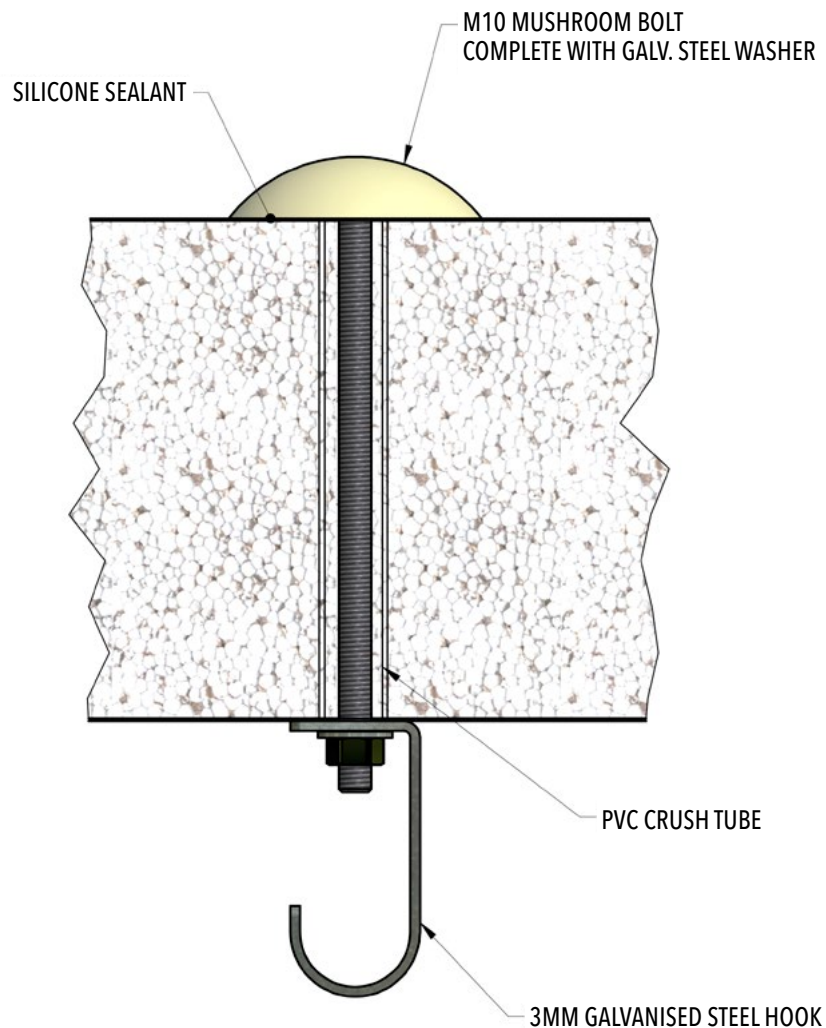


18. INSTALLATION OF SERVICES & ACCESSORIES

Mushroom Head Suspension Assembly

To allow for clear spans in working areas it is necessary to suspend the roof from the structural frame of the building. To attached this a mushroom head suspension system is used. Please refer to the engineering in regarding to spacings and allowable load limits

MUSHROOM HEAD BOLT FOR CEILING SUSPENSION

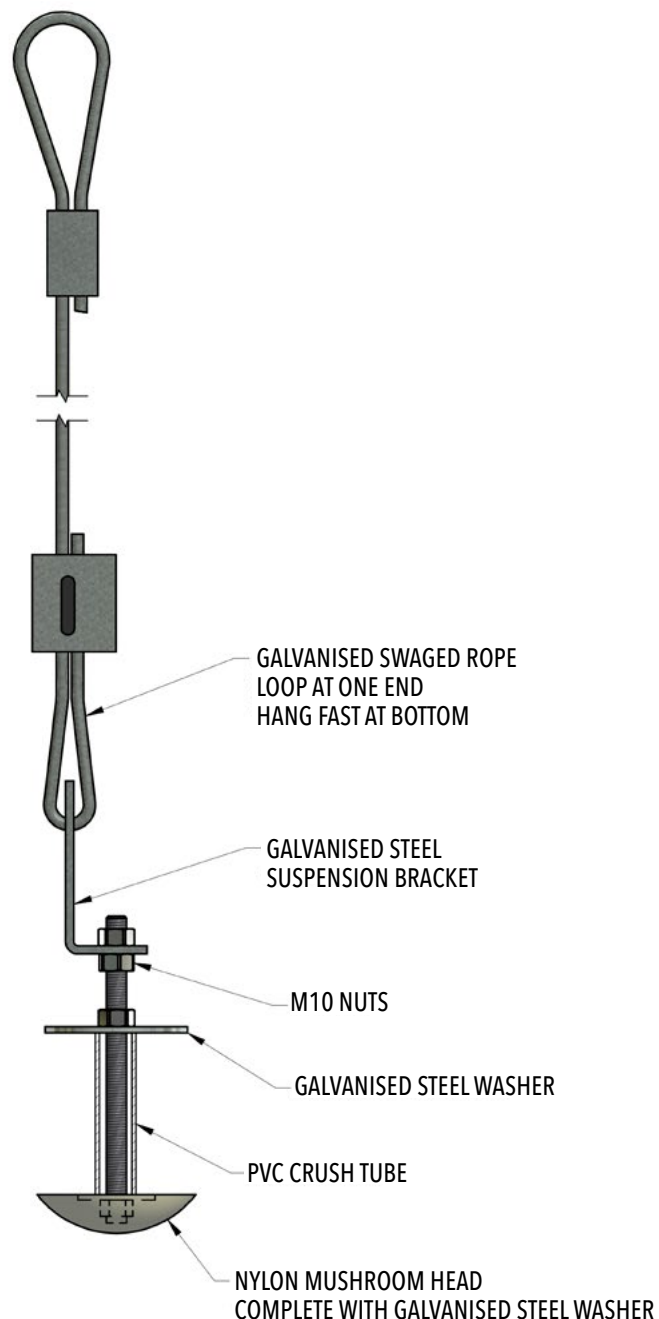



Delta Panels™ Pty Ltd is committed to an ongoing programme of product research and development and reserves the right to update and amend information without prior notice. Reasonable care has been taken to ensure that all published information is correct and accurately reflects the properties of our products and their design applications at the time of publication. However these are a general guide only, it is the customers responsibility to ensure that all products and their stated applications are fit for purpose and complies with all relevant statutory requirements. To ensure that you keep abreast of all updates in our product range, all current reference material are available on our web page for downloading.

All information contained within this document is subject to Copyright and may not be copied without the express permission of Delta Panels™ Pty Ltd.

Delta Panels™, DeltaCool™, DeltaSecretFix™, DeltaLowProfile™ & DeltaPanelLight™ are registered trademarks of Delta Panels™ Pty Ltd.
